


PROJECT 1-23 METOXEN, DIXON, QUINNEY & SEVENTH

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 8/7 - 8/11 -UPDATE

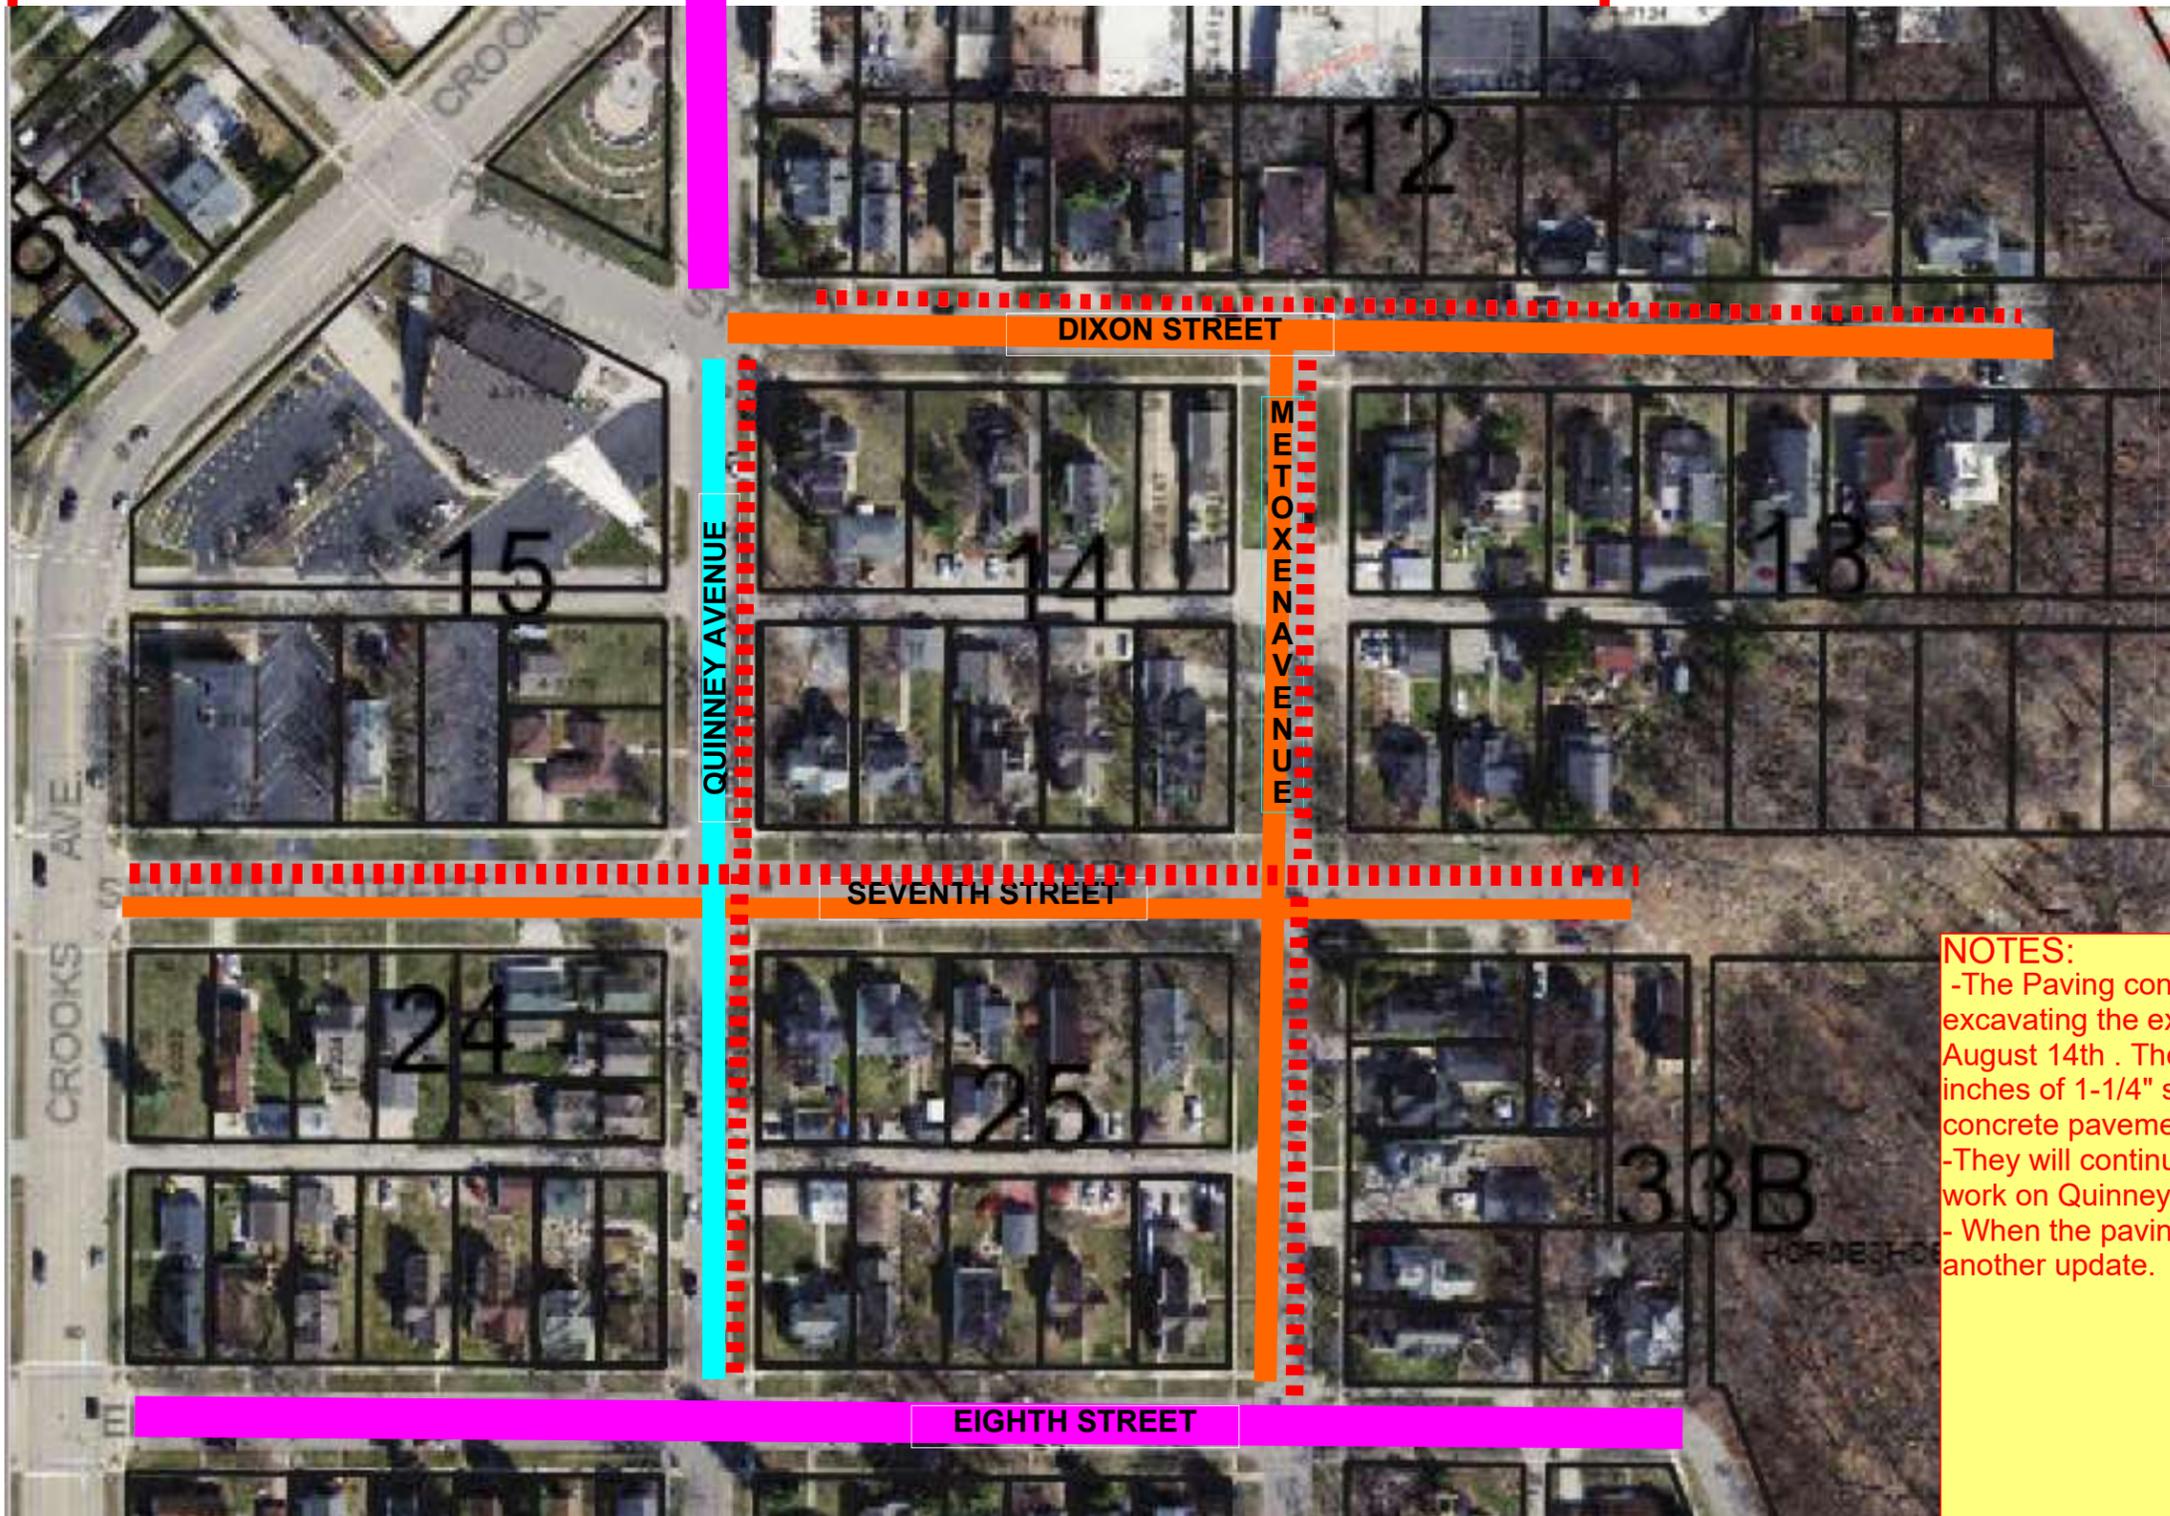

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDWALK/DRIVEWAY WORK
- RECOMMENDED PARKING
- NO PARKING = [Red dashed line]
- TEMPORARY PARKING = [Magenta bar]

NOTES:
 -The Paving contractor will continue removing existing pavement, excavating the existing stone base, and placing new road stone the week of August 14th . The new road stone consists of 6 inches of 3" stone with 6 inches of 1-1/4" stone on top of the 3" stone. There will be 6 inches of concrete pavement on the stone with 6 inch high curb.
 -They will continue on Metoxen Avenue and Seventh Street. They will also work on Quinney Avenue the week of August 21st
 - When the paving contractor sends an updated schedule, I will send out another update.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 WHITE DOVE, WHITE BIRCH, LODERBAUER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 8/7 - 8/11-UPDATE

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.



- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDEWALK/DRIVEWAY WORK
- RECOMMENDED PARKING
- NO PARKING = [Red dashed line]
- TEMPORARY PARKING = [Pink solid bar]

NOTES:

- The week of August 14th, the sidewalk contractor will finish working on constructing the sidewalk and driveway aprons.
- You will not be able to get into your driveway for 7 days after the sidewalk contractor constructs your driveway apron and the sidewalk that goes across your driveway. You can continue to park at the northern portion of White Birch and Red Fox Lane(see map to left.) while your driveway apron and sidewalk cure and harden.
- Shortly after the sidewalk and driveway aprons are complete, the landscaper should start the landscape work.

PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 8/7 - 8/11 - UPDATE



*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

RECOMMENDED PARKING

NO PARKING = 
TEMPORARY PARKING = 

NOTES:

- The week of August 14th, the sidewalk contractor will finish working on constructing the sidewalk and driveway aprons.
 - You will not be able to get into your driveway for 7 days after the sidewalk contractor constructs your driveway apron and the sidewalk that goes across your driveway. You can continue to park at the southern portion of Greyhound and Boxer (see map to left.) while your driveway apron and sidewalk cure and harden.
 - Shortly after the sidewalk and driveway aprons are complete, the landscaper should start the landscape work..
- When the paving contractor sends an updated schedule, I will send out another update..
- The curved section connecting Setter and Boxer that was not paved in concrete, will be paved in asphalt later this summer.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 8/7 - 8/11



*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
 - STORM SEWER WORK
 - PAVMENT REMOVALS
 - GRADING
 - CONCRETE PAVING
 - SIDWALK/DRIVEWAY WORK
 - RECOMMENDED PARKING
- NO PARKING = 
- TEMPORARY PARKING = 

NOTES:

- The sewer contractor is planning to start the storm sewer work the week of August 21st, if the water main work is completed.
- The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of August 28th. When the paving contractor sends an updated schedule, I will send out another update.
- the Water Department' contractor will be boring across the navigation canal for the next week. The contractor will then relay the water main in Canal Street which will take about a week. The water main project should be done by mid August. Their contractor should be handing out notices before the works starts.
