


PROJECT 2-22 (KENNETH AVENUE AREA UTILITY RELAY)

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 8/22 - 8/26

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

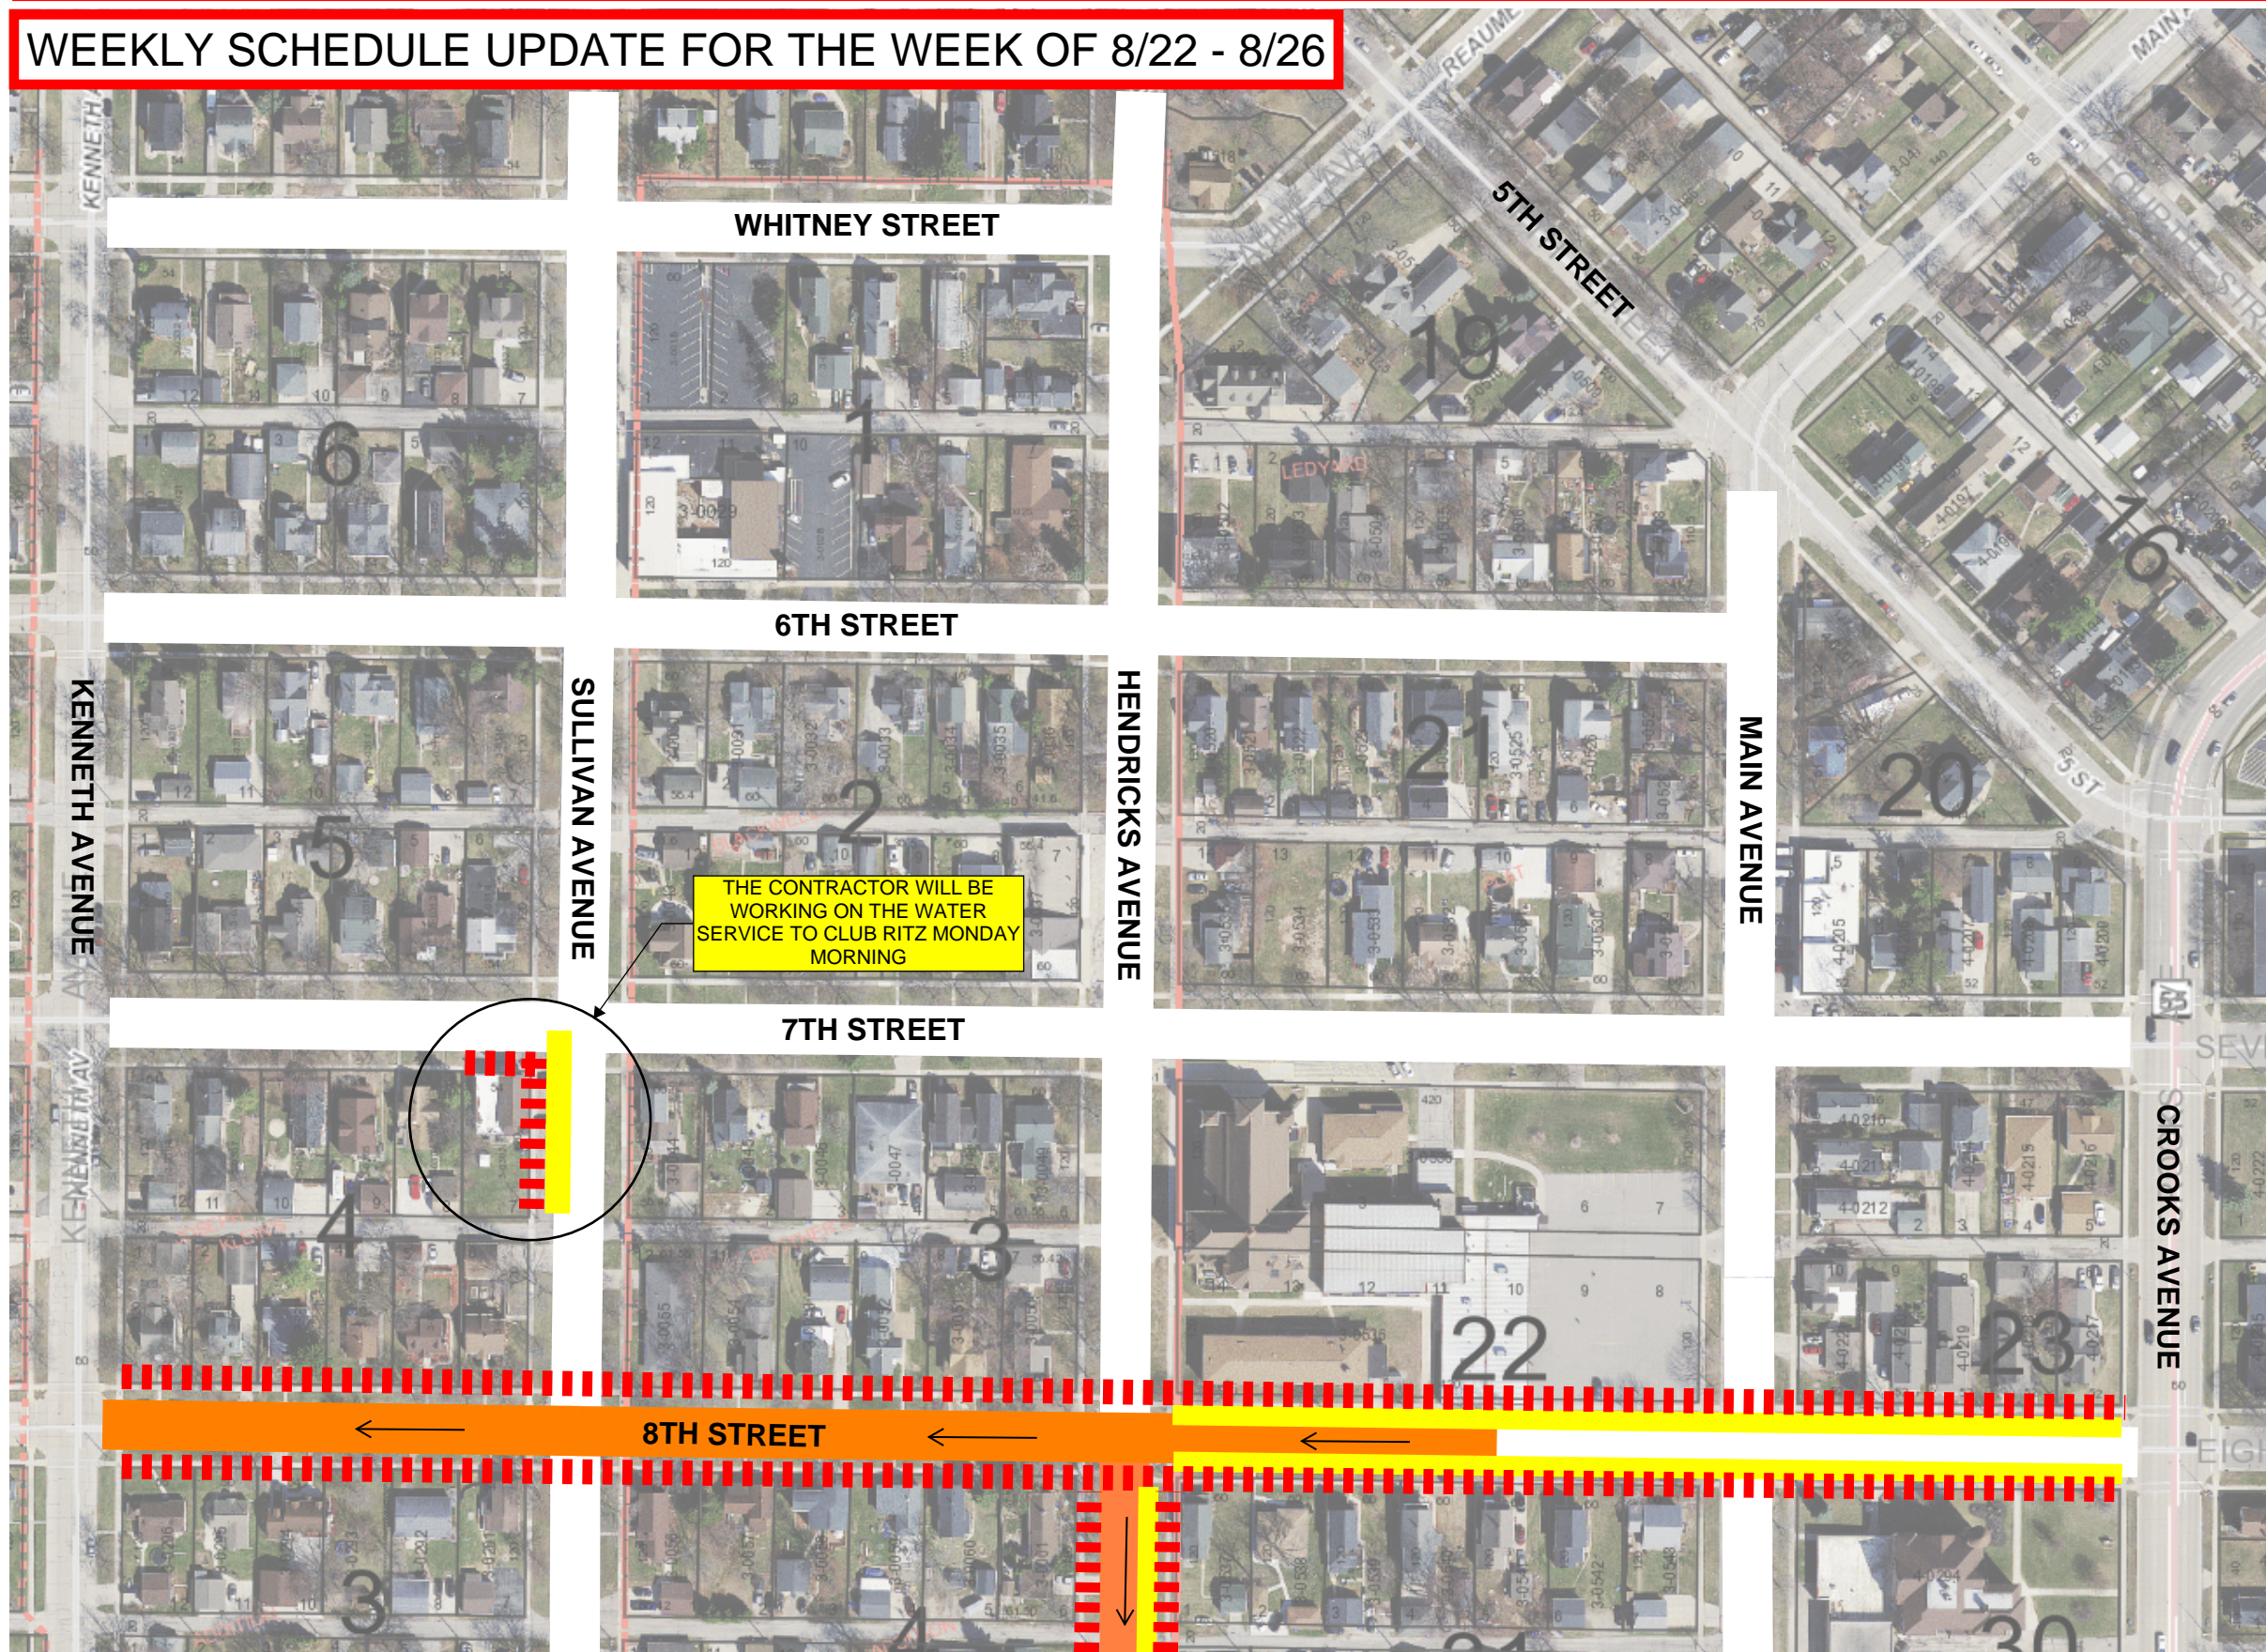

- NO ACTIVE WORK
- SANITARY SEWER WORK
- WATER MAIN WORK
- PUBLIC LATERALS/SERVICES
- GRADING WORK
- ASPHALT PAVING WORK
- RESTORATION

NO STREET PARKING = [Red dashed line icon]

NOTES:

Contractor will continue working on Sanitary Sewer Main on 8th Street. They will continue on Monday where they end today (Friday). When they get to Hendricks Avenue, they will be work on Sewer from 8th to 9th on Hendricks before continuing west on 8th.

Second crew will continue working on sewer and water services to properties in the public right of way. They will finish last remaining service on 7th to Club Ritz, then do some miscellaneous water valve work. After that is complete, they will begin working on 8th Street Laterals following behind the Sewer Main crew.

Please avoid driving on 8th throughout next week.

Recommended Parking - During construction hours, please find an alternate parking space if you can not access your driveway. Driveways should be open overnight once construction has ceased for the day.

Thank you for joining the weekly email list! Encourage your neighbors to email Taylor Conger at tconger@kaukauna-wi.org to be added to the weekly email update list.
