


# PROJECT 2-22 (KENNETH AVENUE AREA UTILITY RELAY)

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 8/1 - 8/5

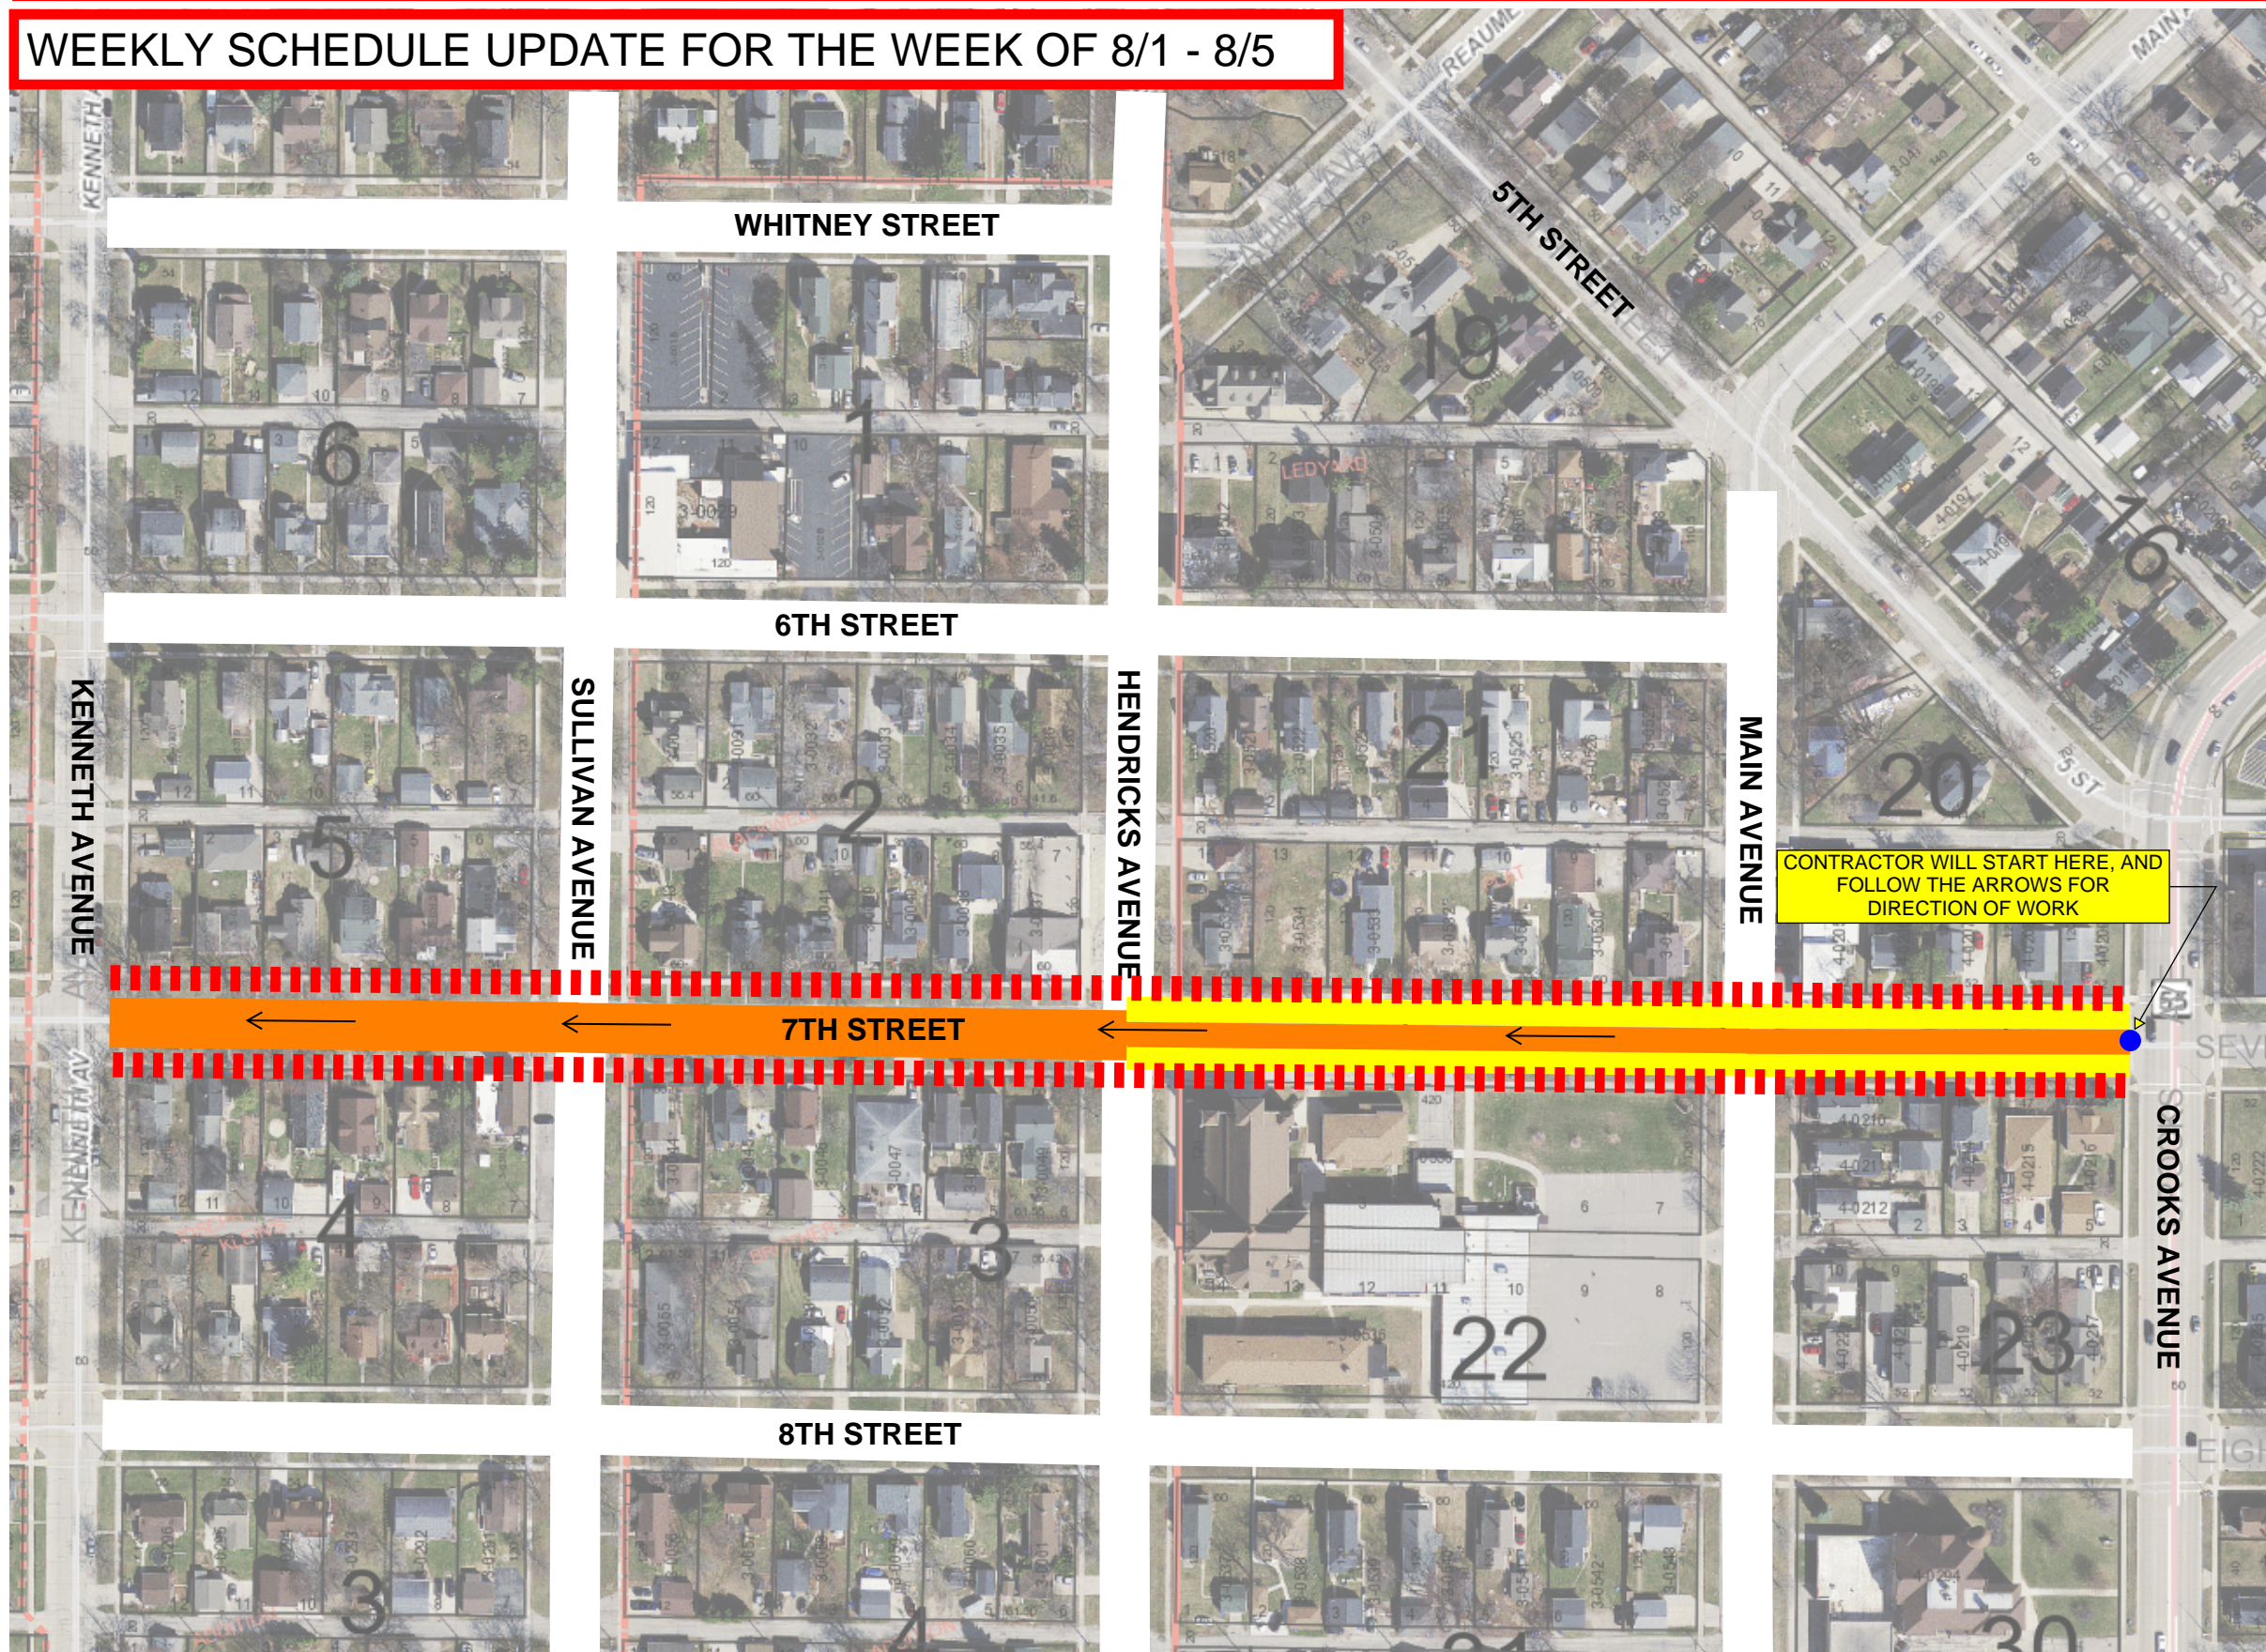

\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- NO ACTIVE WORK
- SANITARY SEWER WORK
- WATER MAIN WORK
- PUBLIC LATERALS/SERVICES
- GRADING WORK
- ASPHALT PAVING WORK
- RESTORATION

NO STREET PARKING = [Red dashed line with vertical bars]

**NOTES:**

Contractor will be switching to Sanitary Sewer work on Monday, August 1st. They will be working in the same direction as the water main on 7th Street, starting at the East end of the project (Crooks) and working to the west (toward Kenneth). The sanitary sewer is located at the centerline of the road. This means that there will be little to no room for cars to drive by. Once workers get a few blocks of Sanitary Sewer Main completed, another crew will come in to begin working on water and sewer services to the sidewalk (in the Public Right of way, not private property). Please avoid driving down 7th with the exception of getting to your house. PLEASE, DO NOT PARK VEHICLES ON EITHER SIDE OF 7TH STREET DURING WORK HOURS.

**Recommended Parking** - During construction hours, please find an alternate parking space if you can not access your driveway. Driveways should be open overnight once construction has ceased for the day.

Thank you for joining the weekly email list! Encourage your neighbors to email Taylor Conger at [tconger@kaukauna-wi.org](mailto:tconger@kaukauna-wi.org) to be added to the weekly email update list.
