


# PROJECT 2-22 (KENNETH AVENUE AREA UTILITY RELAY)

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 8/15 - 8/19

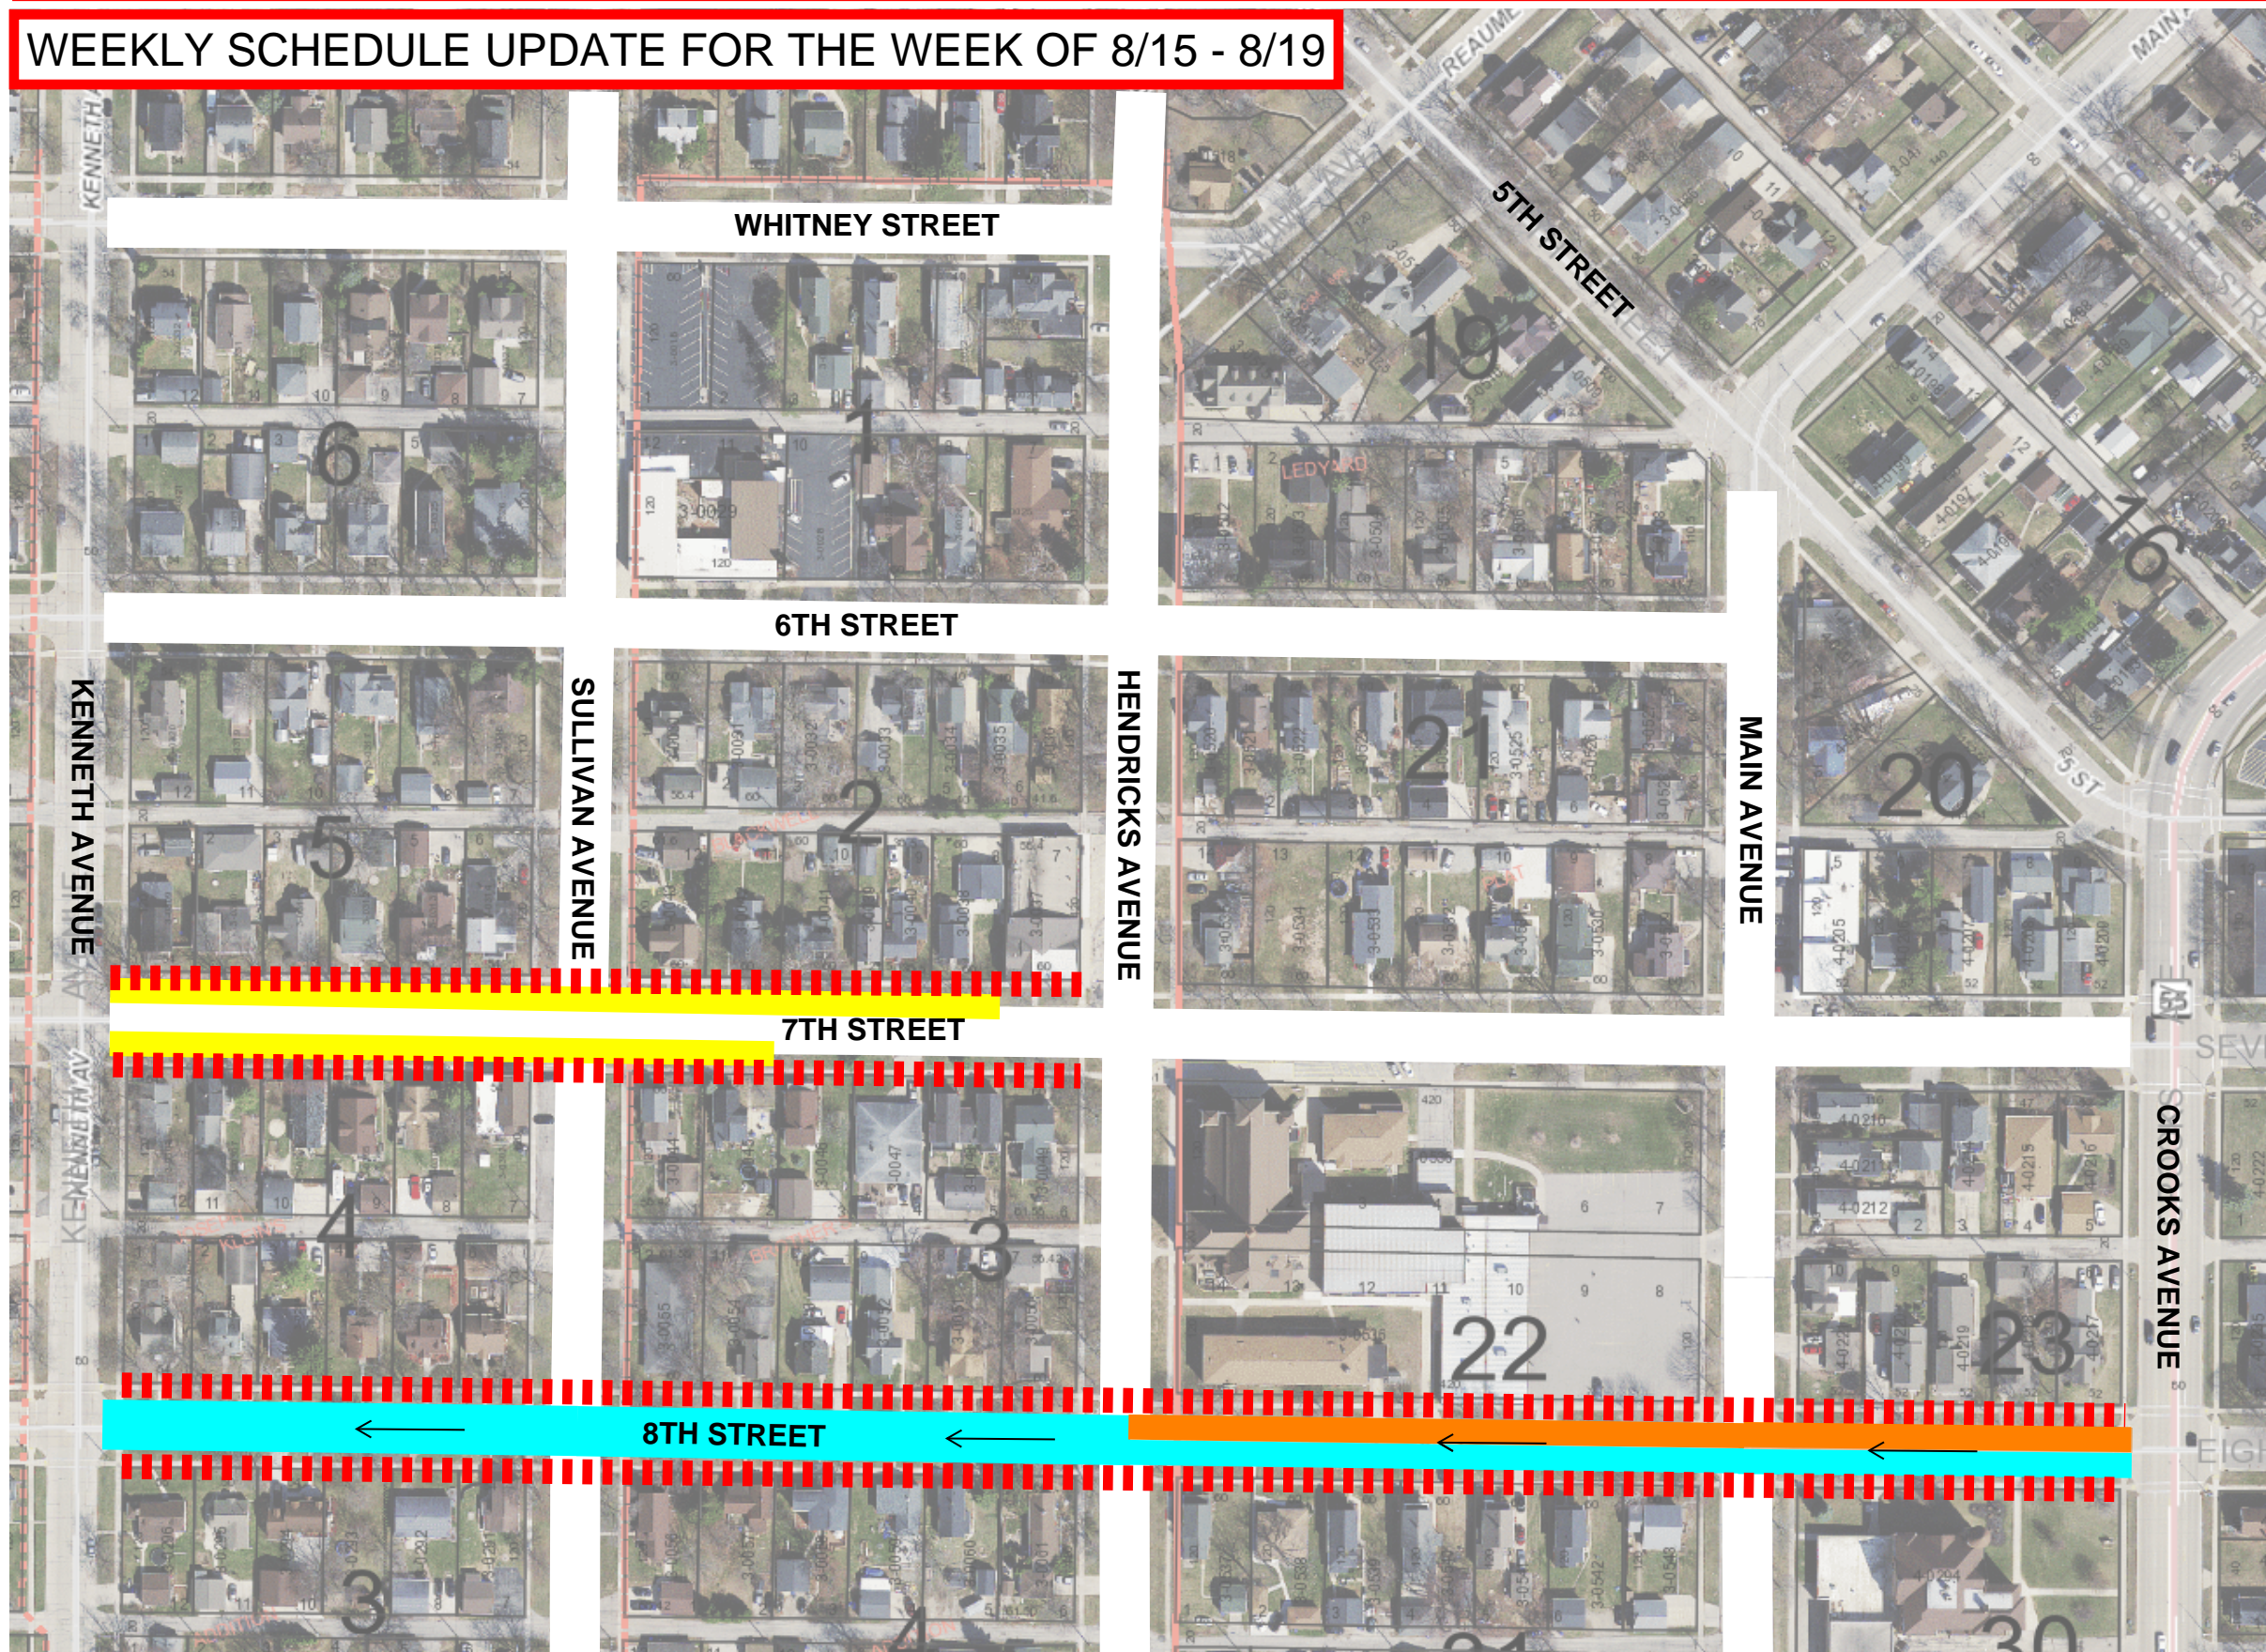

\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- NO ACTIVE WORK
- SANITARY SEWER WORK
- WATER MAIN WORK
- PUBLIC LATERALS/SERVICES
- GRADING WORK
- ASPHALT PAVING WORK
- RESTORATION

NO STREET PARKING = [Red dashed line]

**NOTES:**

Contractor is going to begin working on Water Main on 8th Street on Monday. They will start at Crooks, and work toward Kenneth. They will continue with Water Main until they finish. Once they get a few blocks of water main done, another crew will come back to Crooks & 8th to begin working on Sanitary Sewer Main. They will work on Sanitary Main for remainder of week.

Separate crews will also finish the remaining water and sanitary sewer services to each property on 7th. This work is only the public Right of Way work, not the private work.

Please avoid driving on 7th and 8th throughout next week.

**Recommended Parking** - During construction hours, please find an alternate parking space if you can not access your driveway. Driveways should be open overnight once construction has ceased for the day.

Thank you for joining the weekly email list! Encourage your neighbors to email Taylor Conger at [tconger@kaukauna-wi.org](mailto:tconger@kaukauna-wi.org) to be added to the weekly email update list.
