


# PROJECT 2-22 (KENNETH AVENUE AREA UTILITY RELAY)

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 8/29 - 9/2

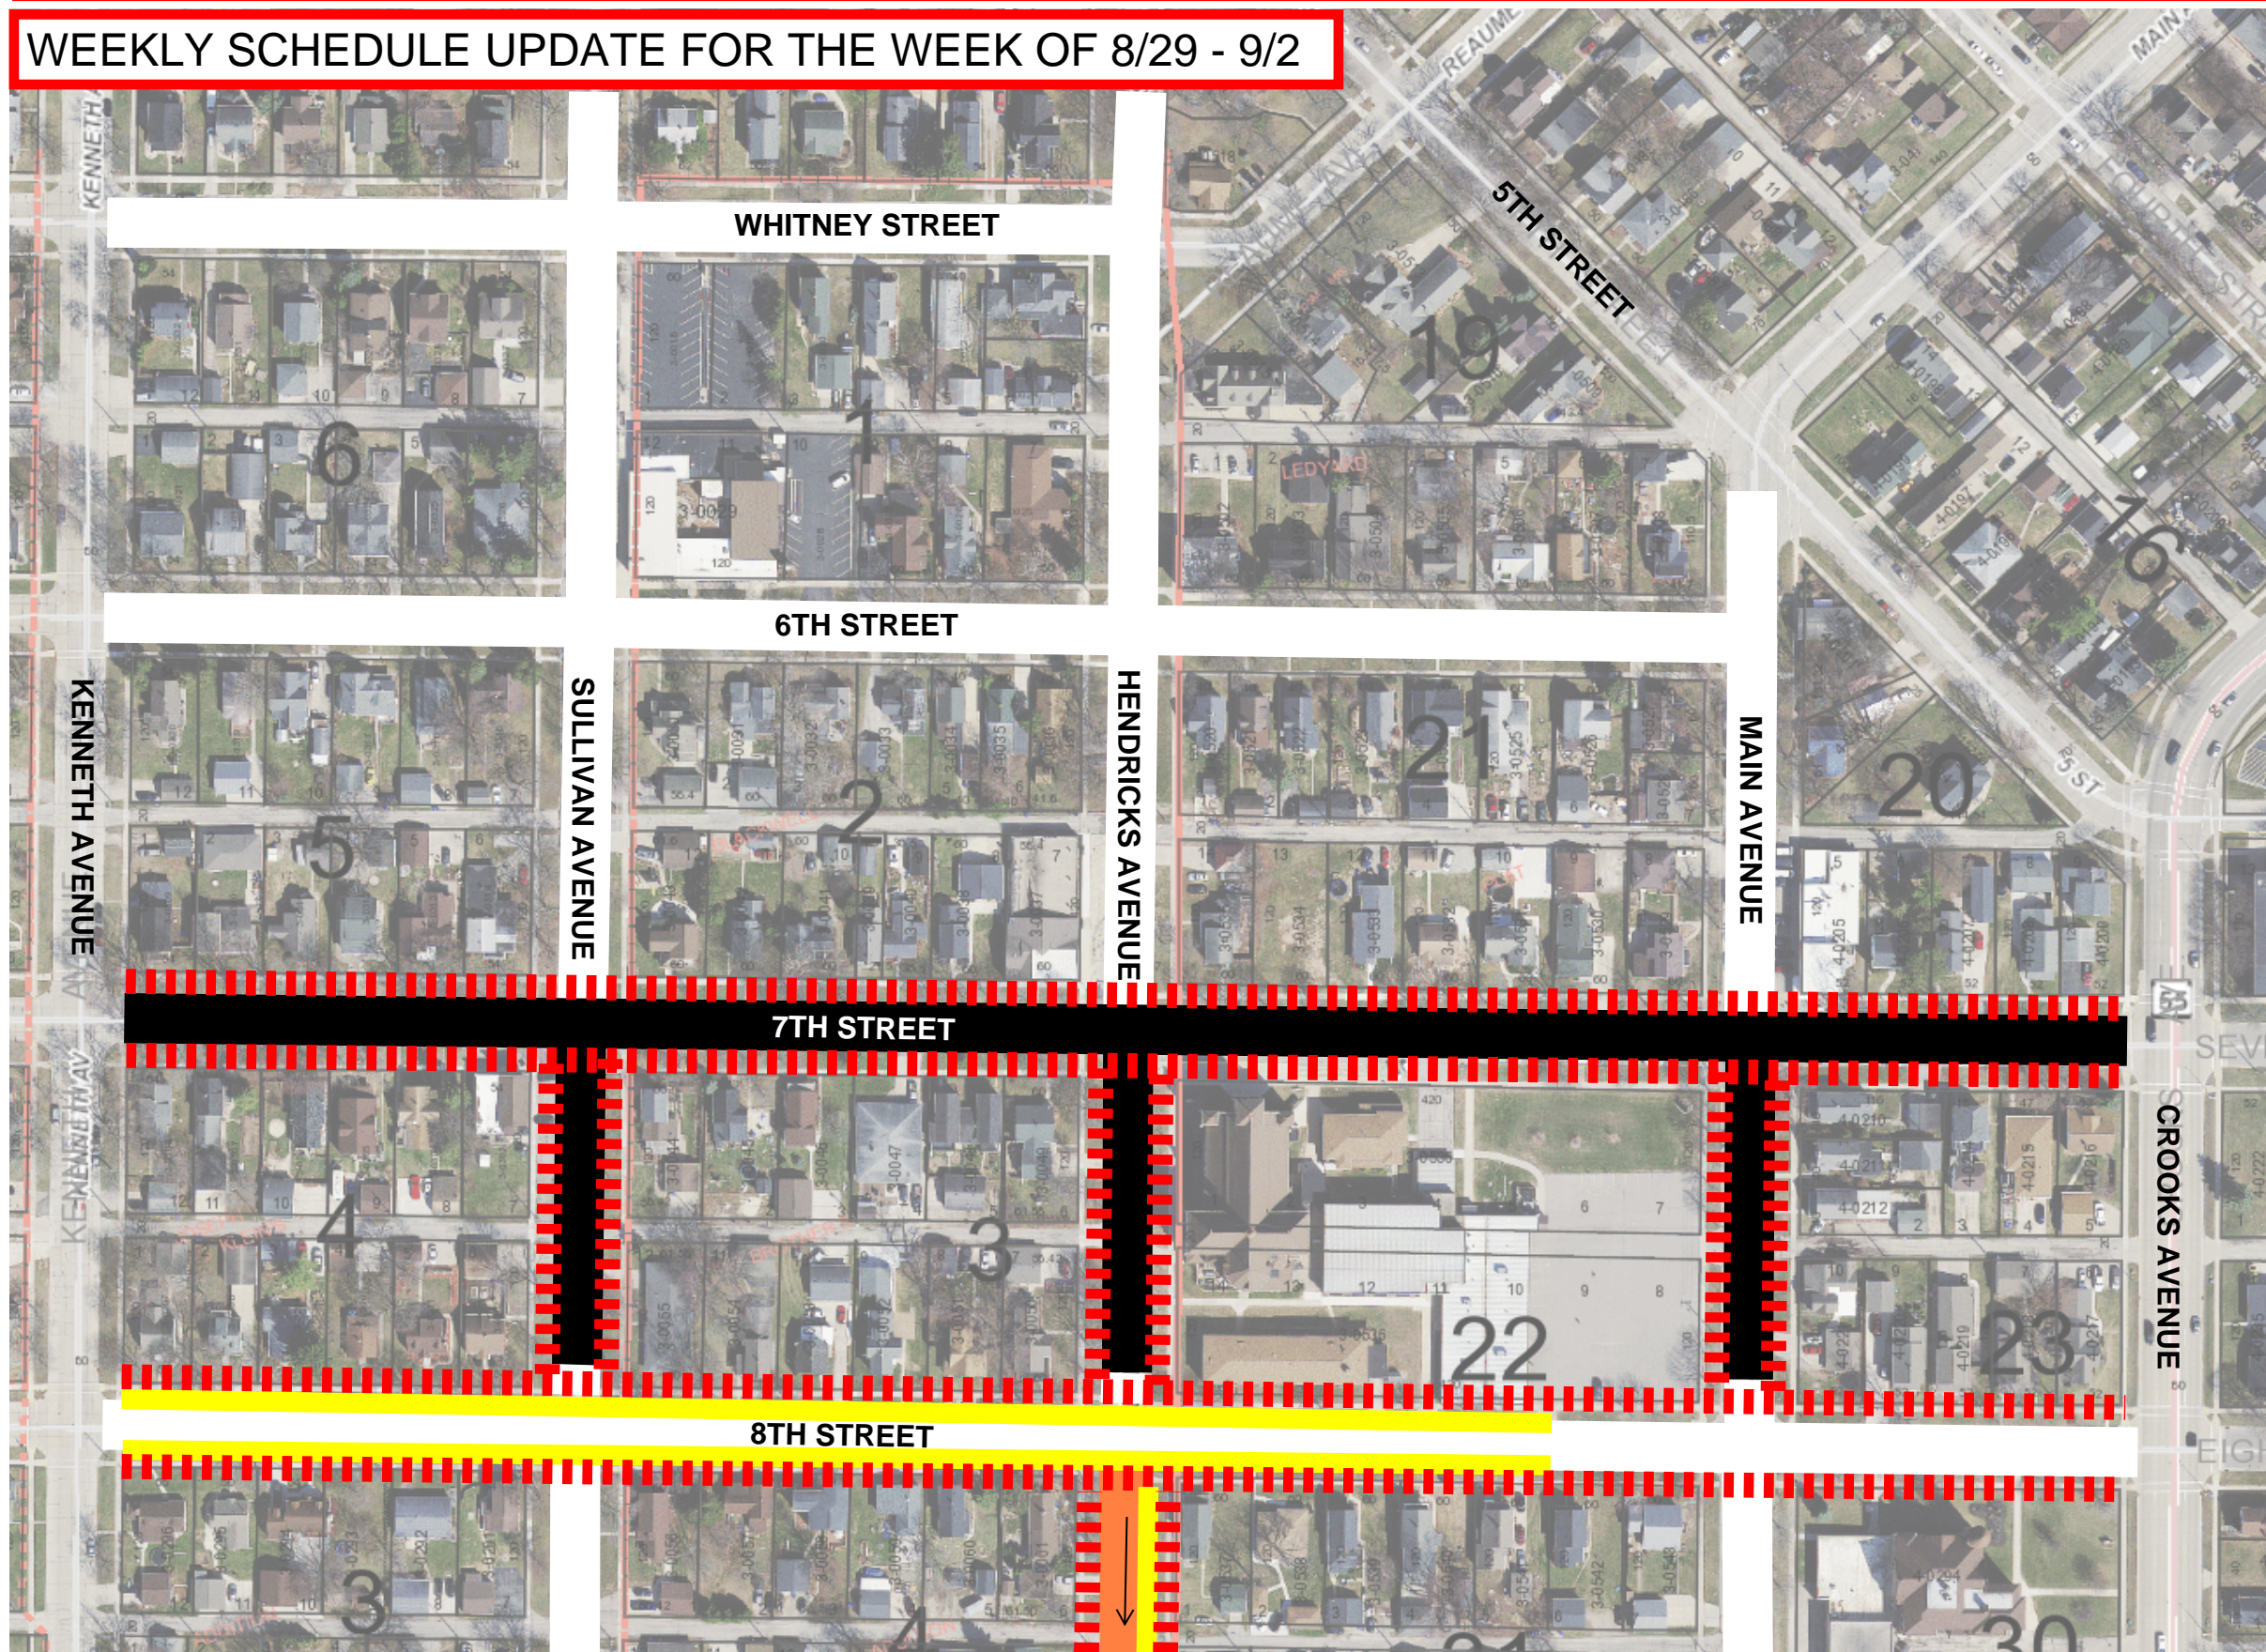

\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- NO ACTIVE WORK
  - SANITARY SEWER WORK
  - WATER MAIN WORK
  - PUBLIC LATERALS/SERVICES
  - GRADING & PAVING WORK
  - RESTORATION
- NO STREET PARKING =

**NOTES:**

The Sewer contractor will be working on the Sanitary Main on Hendricks from 8th to 9th to begin the week. Once they complete that, both sewer crews will be working on Sanitary Laterals and Water Services to individual properties within the Right of Way (Back of sidewalk on each side). This work will last for the remainder of the week.

The Paving contractor began working on 7th Street today (the 26th). They will continue working throughout next week as they remove existing asphalt pavement, prep the roadway, and then place new pavement (Tentatively next Wednesday & Thursday).

**Recommended Parking** - During construction hours, please find an alternate parking space if you can not access your driveway. Driveways should be open overnight once construction has ceased for the day. Please avoid driving on 7th & 8th throughout the week.

Thank you for joining the weekly email list! Encourage your neighbors to email Taylor Conger at [tconger@kaukauna-wi.org](mailto:tconger@kaukauna-wi.org) to be added to the weekly email update list.
