


PROJECT 2-22 (KENNETH AVENUE AREA UTILITY RELAY)

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 9/12 - 9/16 AND UPDATE FOR 9/10/2022

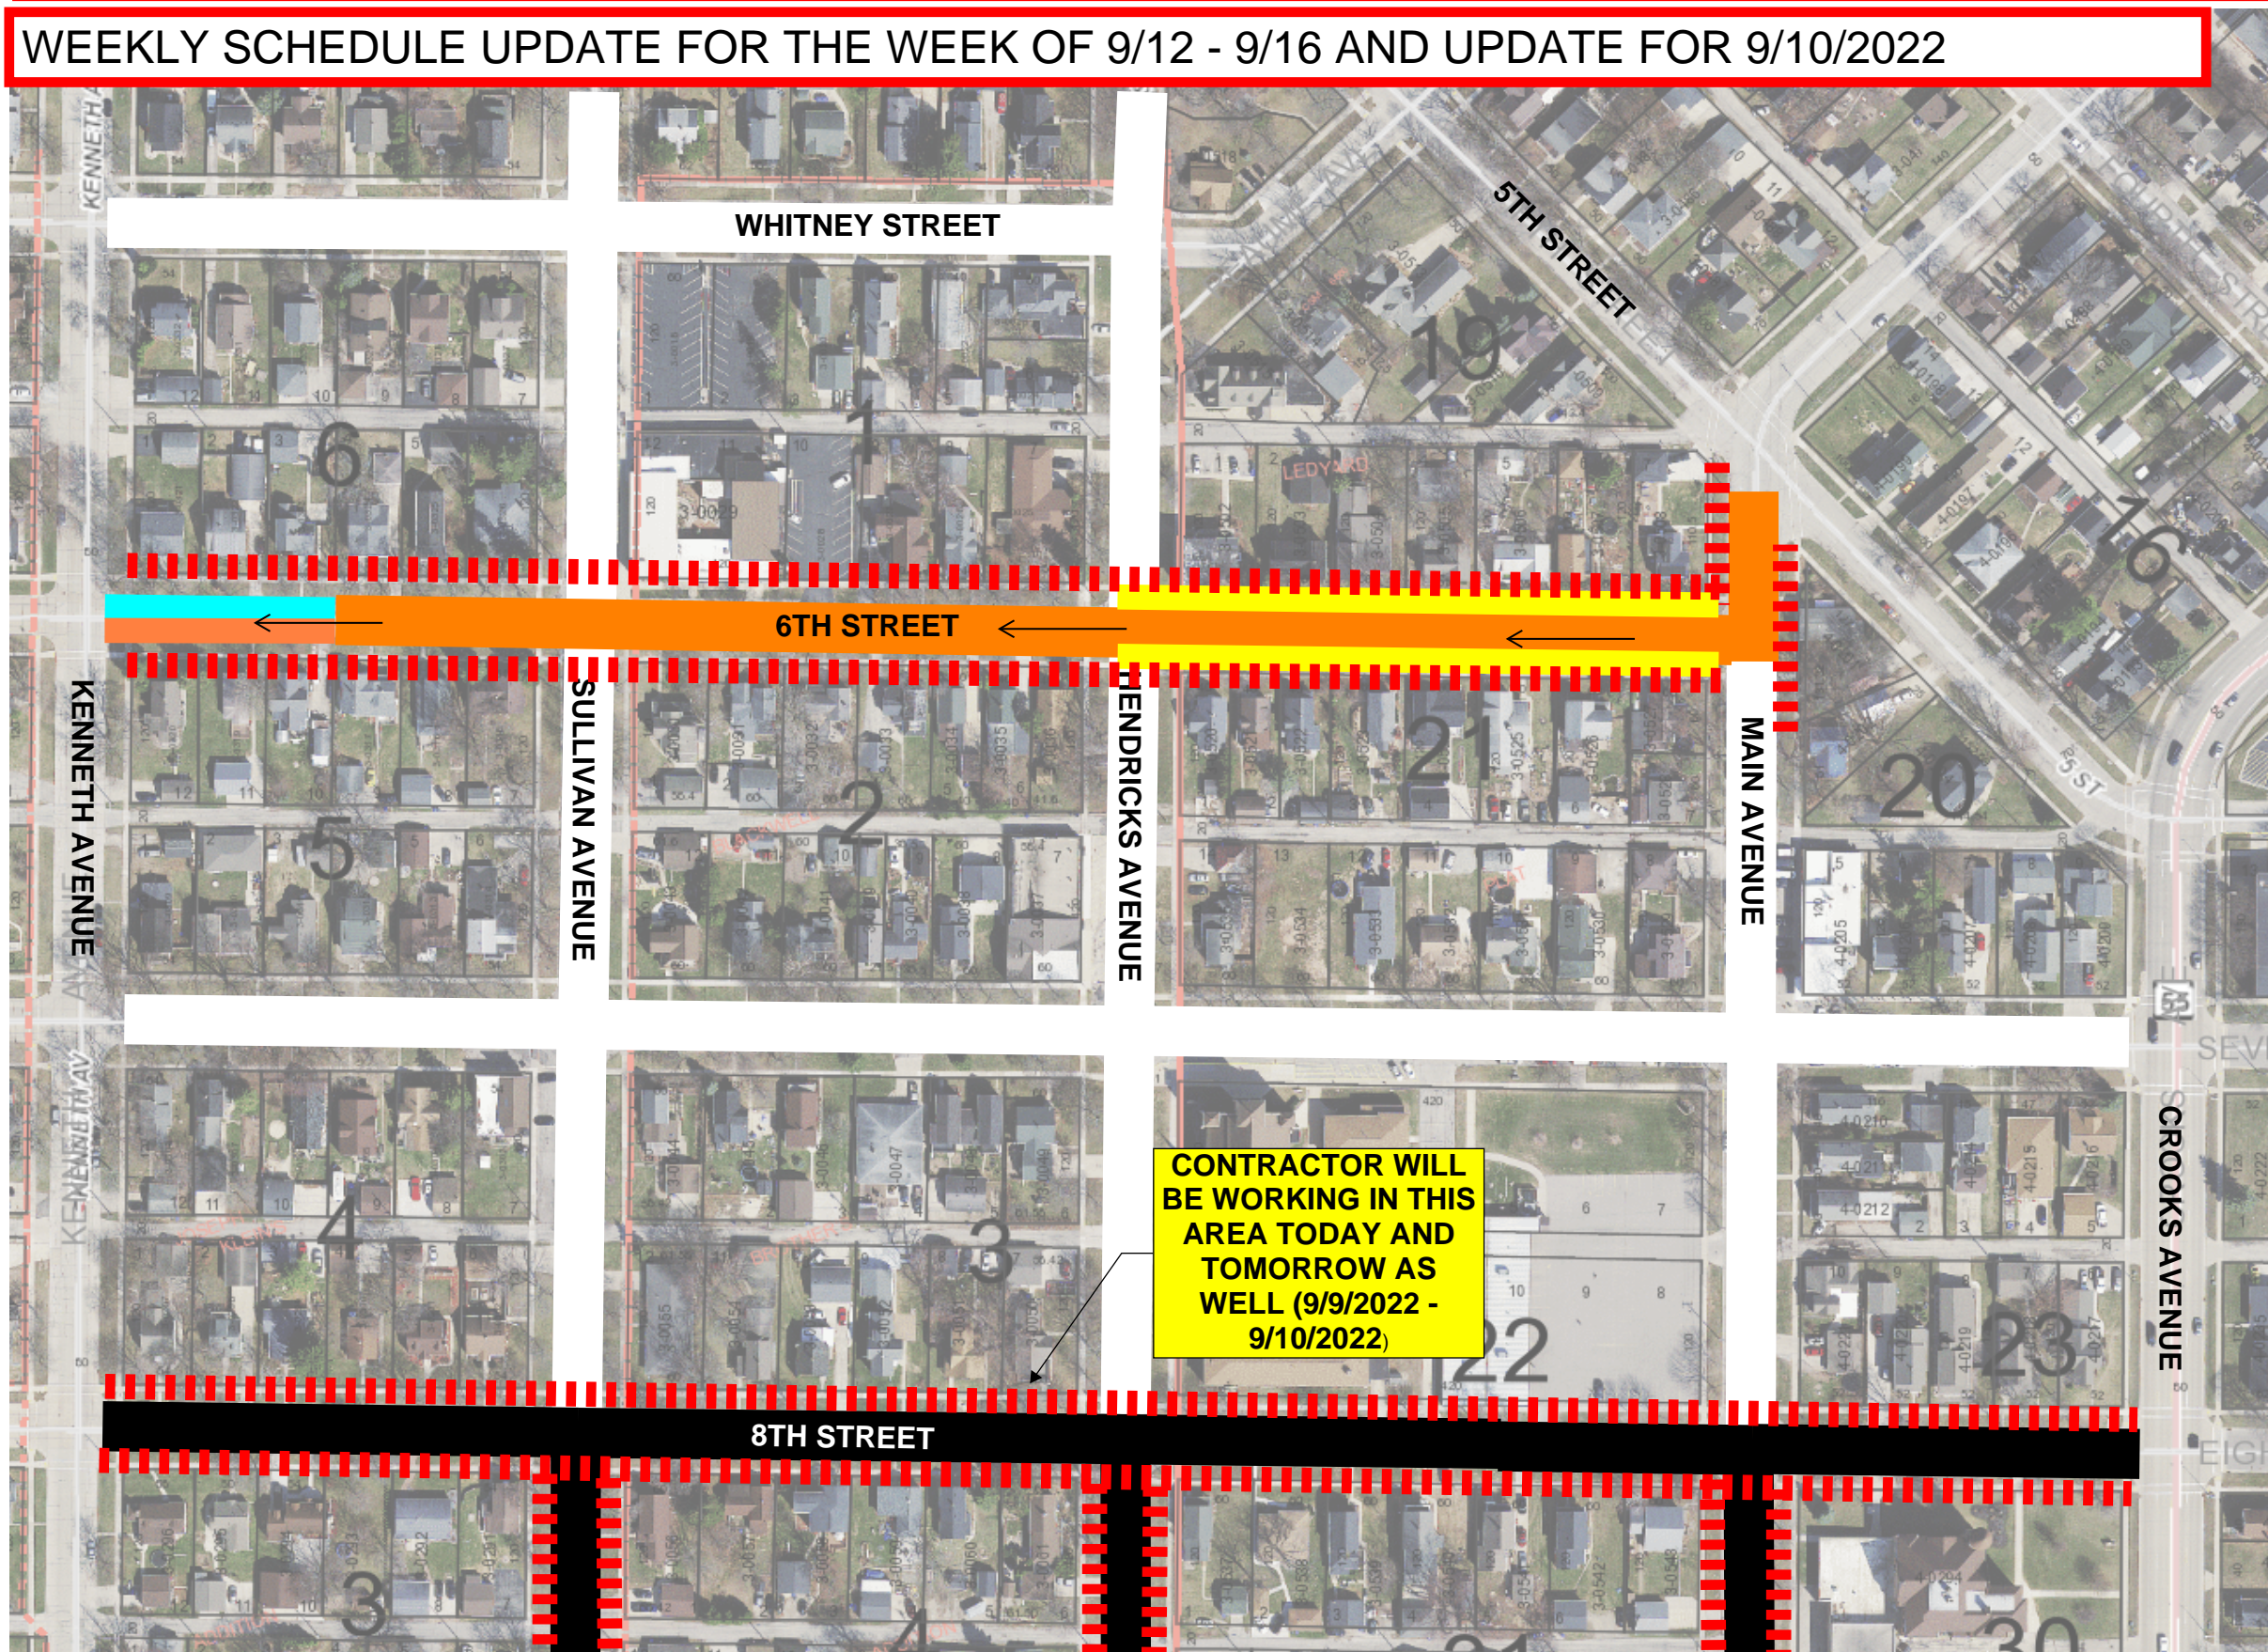

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

NO ACTIVE WORK

SANITARY SEWER WORK

WATER MAIN WORK

PUBLIC LATERALS/SERVICES

GRADING & PAVING WORK

RESTORATION

NO STREET PARKING = 

NOTES:

Update for Friday and Saturday (9/9 - 9/10):
The Paving Contractor will be on site this afternoon and tomorrow to Mill, prep, and pave 8th Street and Main, Sullivan, & Hendricks from 8th toward 9th. They will continue working next week to finish whatever is left after tomorrow.

On Monday the Sewer Contractor will begin working on Sanitary Sewer on Main Avenue. They will begin at 5th Intersection, work south toward 6th/Main intersection, then turn west down 6th and work toward Kenneth. Halfway through the week the 2nd crew will be back on site to finish Water Main on 6th, then begin working on public laterals following the 1st crew.

Recommended Parking - During construction hours, please find an alternate parking space if you can not access your driveway. Driveways should be open overnight once construction has ceased for the day. Please avoid driving on 6th Street all next week.

Thank you for joining the weekly email list! Encourage your neighbors to email Taylor Conger at tconger@kaukauna-wi.org to be added to the weekly email update list.
