


PROJECT 2-22 (KENNETH AVENUE AREA UTILITY RELAY)

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 9/19 - 9/23

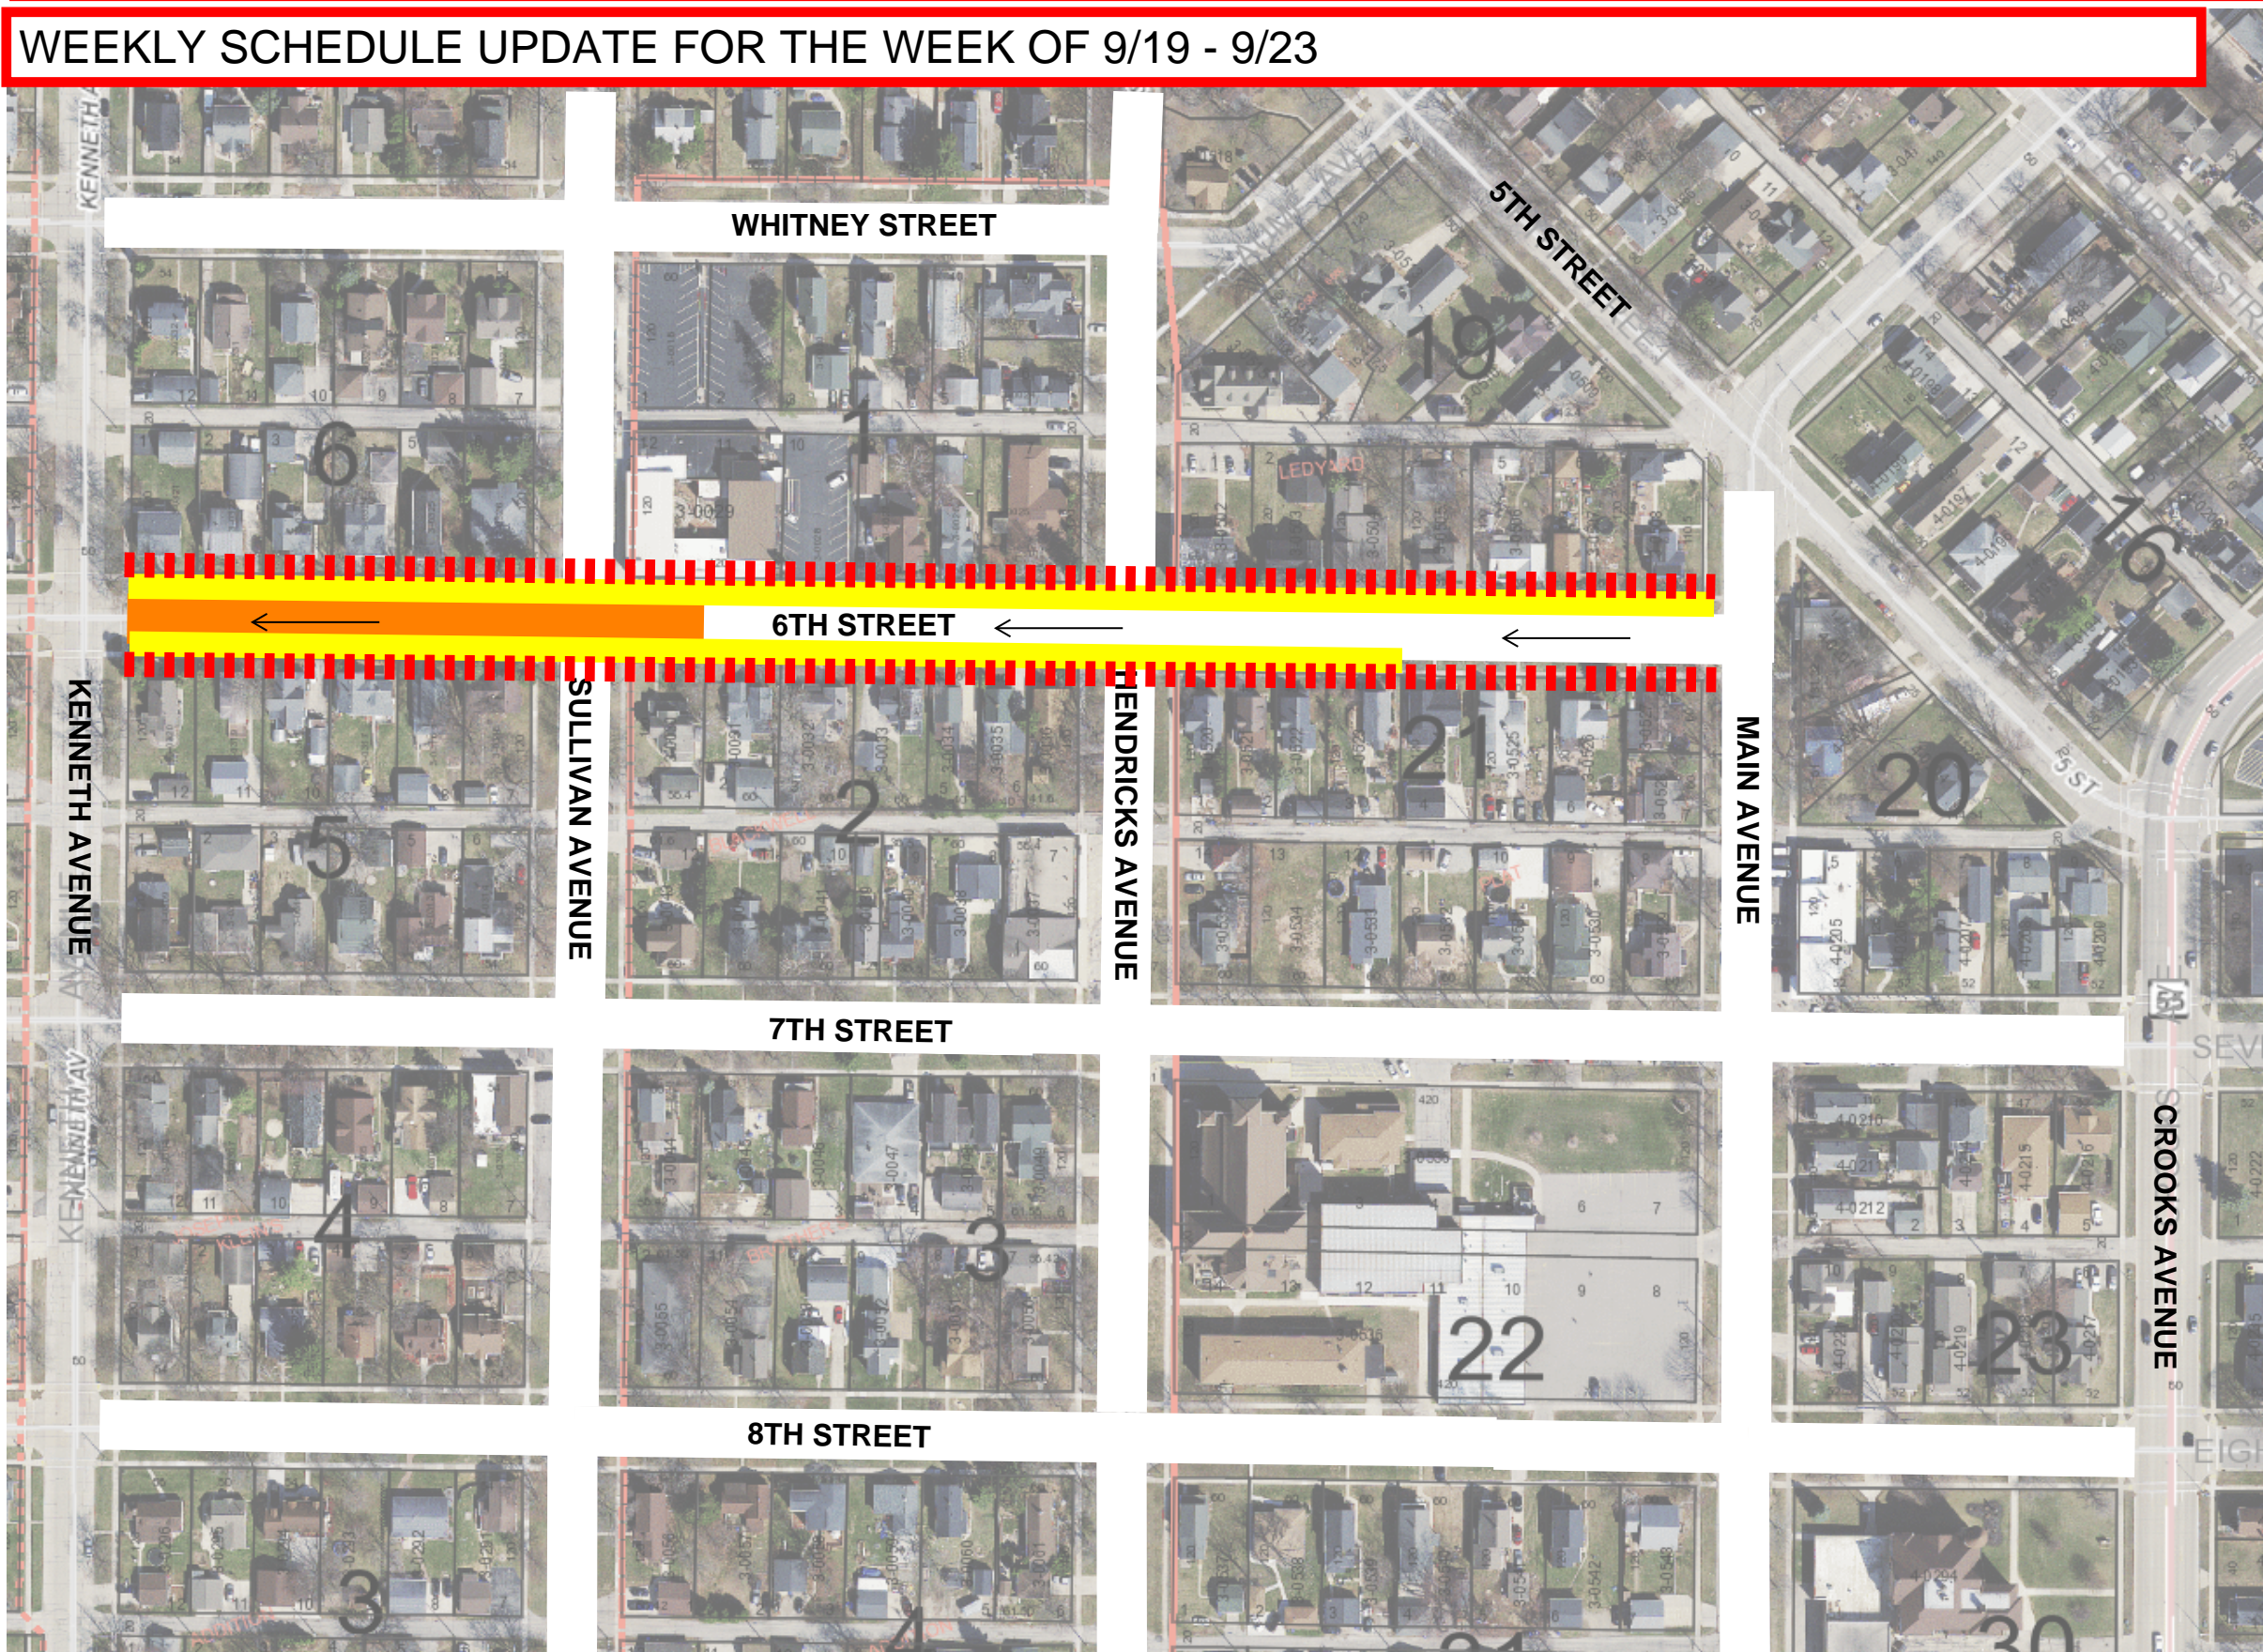

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- NO ACTIVE WORK
 - SANITARY SEWER WORK
 - WATER MAIN WORK
 - PUBLIC LATERALS/SERVICES
 - GRADING & PAVING WORK
 - RESTORATION
- NO STREET PARKING =

NOTES:

The Mainline Sewer crew will continue working on Sanitary main on 6th Street, continuing on Monday where they end today. The 2nd crew on site will be working on sanitary laterals and water services up to the back of sidewalk. Once the Main crew finishes Sanitary Main on 6th, they will also work on laterals.

Recommended Parking - During construction hours, please find an alternate parking space if you can not access your driveway. Driveways should be open overnight once construction has ceased for the day. Please avoid driving on 6th Street all next week.

Thank you for joining the weekly email list! Encourage your neighbors to email Taylor Conger at tconger@kaukauna-wi.org to be added to the weekly email update list.
