


# PROJECT 2-22 (KENNETH AVENUE AREA UTILITY RELAY)

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 9/26 - 9/30

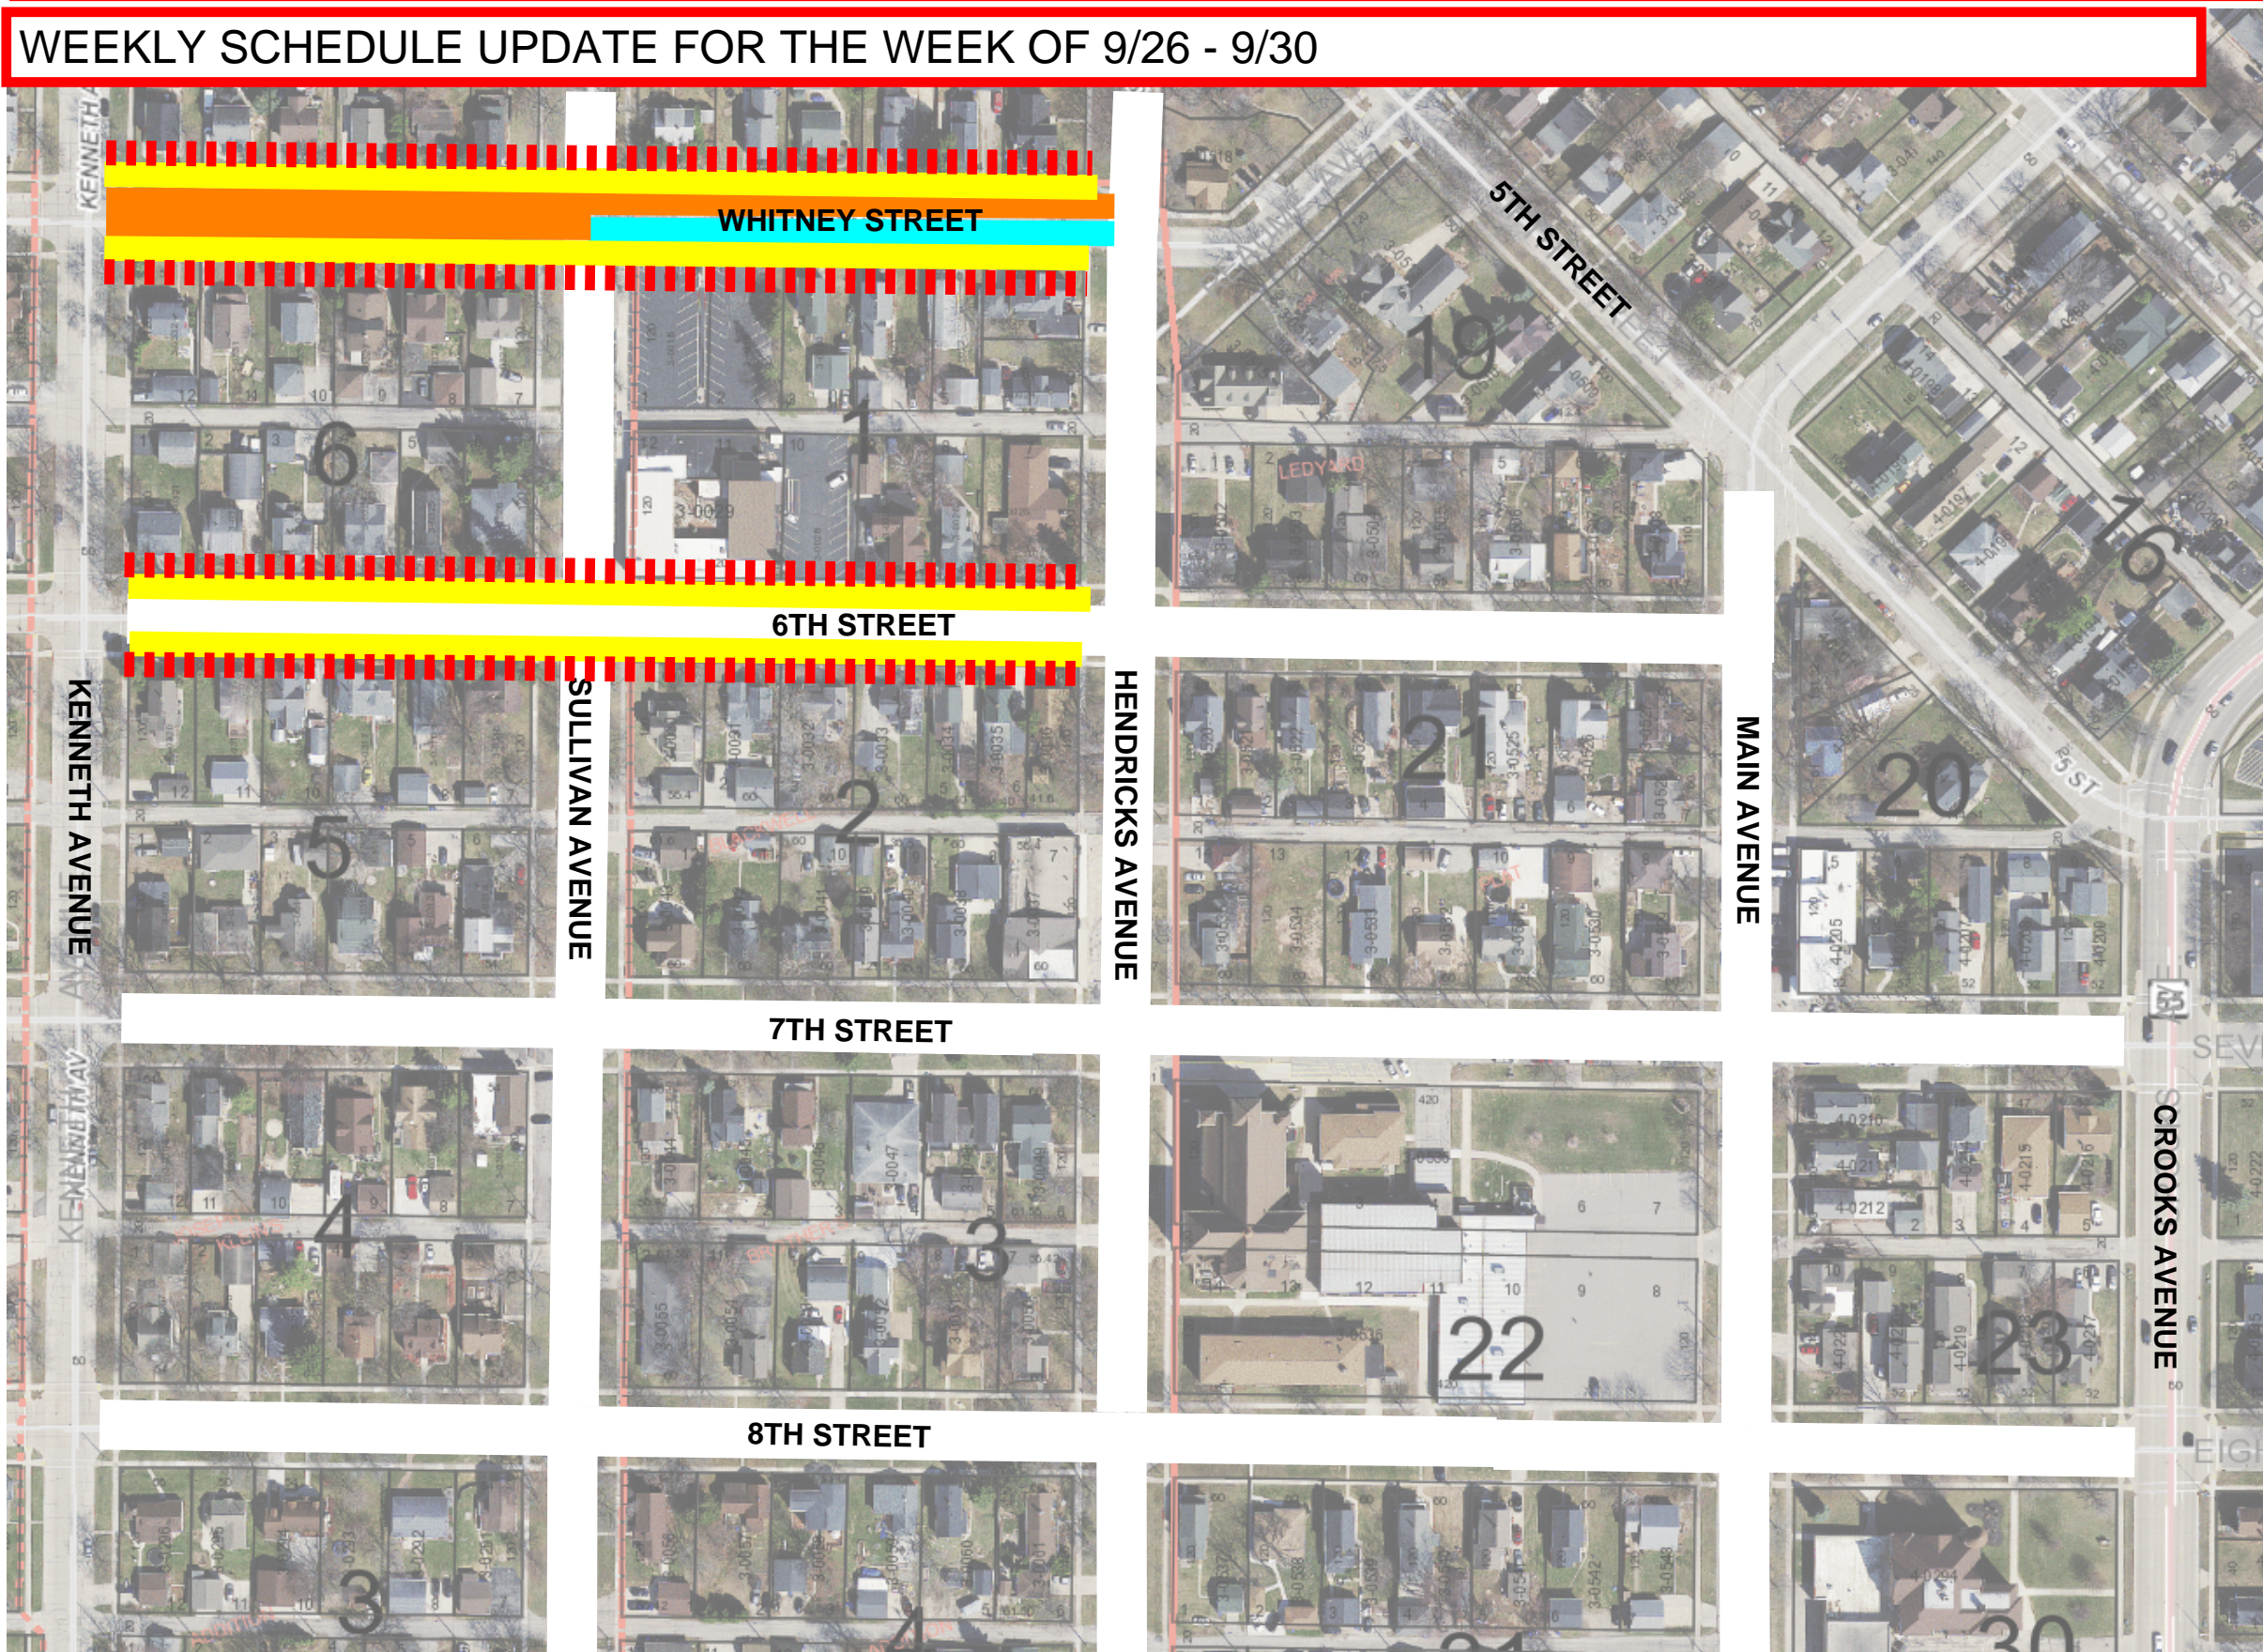

\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- NO ACTIVE WORK
- SANITARY SEWER WORK
- WATER MAIN WORK
- PUBLIC LATERALS/SERVICES
- GRADING & PAVING WORK
- RESTORATION

NO STREET PARKING = 

**NOTES:**

The Mainline sewer crew will be working on Sanitary Sewer and Water Main on Whitney Street next week. They will start with water between Sullivan and Hendricks, then work on Sanitary from Hendricks to Kenneth. Once both mains are constructed, they will work on public laterals on Whitney. The 2nd crew will continue working on 6th Street laterals until 6th is complete.

**Recommended Parking** - During construction hours, please find an alternate parking space if you can not access your driveway. Driveways should be open overnight once construction has ceased for the day. Please avoid driving on 6th Street all next week.

Thank you for joining the weekly email list! Encourage your neighbors to email Taylor Conger at [tconger@kaukauna-wi.org](mailto:tconger@kaukauna-wi.org) to be added to the weekly email update list.
