


# PROJECT 2-22 (KENNETH AVENUE AREA UTILITY RELAY)

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 9/6 - 9/9

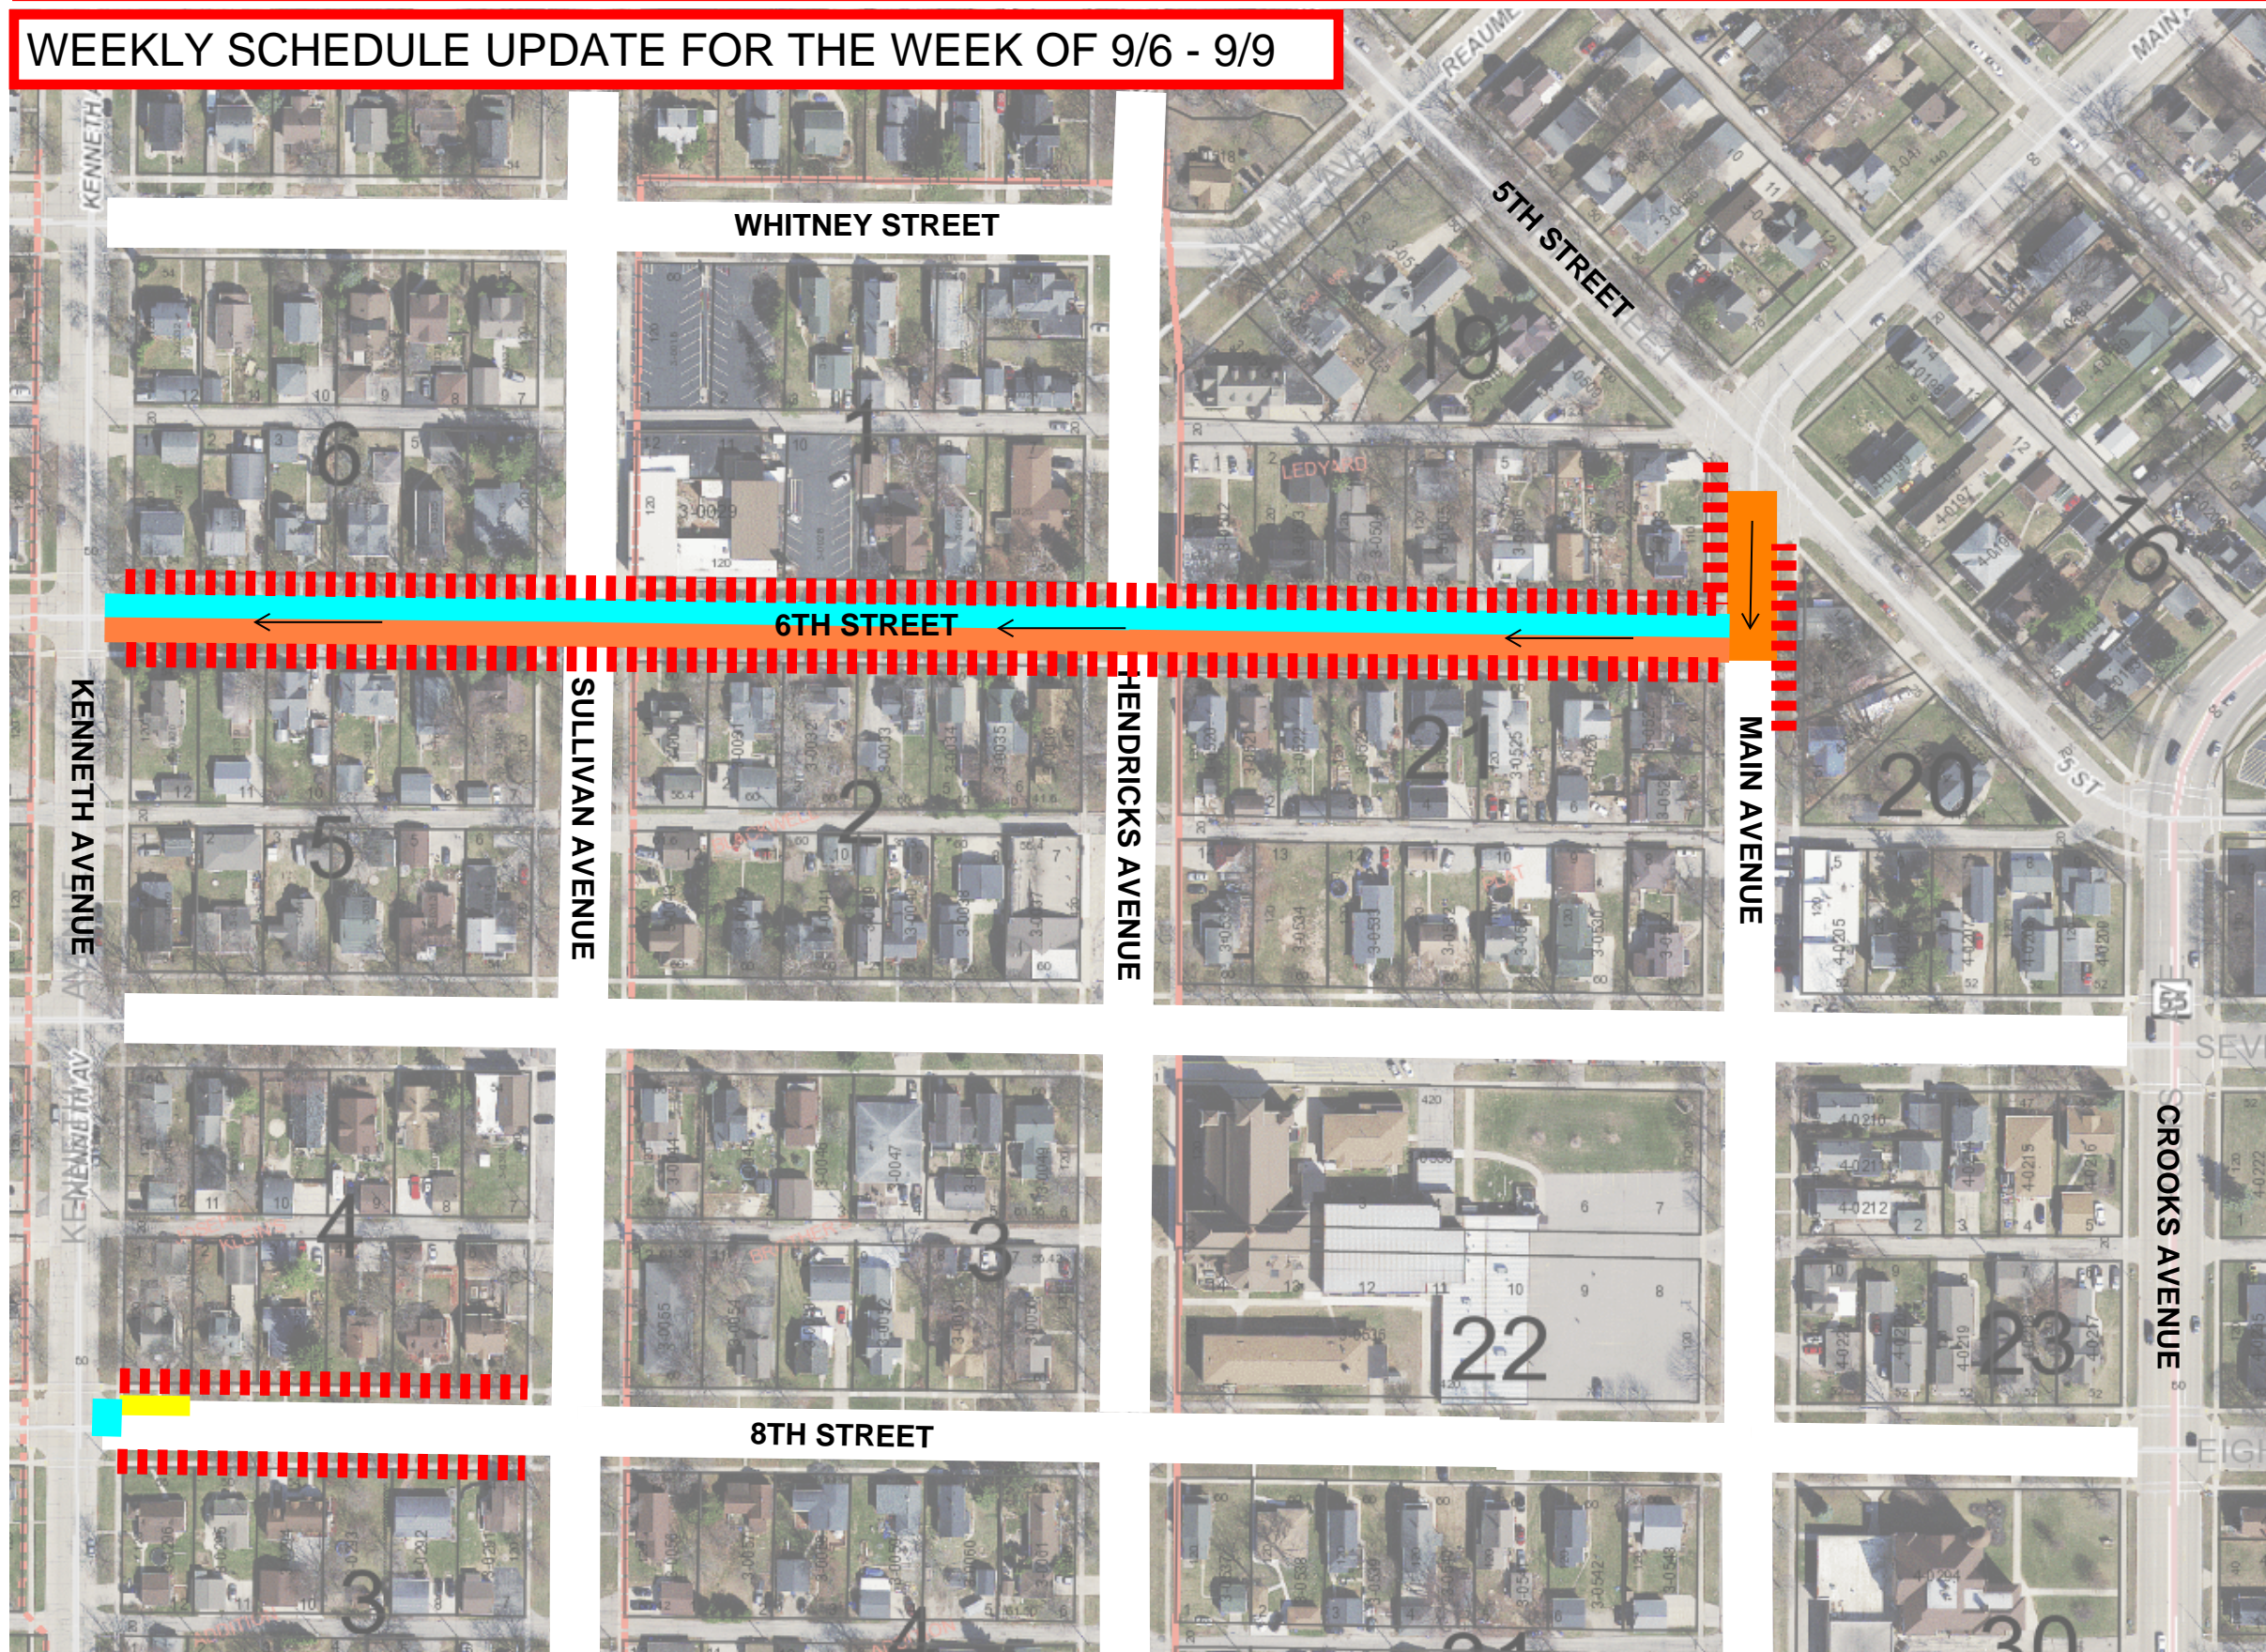

\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- NO ACTIVE WORK
  - SANITARY SEWER WORK
  - WATER MAIN WORK
  - PUBLIC LATERALS/SERVICES
  - GRADING & PAVING WORK
  - RESTORATION
- NO STREET PARKING =

**NOTES:**

Monday is a Holiday, there will be no work on site.

Tuesday - Friday: Contractor will begin working on 6th Street Sewer & Water Mains next week. They will begin by Main Avenue, and work their way West toward Kenneth Avenue. They will start with Water Main, and transition to Sanitary throughout the week. There are a few miscellaneous items to be completed on 8th Street that the 2nd crew will be finishing Tuesday/Wednesday before joining 1st Crew on 6th.

**Recommended Parking** - During construction hours, please find an alternate parking space if you can not access your driveway. Driveways should be open overnight once construction has ceased for the day. Please avoid driving on 6th Street all next week.

Thank you for joining the weekly email list! Encourage your neighbors to email Taylor Conger at [tconger@kaukauna-wi.org](mailto:tconger@kaukauna-wi.org) to be added to the weekly email update list.
