


# PROJECT 1-22 (ISLAND STREET RECONSTRUCTION)

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 10/3 - 10/7

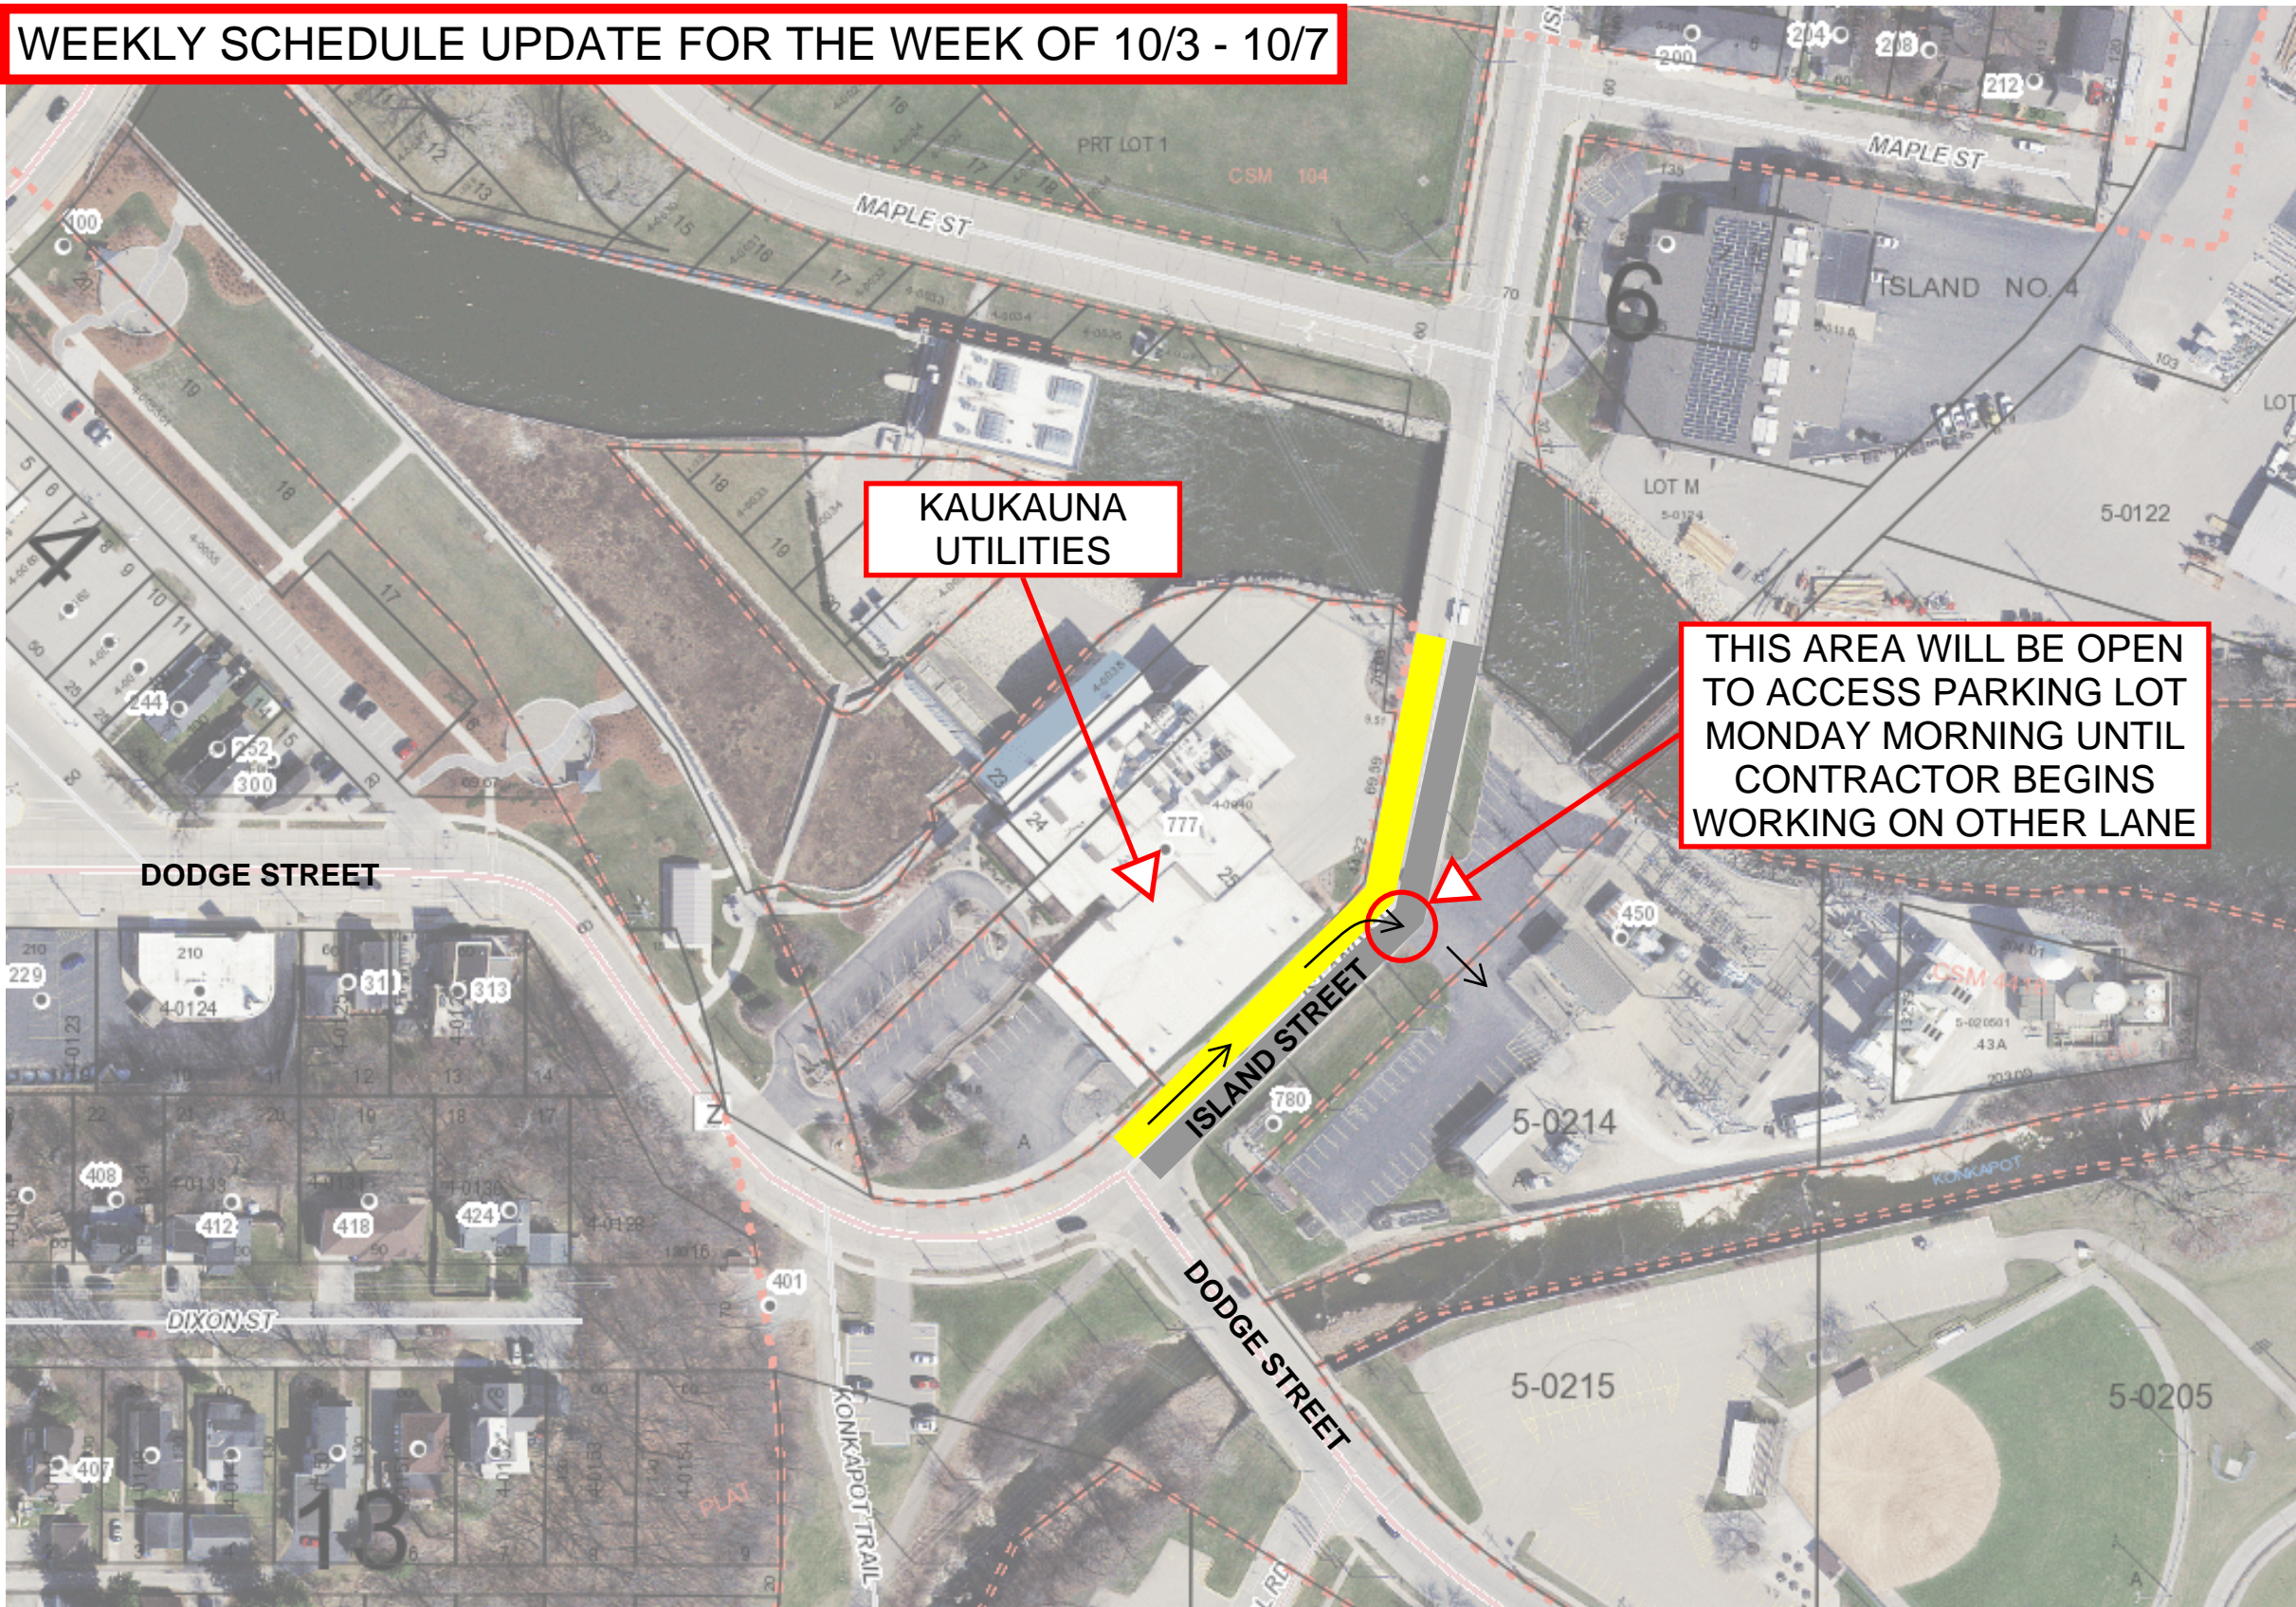

\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- CONCRETE PAVING COMPLETE
- SIDEWALK/DRIVEWAY WORK
- RECOMMENDED PARKING
- NO PARKING = [Red dashed line]
- TEMPORARY PARKING = [Pink solid line]

THIS AREA WILL BE OPEN TO ACCESS PARKING LOT MONDAY MORNING UNTIL CONTRACTOR BEGINS WORKING ON OTHER LANE

KAUKAUNA UTILITIES

NOTES:  
 East lane was paved today. 1 Day Cure mix was used in the area circled in the drawing. By Monday morning this area will be ramped with gravel and will be open to access the parking lot there. This area will remain ramped until the contractor comes back to site to work on the west lane (Scheduled for Thursday & Friday next week).

Thank you for joining the weekly email list! Encourage your neighbors to email Taylor Conger at [tconger@kaukauna-wi.org](mailto:tconger@kaukauna-wi.org) to be added to the weekly email update list.
