


PROJECT 2-22 (KENNETH AVENUE AREA UTILITY RELAY)

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 10/3 - 10/7

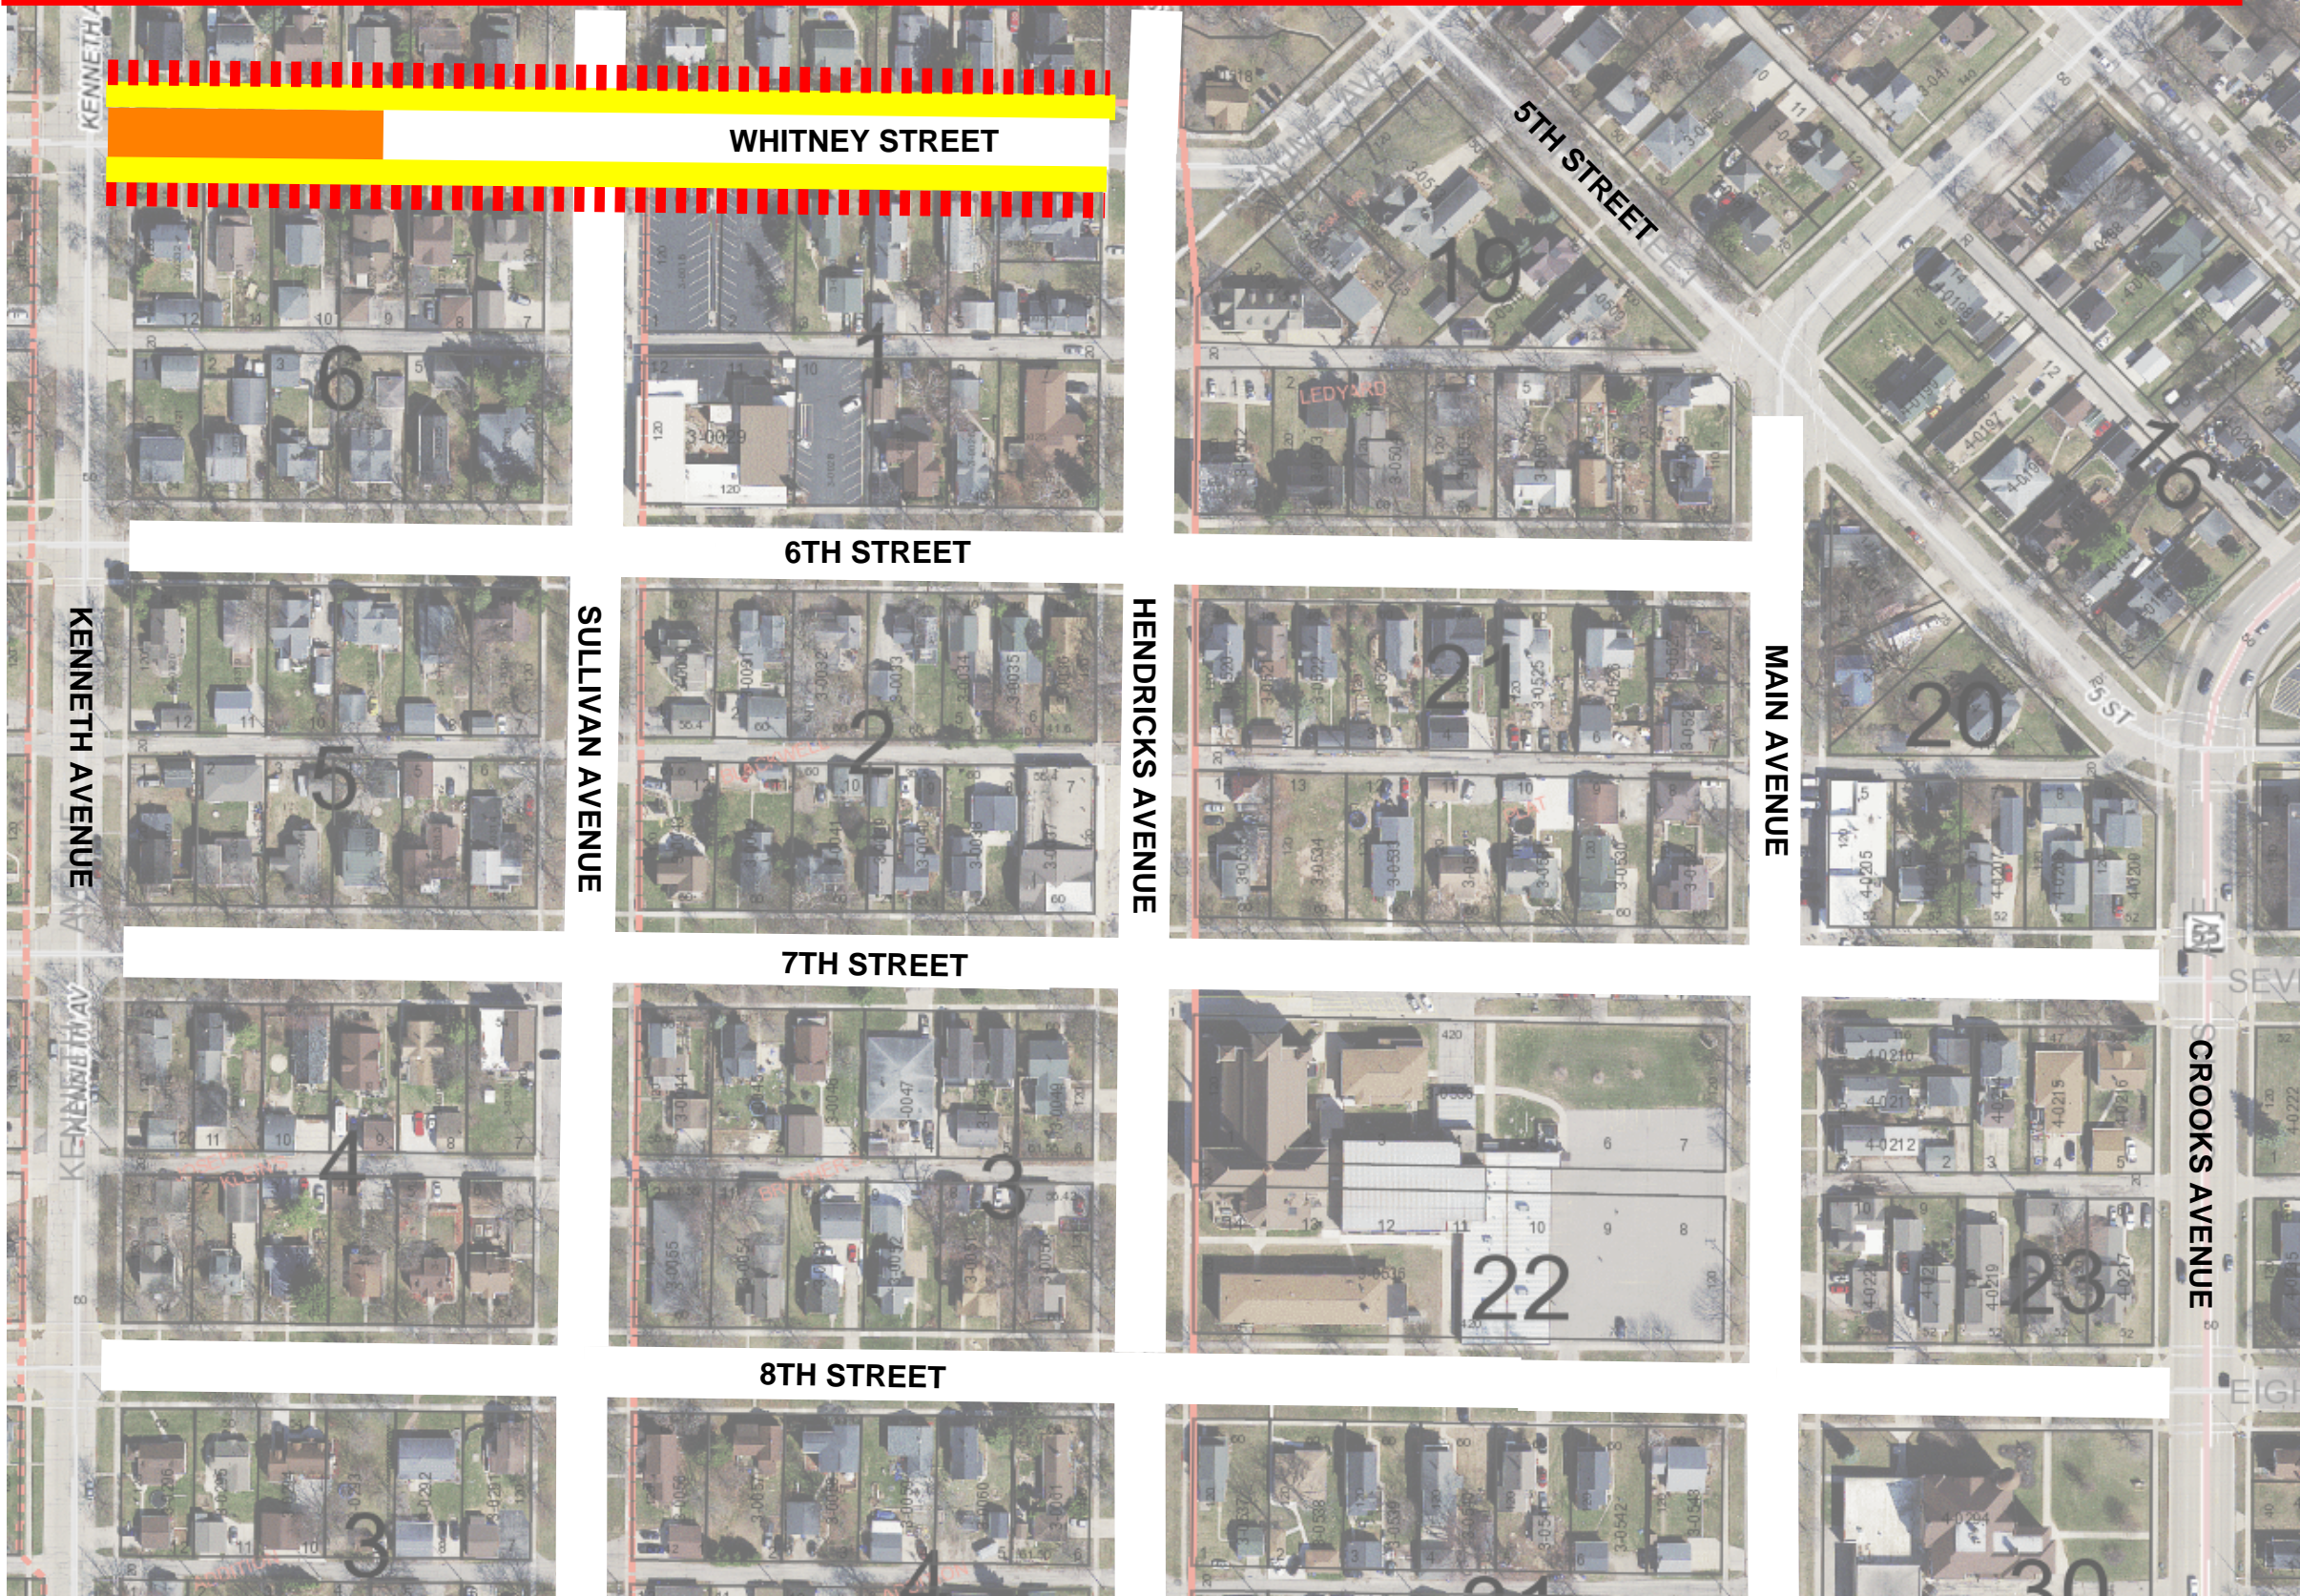

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- NO ACTIVE WORK
 - SANITARY SEWER WORK
 - WATER MAIN WORK
 - PUBLIC LATERALS/SERVICES
 - GRADING & PAVING WORK
 - RESTORATION
- NO STREET PARKING =

NOTES:

The Mainline sewer crew will continue Sanitary Main Relay for remainder of Whitney Street on Monday. They should be able to finish what's left in one day. Once they finish that, they will begin working on Public Sanitary and Water Services to individual houses for the rest of the week. They will work on those until all are done, then this contractor's main work is complete.

Recommended Parking - During construction hours, please find an alternate parking space if you can not access your driveway. Driveways should be open overnight once construction has ceased for the day. Please avoid driving on 6th Street all next week.

Thank you for joining the weekly email list! Encourage your neighbors to email Taylor Conger at tconger@kaukauna-wi.org to be added to the weekly email update list.
