


PROJECT 1-23 METOXEN, DIXON, QUINNEY & SEVENTH

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 5/22 - 5/26

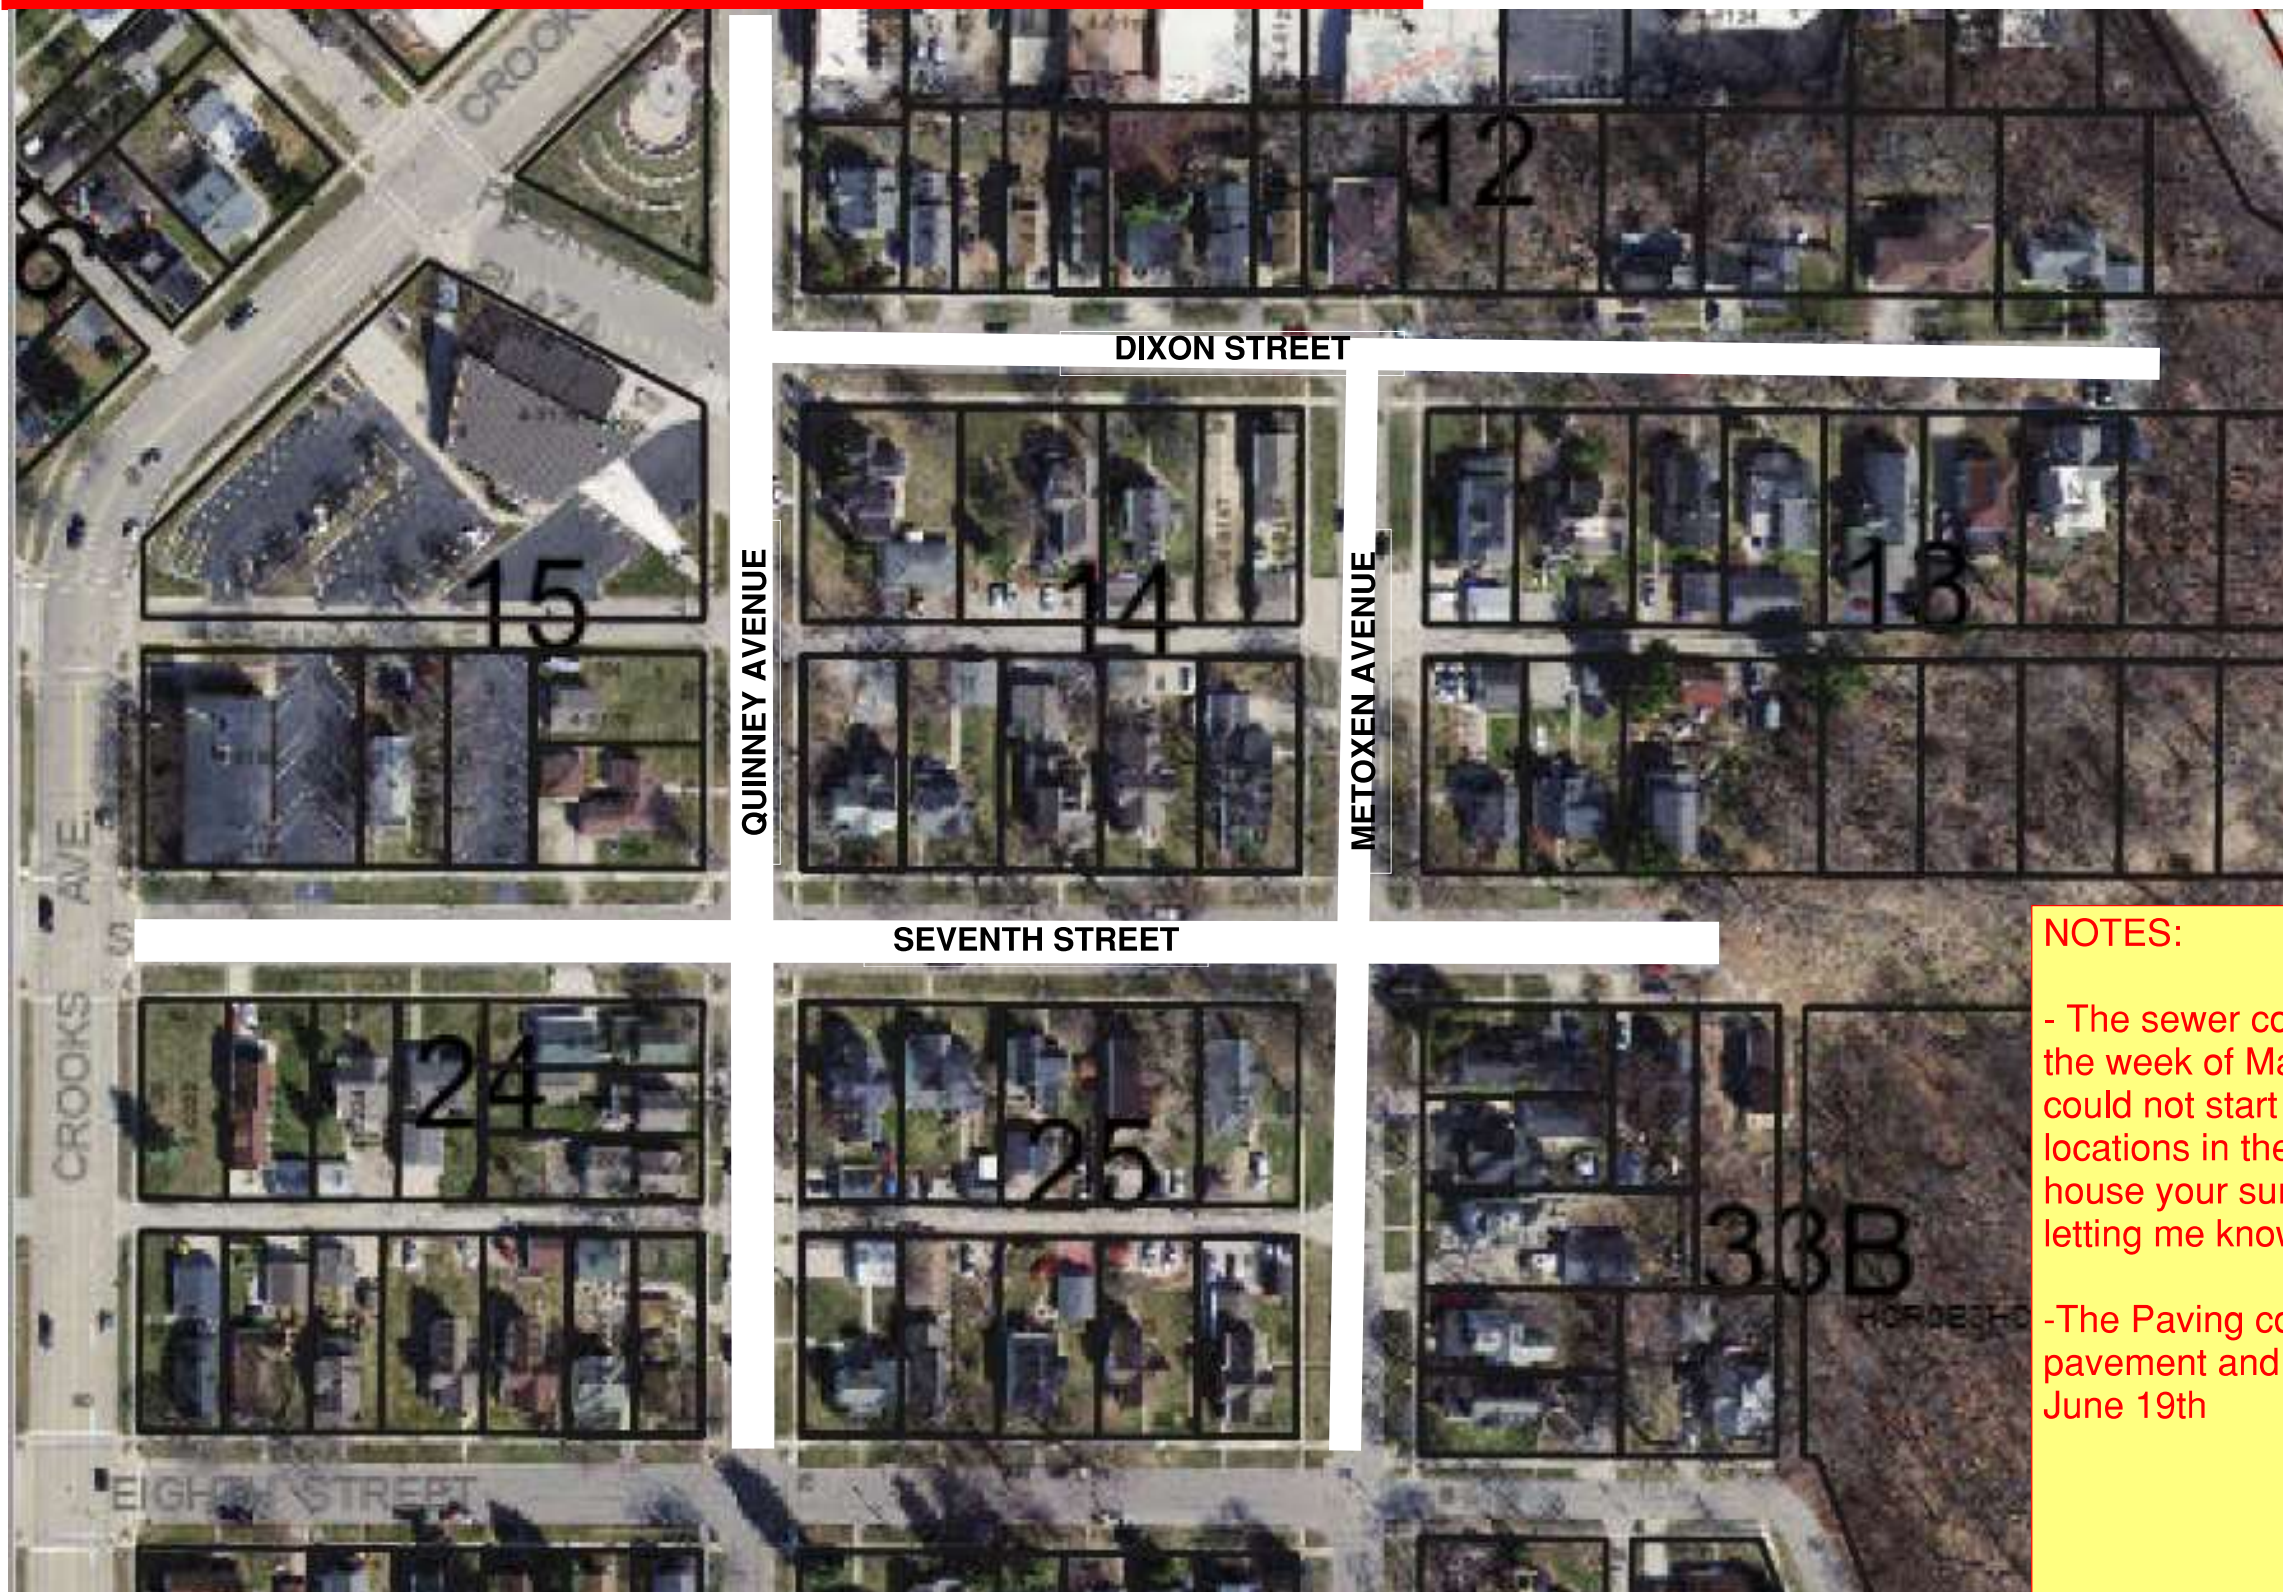

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

NOTES:

- The sewer contractor is planning to start the storm sewer work the week of May 30th. Material details are why the contractor could not start before the 30th. We will be marking storm lateral locations in the next 2 weeks. If you know which side of your house your sump pump discharges to, you send me an e-mail letting me know.

-The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of June 19th

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 WHITE DOVE, WHITE BIRCH, LODERBAUER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 5/22 - 5/26



*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDEWALK/DRIVEWAY WORK

NOTES:

- The Paving contractor is planning to start removing existing pavement and excavating the existing stone base on Loderbauer Road the week of June 26th.
- The Paving contractor will start grading White Dove Lane and White Birch Lane the week of June 26th.
- The Water Utilitie's contractor will doing water replacement along Loderbauer Road, from White Wolf Lane to White Dove Lane, the week of June 5th.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 5/22 - 5/26



*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

NOTES:

-The Paving contractor will start grading Greyhound Street and Boxer Street the week of June 5th.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 OAK & SCHULTHEIS

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 5/22 - 5/26



*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK


NOTES:

- The sewer contractor is planning to start the storm sewer work the week of June 26th

-The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of July 17th

PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 5/22 - 5/26

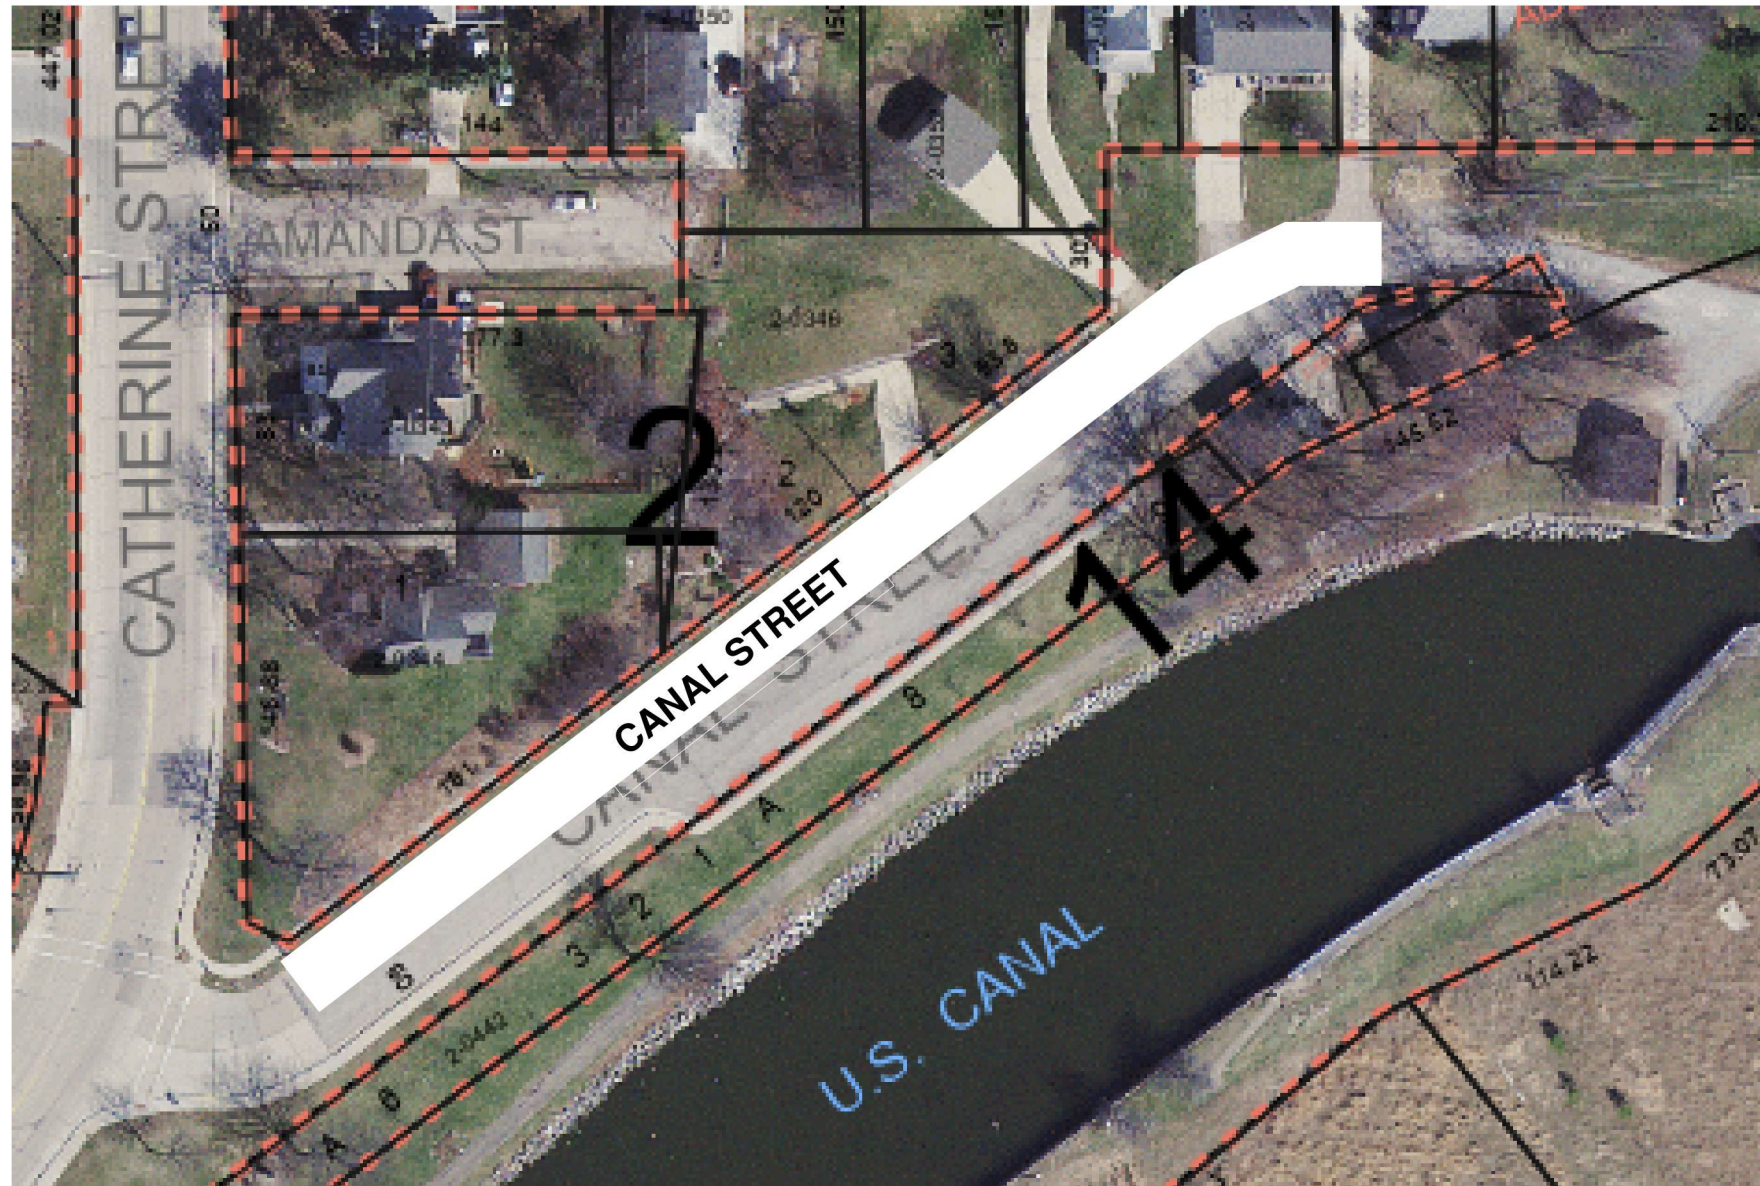

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

NOTES:

- The sewer contractor is planning to start the storm sewer work the week of June 29th

-The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of July 31st

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.
