


PROJECT 1-23 METOXEN, DIXON, QUINNEY & SEVENTH

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 6/12 - 6/16

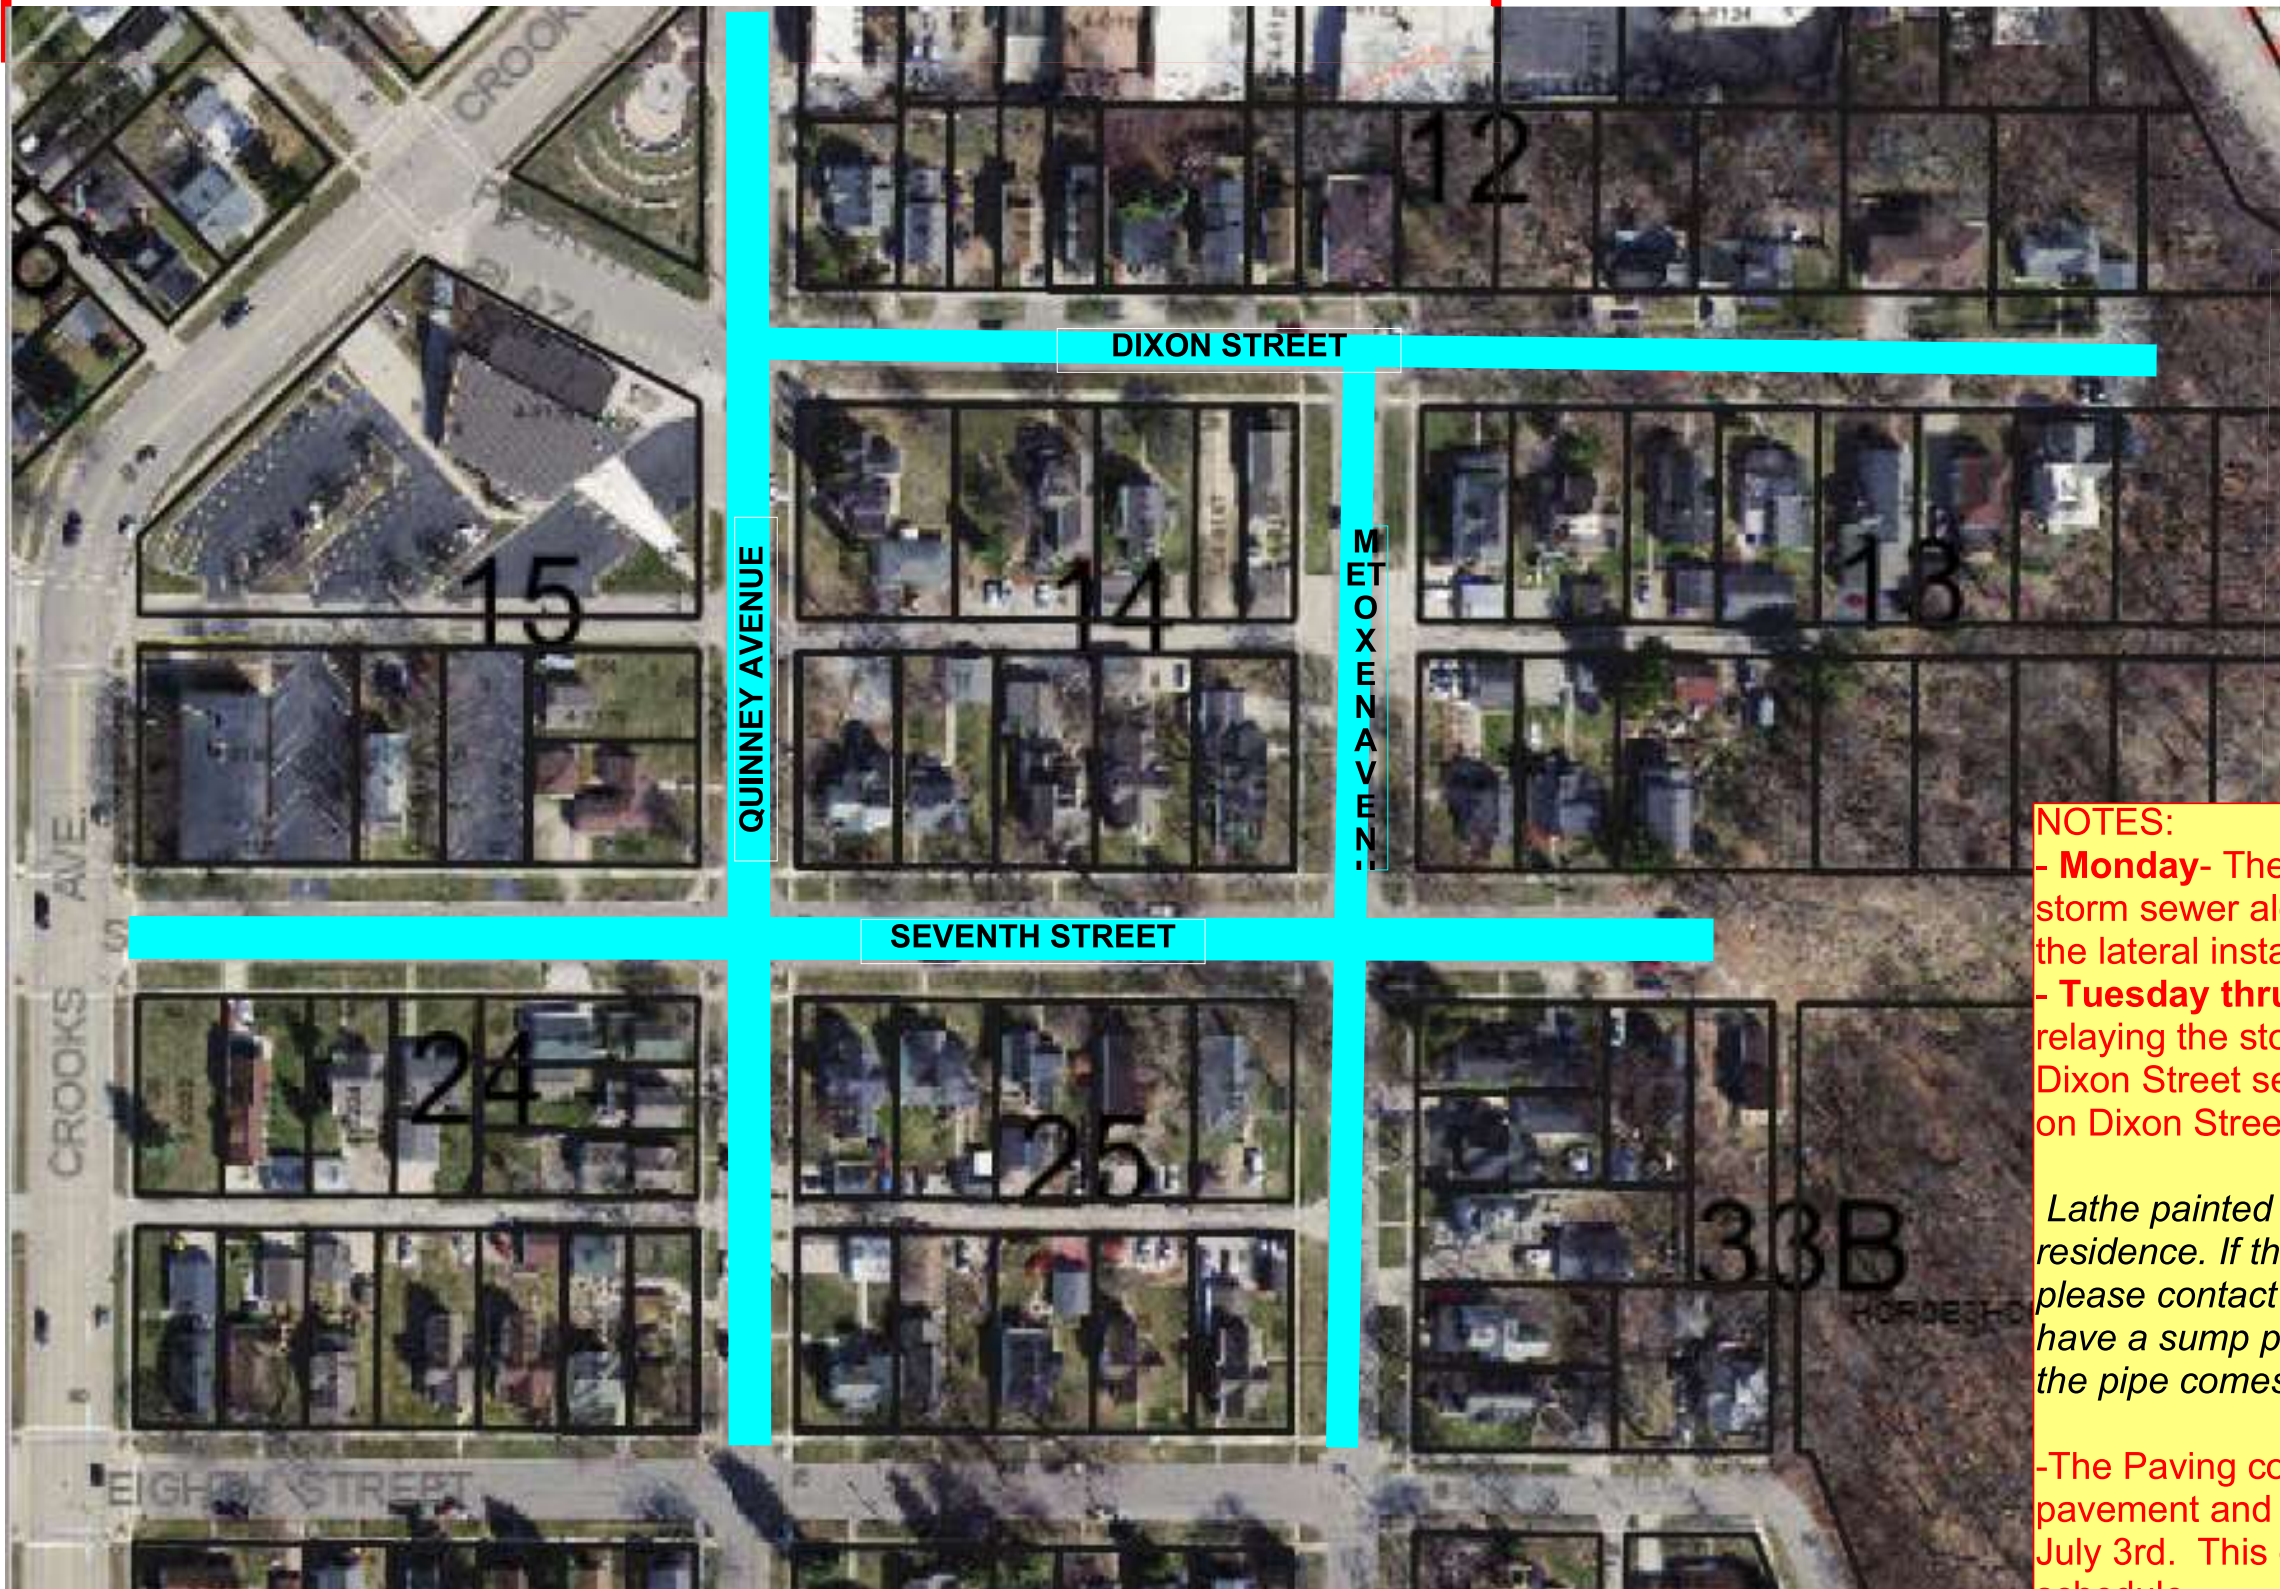

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

NOTES:

- **Monday**- The storm sewer contractor will continue to install storm sewer along Dixon St. Their storm lateral crew might start the lateral installations.
- **Tuesday thru Friday** - The storm sewer contractor may start relaying the storm sewer in Seventh Street when they finish the Dixon Street sewer work. The lateral crew will continue to work on Dixon Street.

Lathe painted pink has been placed in front of most of the residence. If the stake is not where you want your storm lateral, please contact me and I will move it to where you want it. If you have a sump pump, please e-mail me which side of your house the pipe comes out and your address.

-The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of July 3rd. This date was moved back due to the contractors schedule.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 WHITE DOVE, WHITE BIRCH, LODERBAUER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 6/12 - 6/16



*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

NOTES:

- The Paving contractor is planning to start removing existing pavement and excavating the existing stone base on Loderbauer Road the week of July 10th.
- The Paving contractor will start grading White Dove Lane and White Birch Lane the week of July 10th.
- The Water Utilitie's contractor will continue doing water replacement along Loderbauer Road, from White Wolf Lane to White Dove Lane, the week of June 12th. More information about this is attached to the e-mail.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 6/12 - 6/16



*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDEWALK/DRIVEWAY WORK

NOTES:
-The Paving contractor will start grading Greyhound Street and Boxer Street the week of June 19th.

PROJECT 1-23 OAK & SCHULTHEIS

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 6/12 - 6/16



*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK


NOTES:

- The sewer contractor is planning to start the storm sewer work the week of July 3rd.
- The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of July 31st

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 6/12 - 6/16

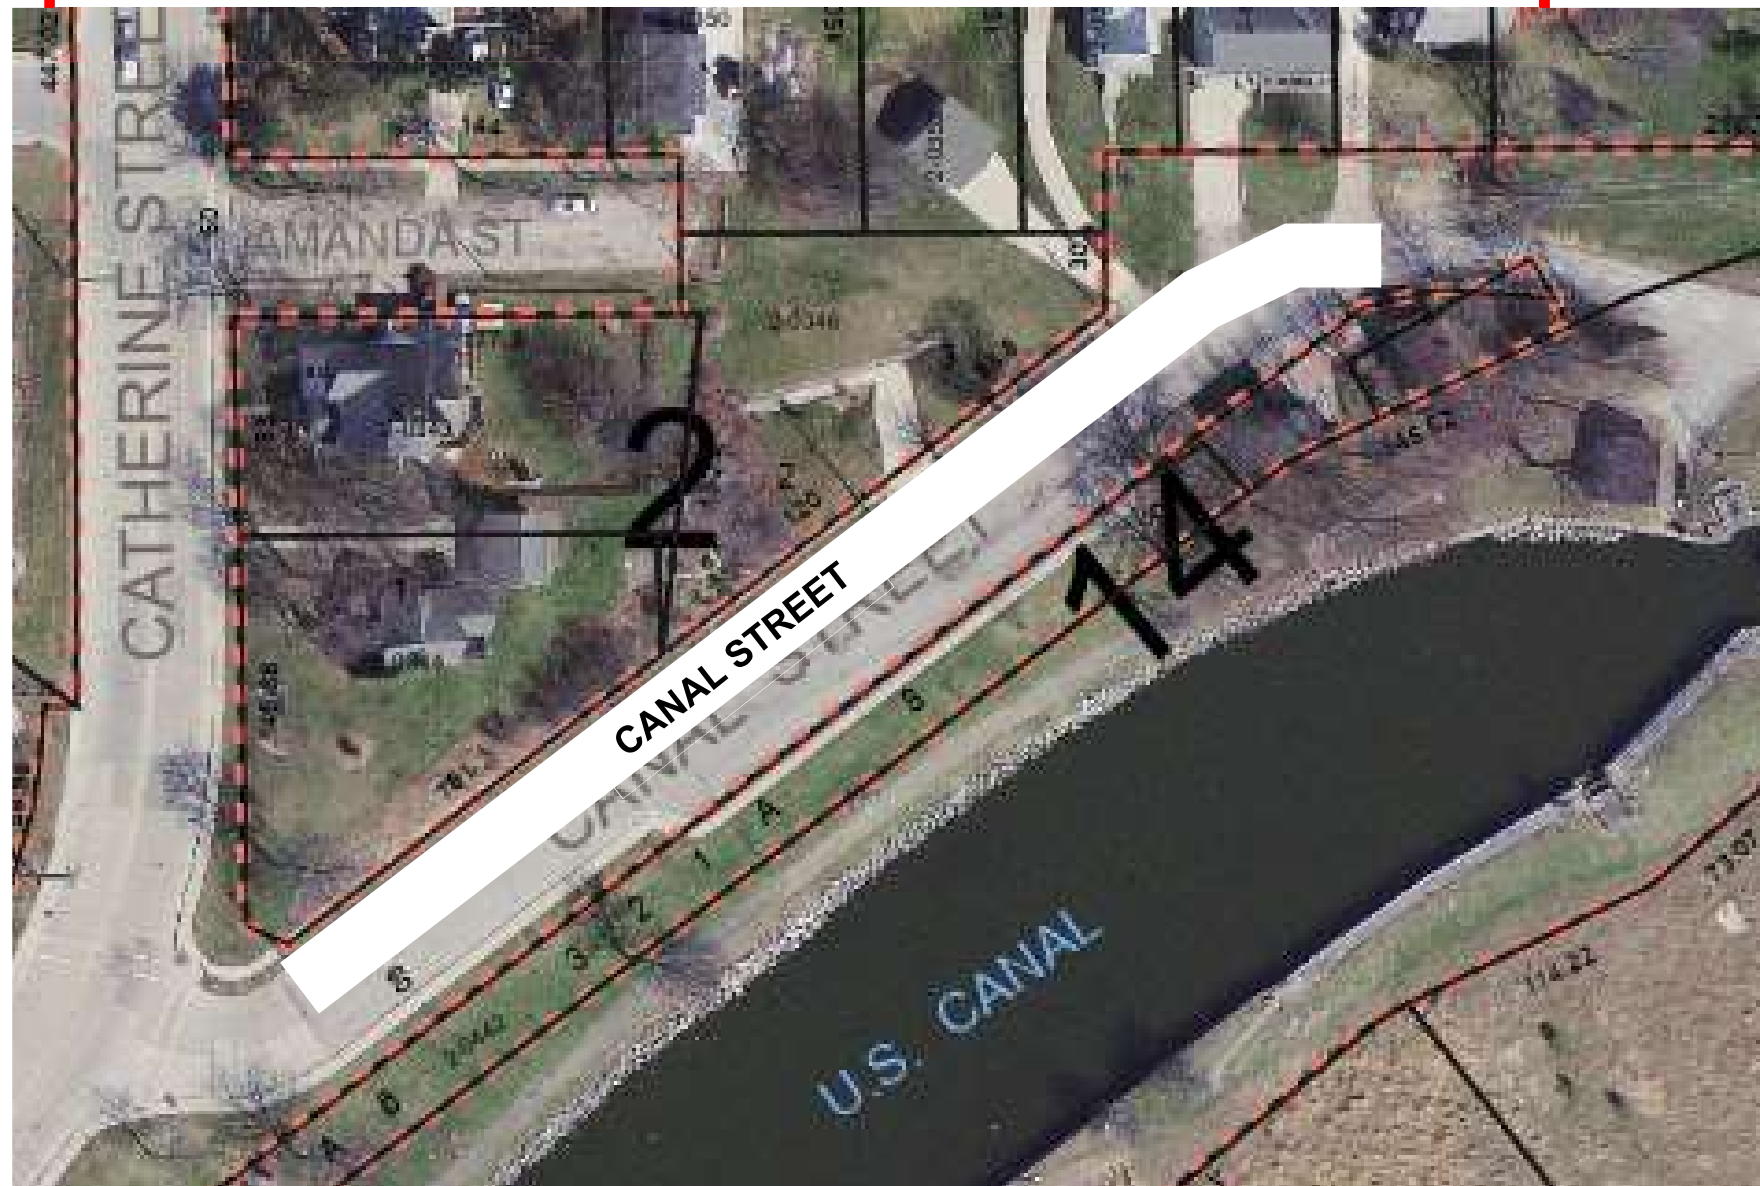

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDEWALK/DRIVEWAY WORK

NOTES:

- The sewer contractor is planning to start the storm sewer work the week of July 10th
- The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of August 7th

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.
