


# PROJECT 1-23 METOXEN, DIXON, QUINNEY & SEVENTH

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 6/19 - 6/23

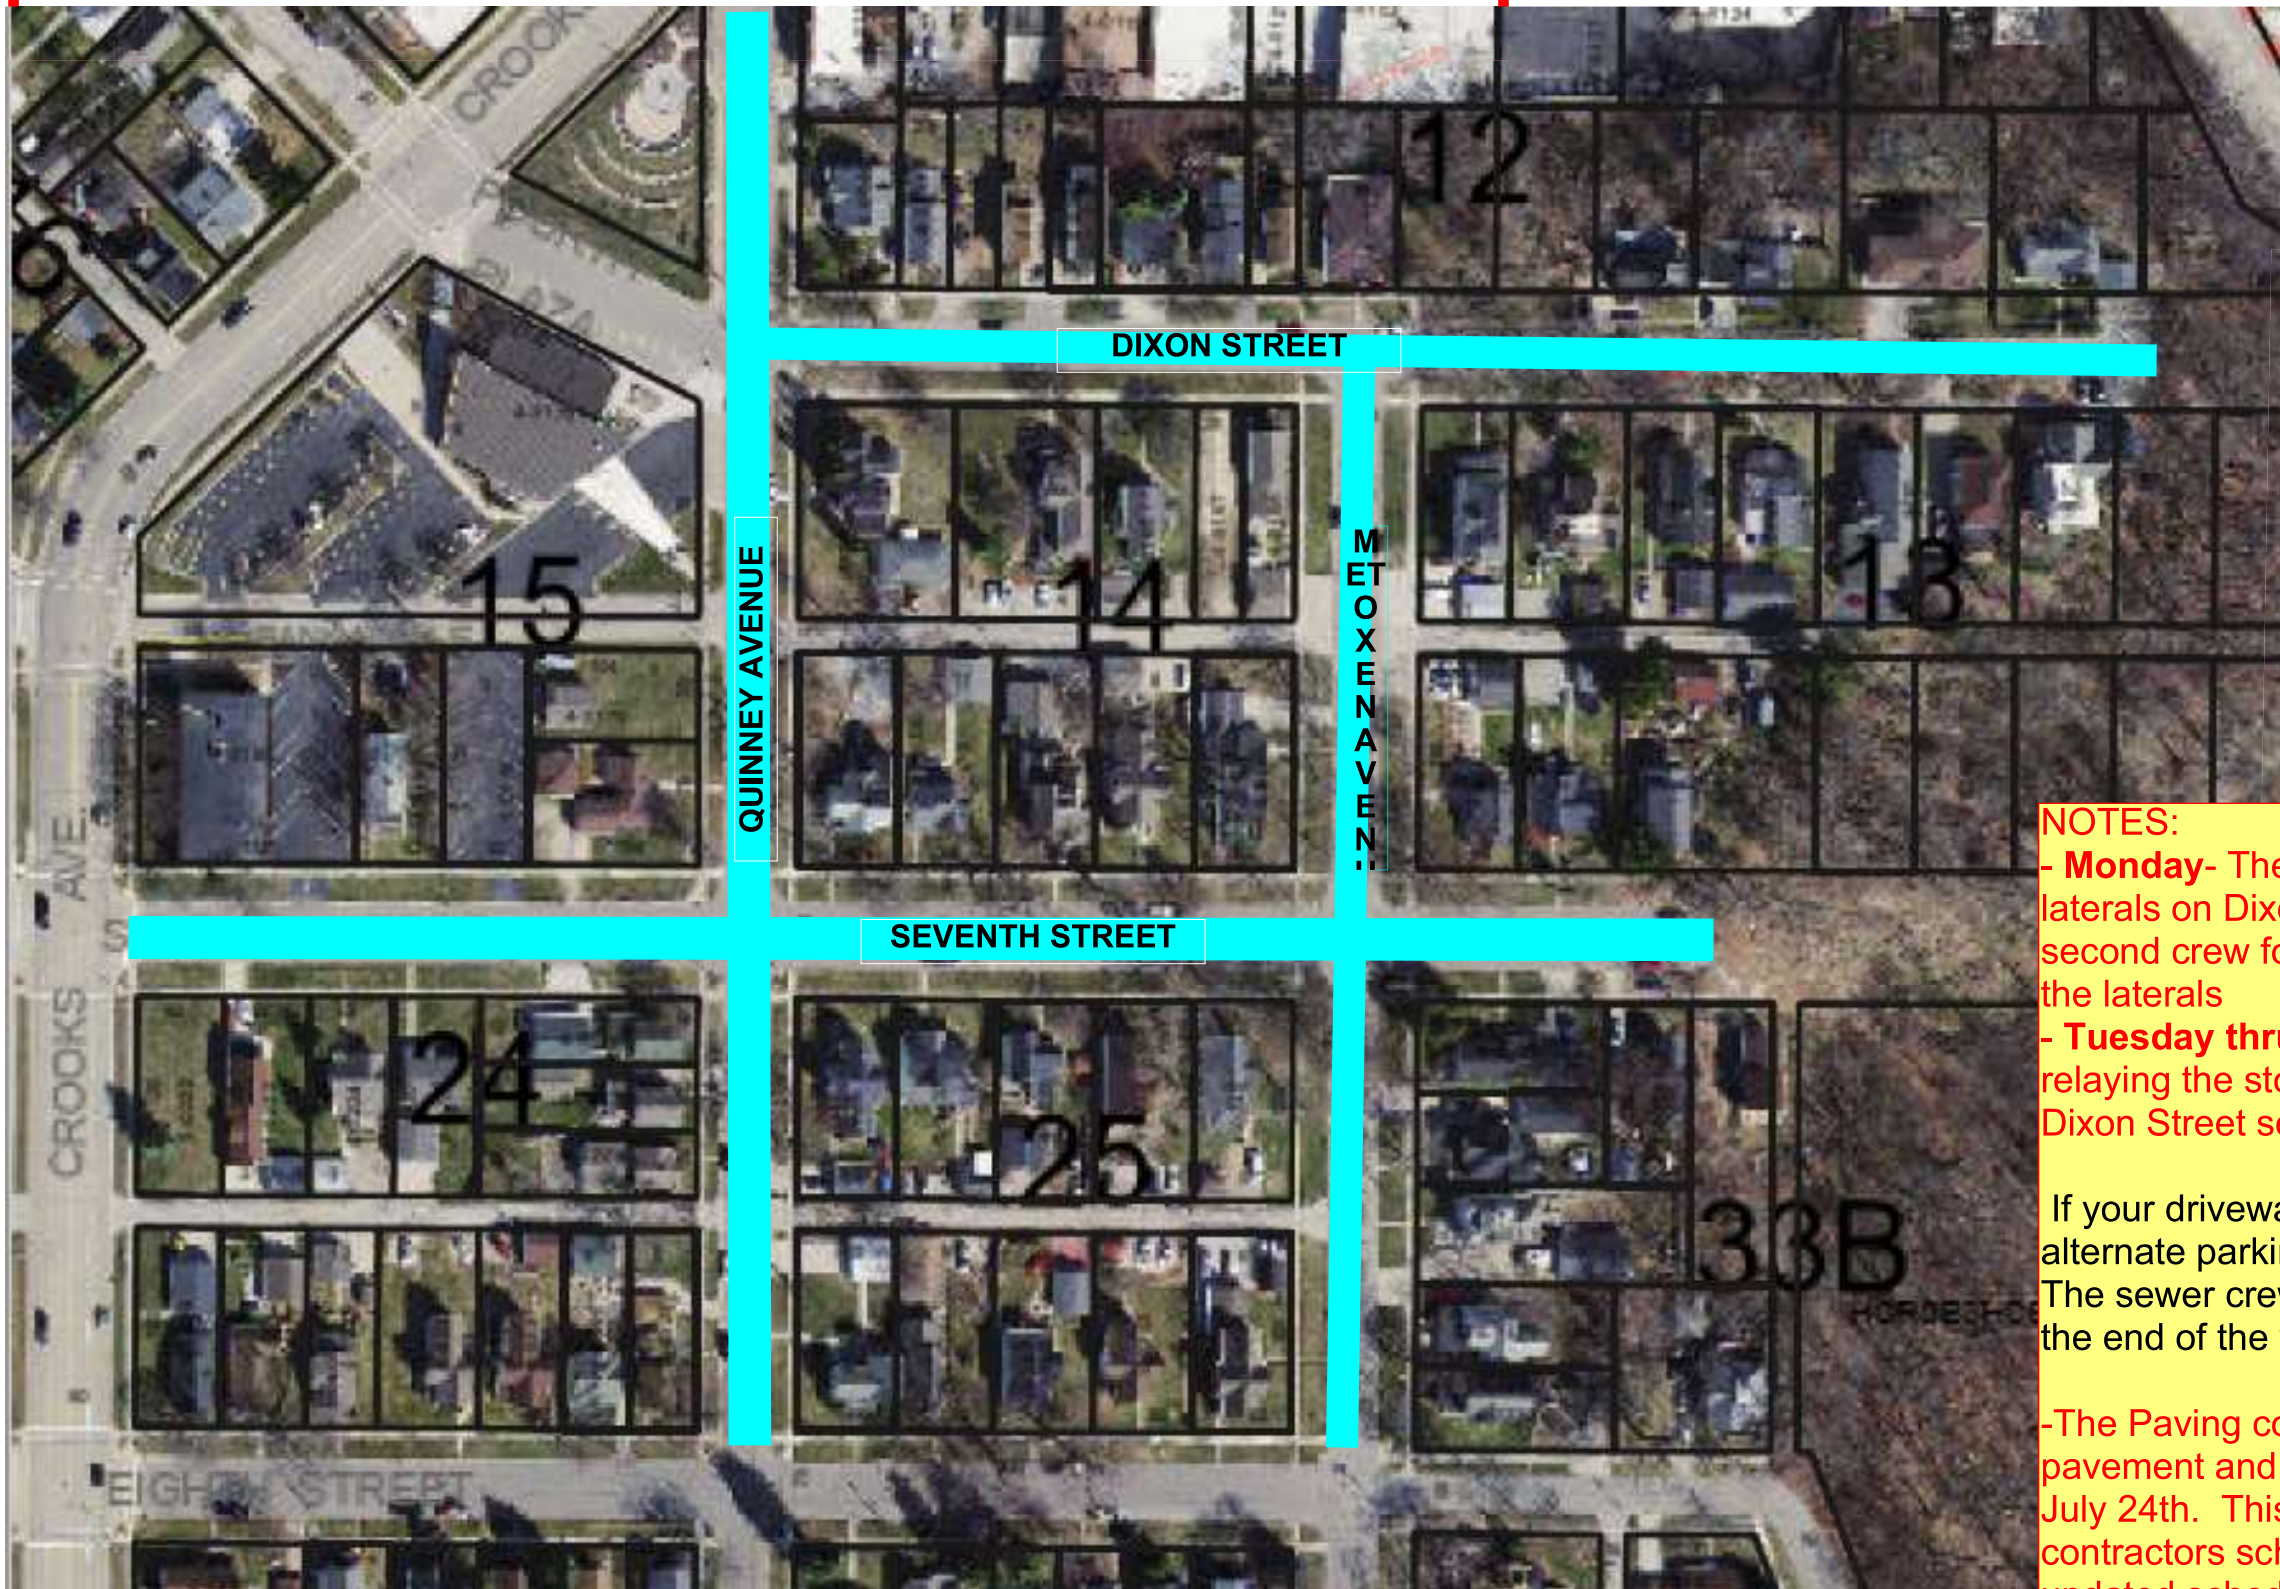

\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDEWALK/DRIVEWAY WORK

### NOTES:

- **Monday**- The storm sewer contractor will finish installing storm laterals on Dixon. The sewer contractor was not able to get a second crew for storm laterals, so the main line crew has to do the laterals
- **Tuesday thru Friday** - The storm sewer contractor should start relaying the storm sewer in Seventh Street when they finish the Dixon Street sewer work.

If your driveway is along Seventh Street, you may need to find alternate parking while the sewer crew works in front of your lot. The sewer crew should have the driveways open for parking at the end of the work day.

-The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of July 24th. This date was moved back again due to the contractors schedule. When the paving contractor has a set updated schedule, I will send out another update.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at [jbodoh@kaukauna-wi.org](mailto:jbodoh@kaukauna-wi.org) to be added to the weekly email update list.



# PROJECT 1-23 WHITE DOVE, WHITE BIRCH, LODERBAUER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 6/19 - 6/23



\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

## NOTES:

-The Paving contractor is planning to start removing existing pavement and excavating the existing stone base on Loderbauer Road the week of July 17th. When the paving contractor has a set updated schedule, I will send out another update.

-The Paving contractor will start grading White Dove Lane and White Birch Lane the week of July 24th. The contractor has moved dates back due to their scheduling issues. When the paving contractor has a set updated schedule, I will send out another update.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at [jbodoh@kaukauna-wi.org](mailto:jbodoh@kaukauna-wi.org) to be added to the weekly email update list.



# PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 6/19 - 6/23



\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

## NOTES:

-The Paving contractor will start grading Greyhound Street and Boxer Street the week of July 5th. The contractor has moved dates back due to their scheduling issues. When the paving contractor has a set updated schedule, I will send out another update.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at [jbodoh@kaukauna-wi.org](mailto:jbodoh@kaukauna-wi.org) to be added to the weekly email update list.

# PROJECT 1-23 OAK & SCHULTHEIS

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 6/19 - 6/23



\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK


## NOTES:

- The sewer contractor is planning to start the storm sewer work the week of July 10th
- The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of August 14th. The contractor has moved dates back due to their scheduling issues. When the paving contractor has a set updated schedule, I will send out another update.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at [jbodoh@kaukauna-wi.org](mailto:jbodoh@kaukauna-wi.org) to be added to the weekly email update list.

# PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 6/19 - 6/23

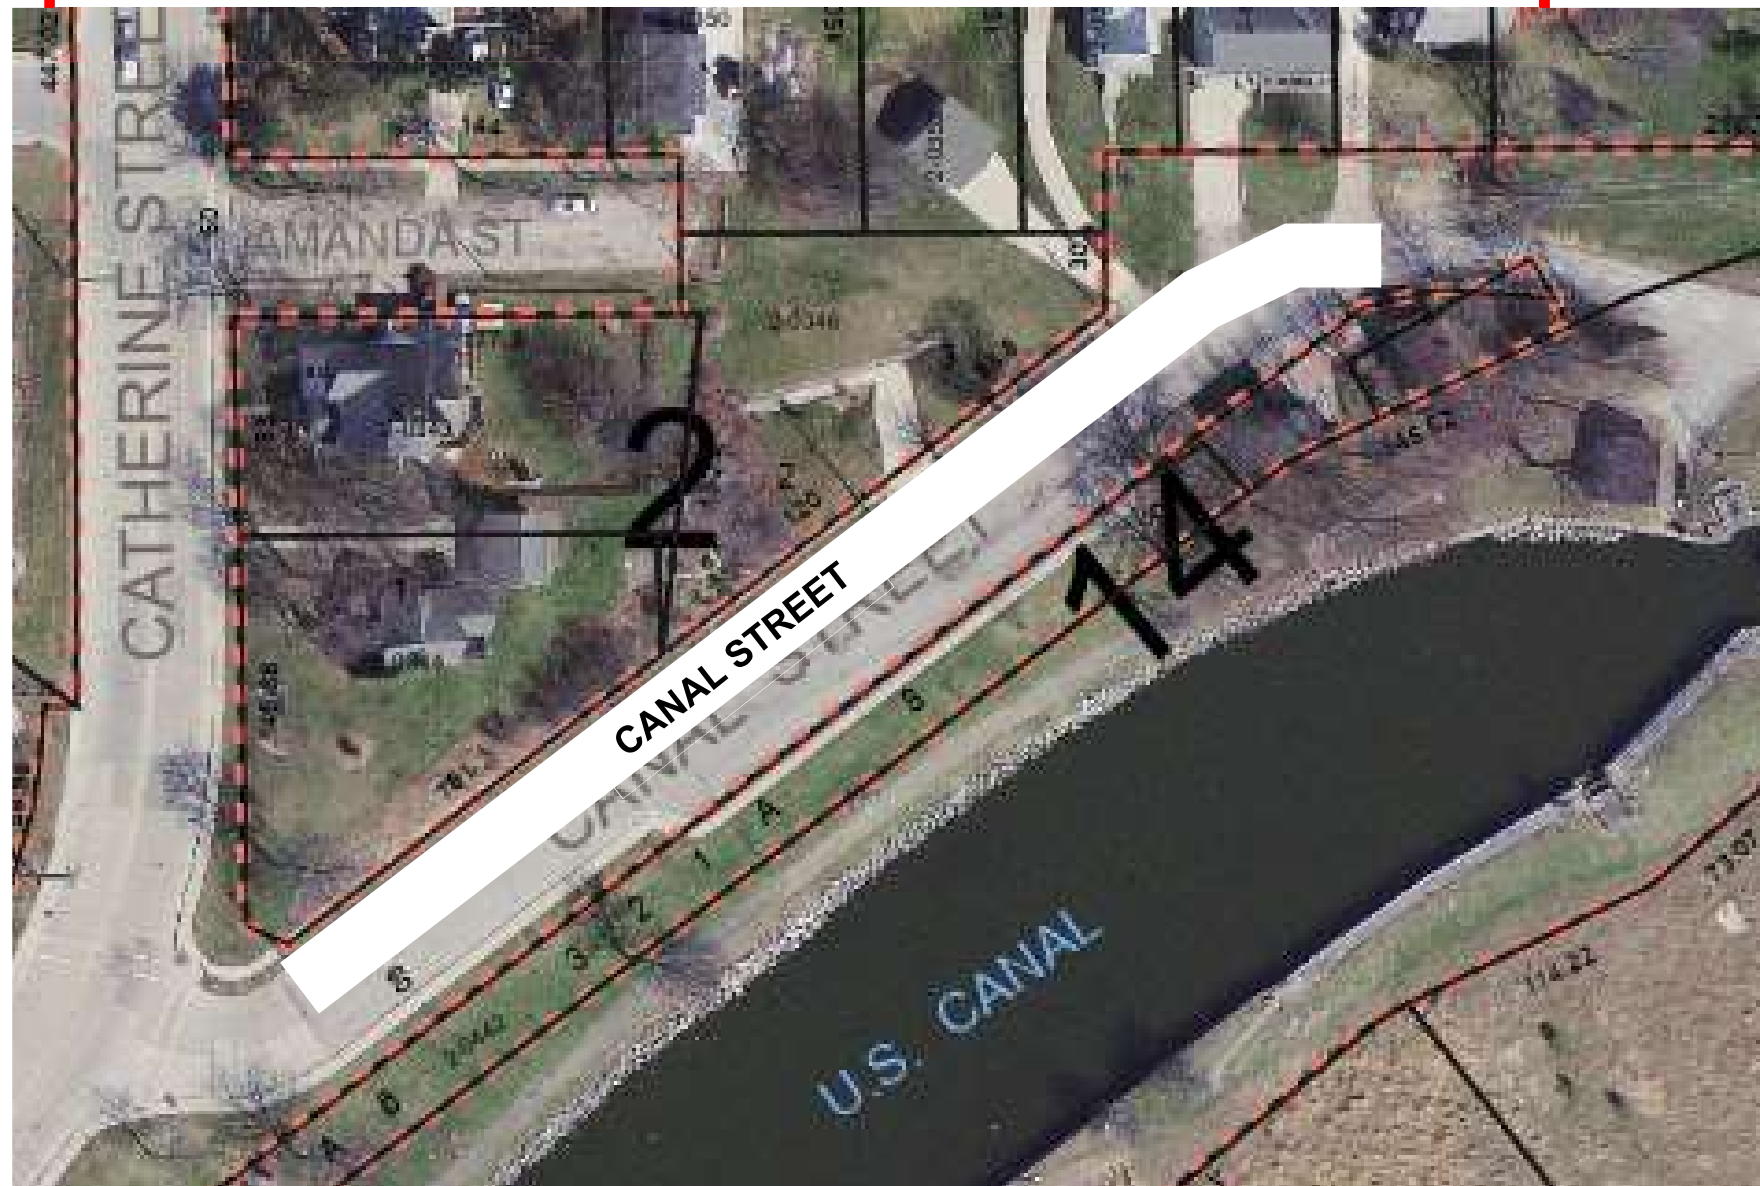

\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

## NOTES:

- The sewer contractor is planning to start the storm sewer work the week of July 17th
- The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of August 21th. The contractor has moved dates back due to their scheduling issues. When the paving contractor has a set updated schedule, I will send out another update.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at [jbodoh@kaukauna-wi.org](mailto:jbodoh@kaukauna-wi.org) to be added to the weekly email update list.
