


PROJECT 1-23 METOXEN, DIXON, QUINNEY & SEVENTH

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 6/26 - 6/30

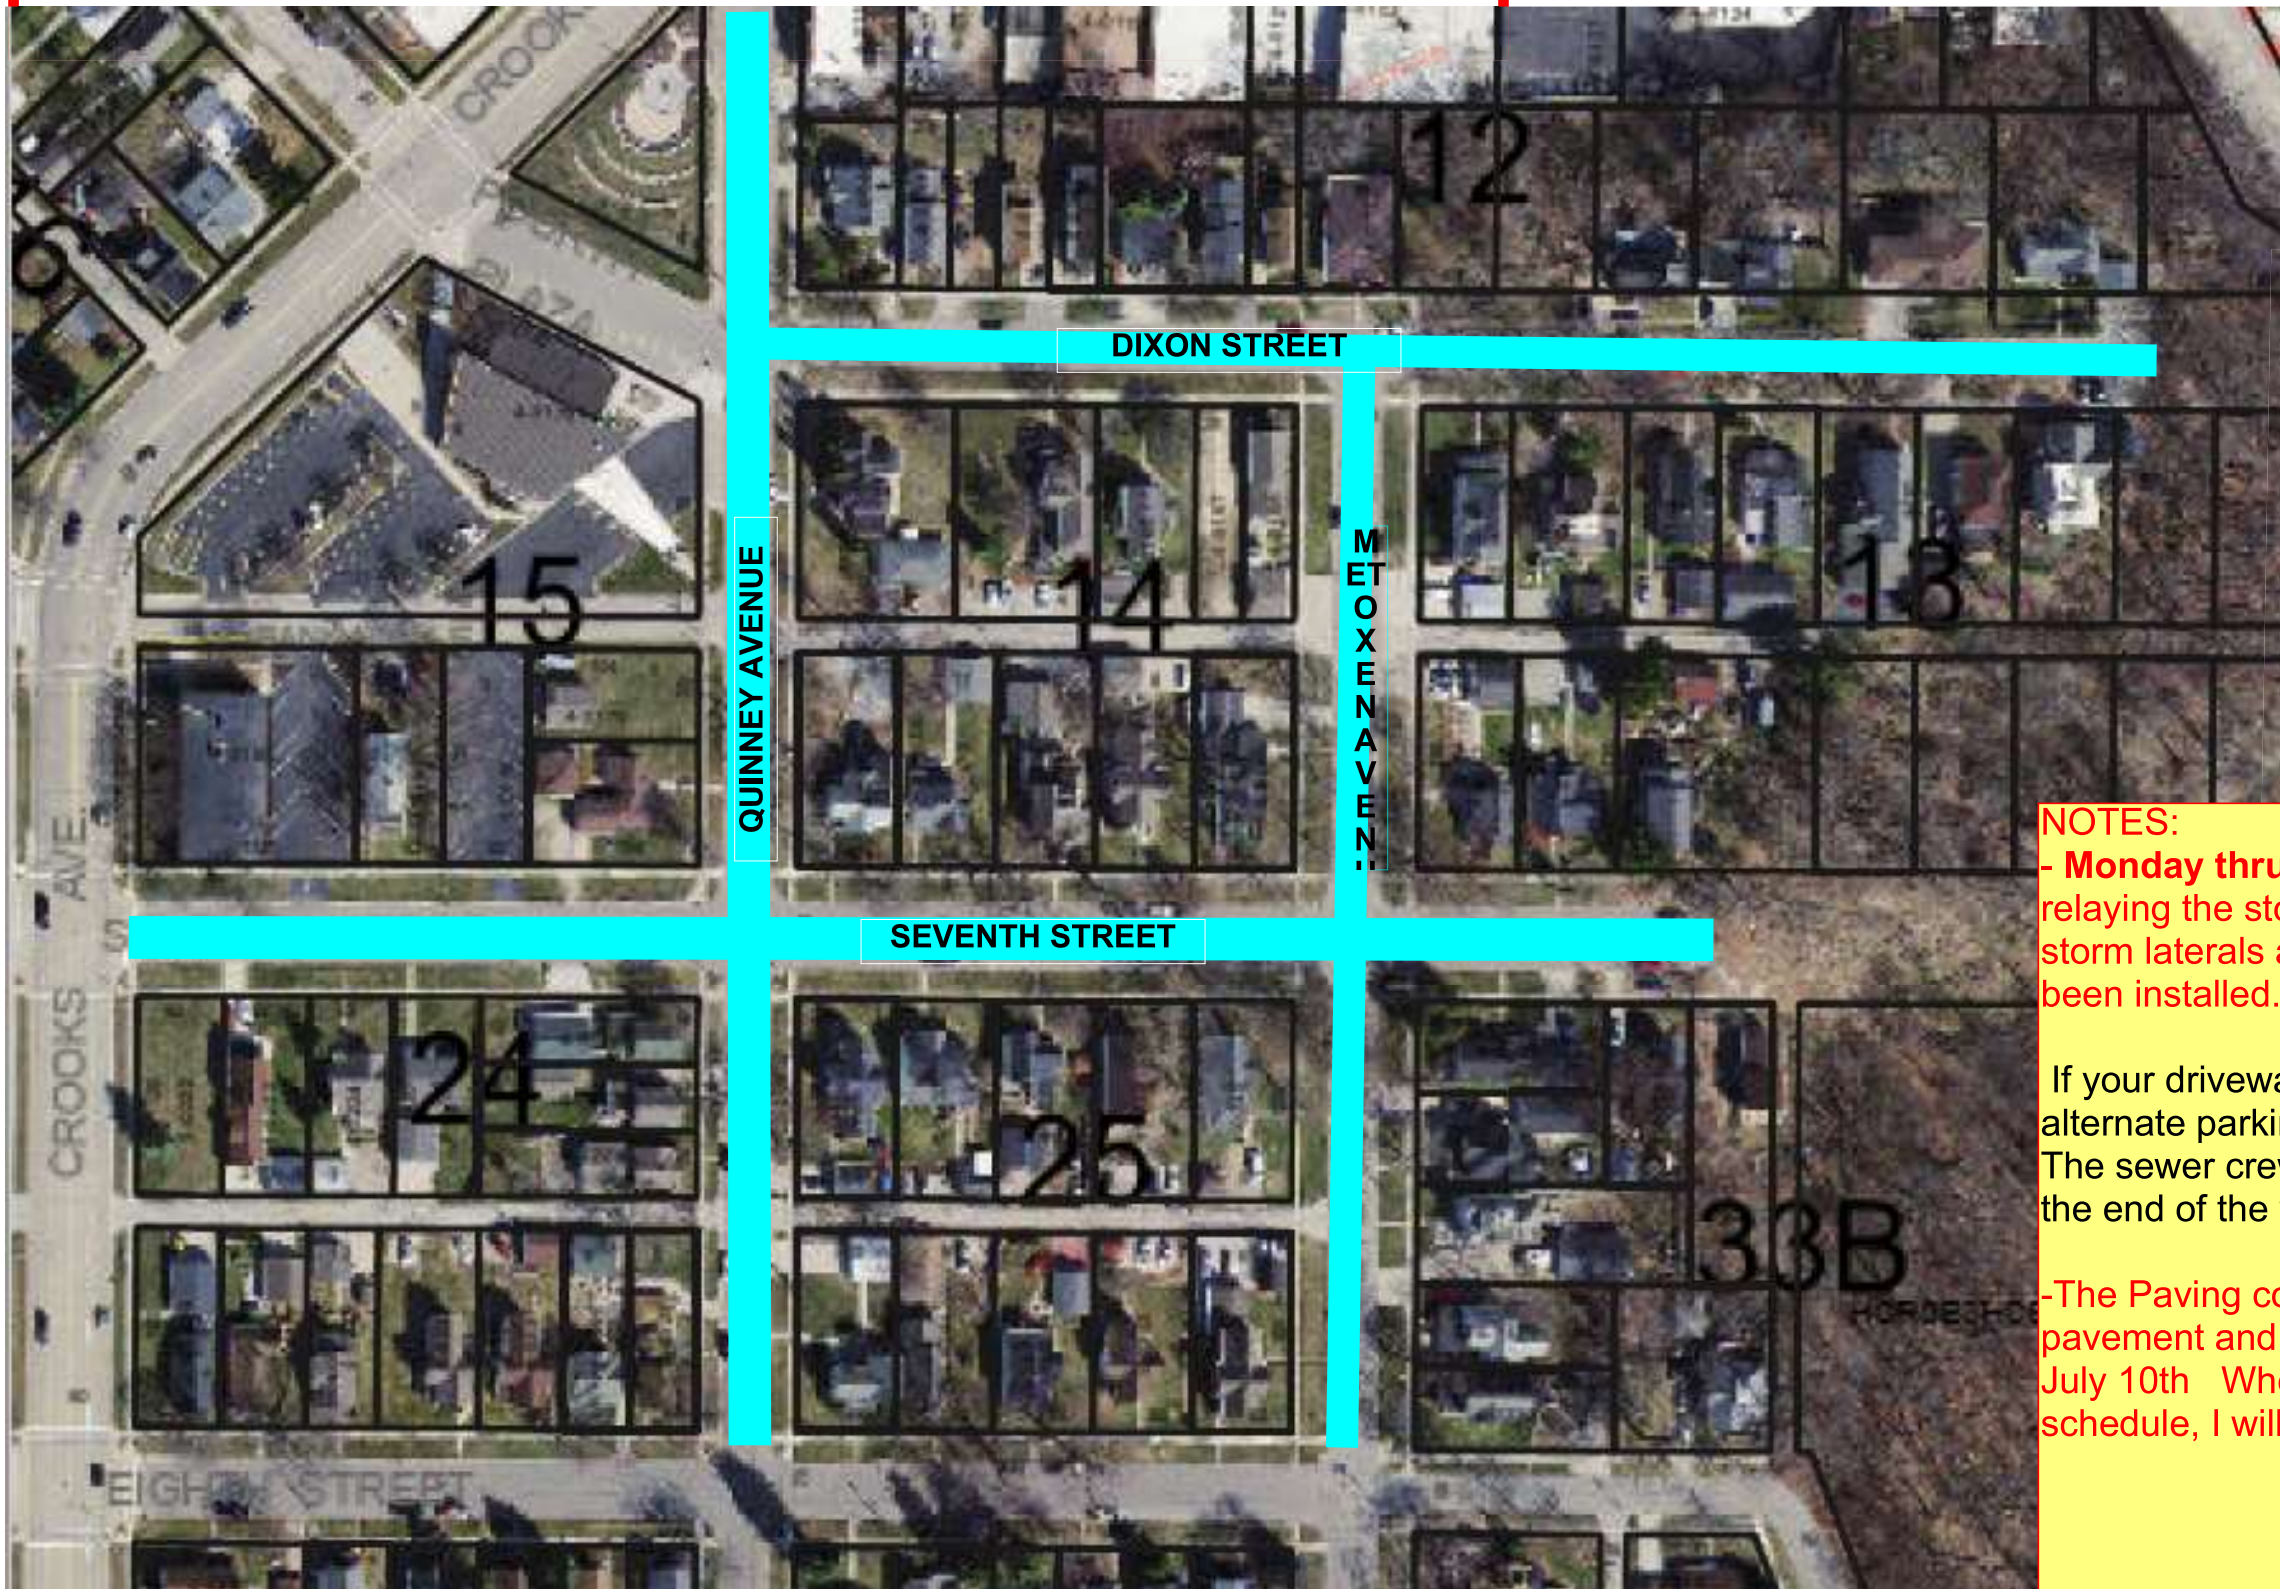

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDEWALK/DRIVEWAY WORK

NOTES:
- **Monday thru Friday** - The storm sewer contractor will continue relaying the storm sewer in Seventh Street. They will also install storm laterals along Seventh Street once the storm main has been installed.

If your driveway is along Seventh Street, you may need to find alternate parking while the sewer crew works in front of your lot. The sewer crew should have the driveways open for parking at the end of the work day.

-The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of July 10th. When the paving contractor sends an updated schedule, I will send out another update.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 WHITE DOVE, WHITE BIRCH, LODERBAUER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 6/26 - 6/30



*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

NOTES:

- The Paving contractor is planning to start removing existing pavement and excavating the existing stone base on Loderbauer Road on July 5th. The contractor will then place base stone and grade the stone.
- The contractor will grade White Dove and White Birch after the Loderbauer grading is done.
- When the paving contractor sends an updated schedule, I will send out another update.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 6/26- 6/30



*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

NOTES:

- The Paving contractor will start grading Greyhound Street and Boxer Street the week of July 5th.
- Paving should start shortly after the grading work is done. When the paving contractor sends an updated schedule, I will send out another update..

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 OAK & SCHULTHEIS

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 6/26 - 6/30



*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING


SIDEWALK/DRIVEWAY WORK

NOTES:

- The sewer contractor is planning to start the storm sewer work the week of July 10th
- The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of August 14th. When the paving contractor sends an updated schedule, I will send out another update.

PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 6/26 - 6/30

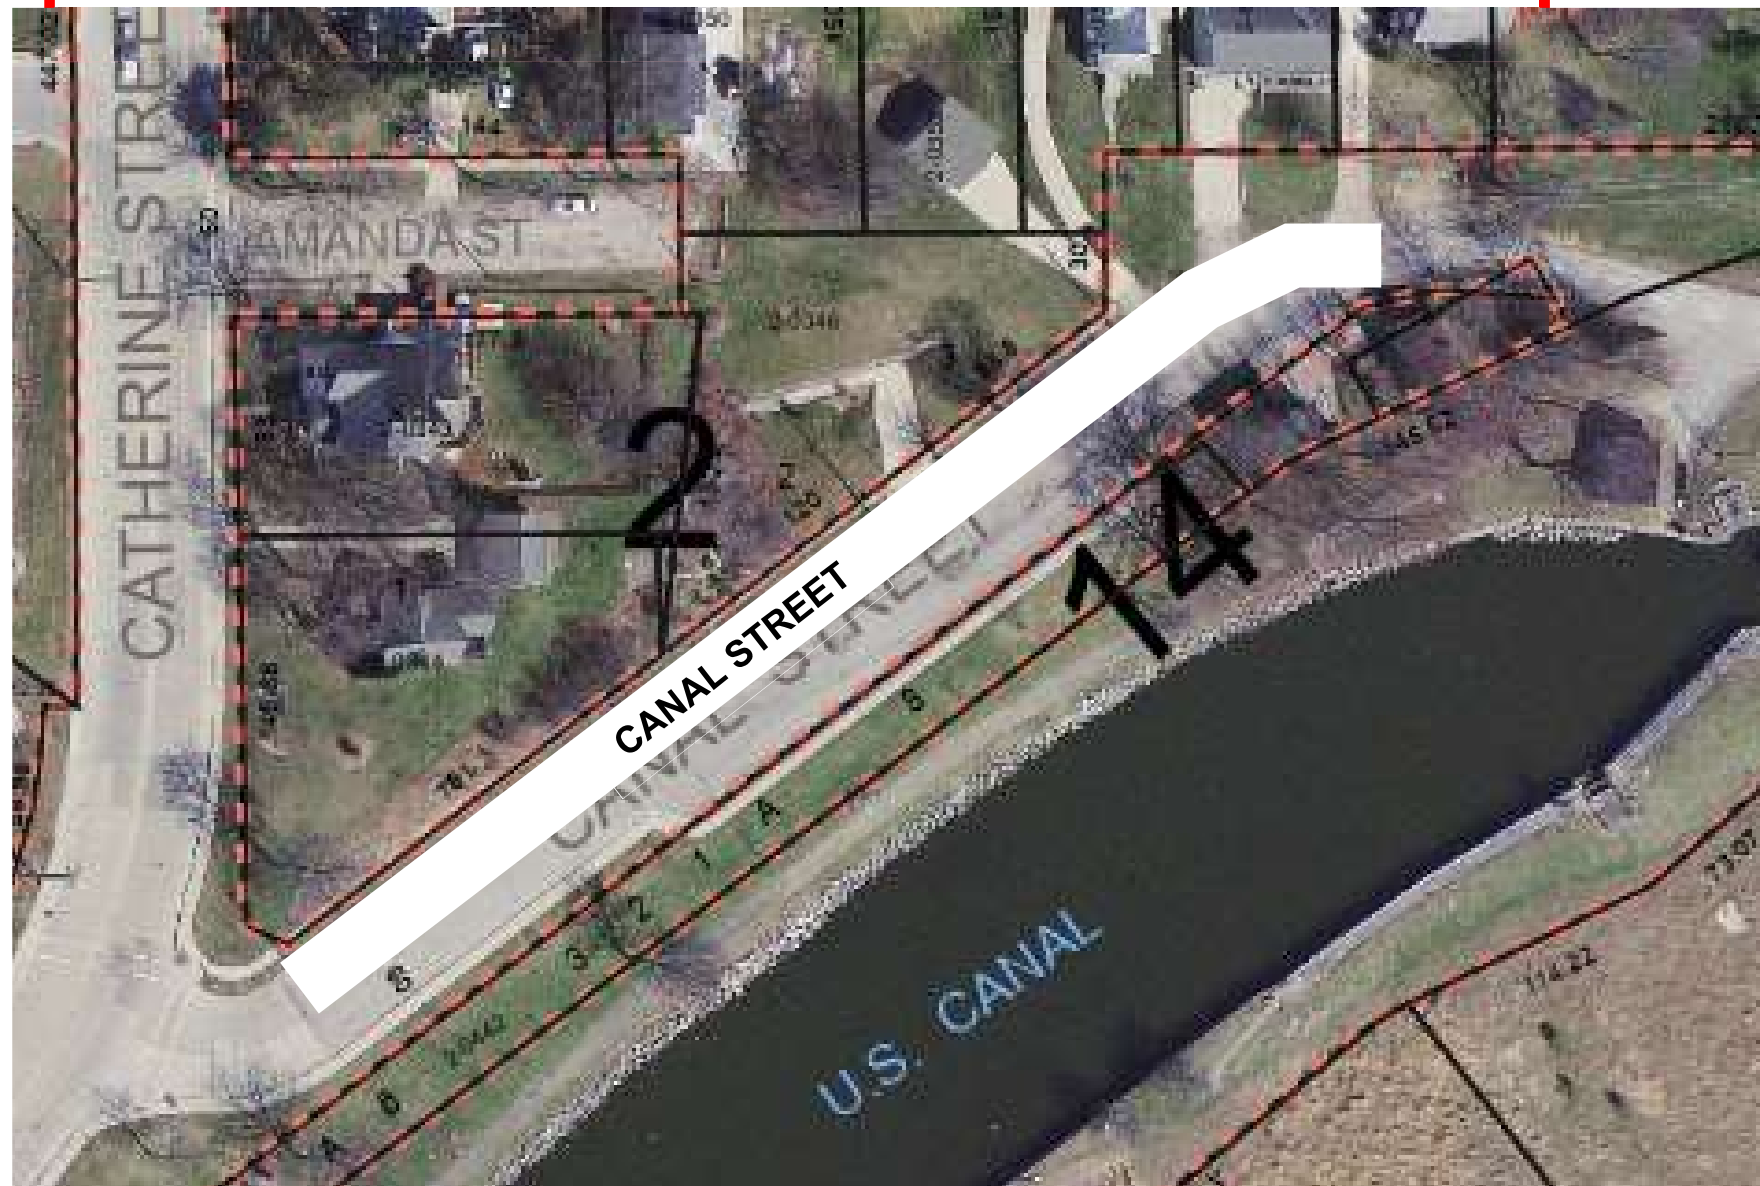

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

NOTES:

- The sewer contractor is planning to start the storm sewer work the week of July 17th
- The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of August 21th. When the paving contractor sends an updated schedule, I will send out another update.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.
