



PROJECT 1-23 METOXEN, DIXON, QUINNEY & SEVENTH

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 7/3 - 7/7 -UPDATE

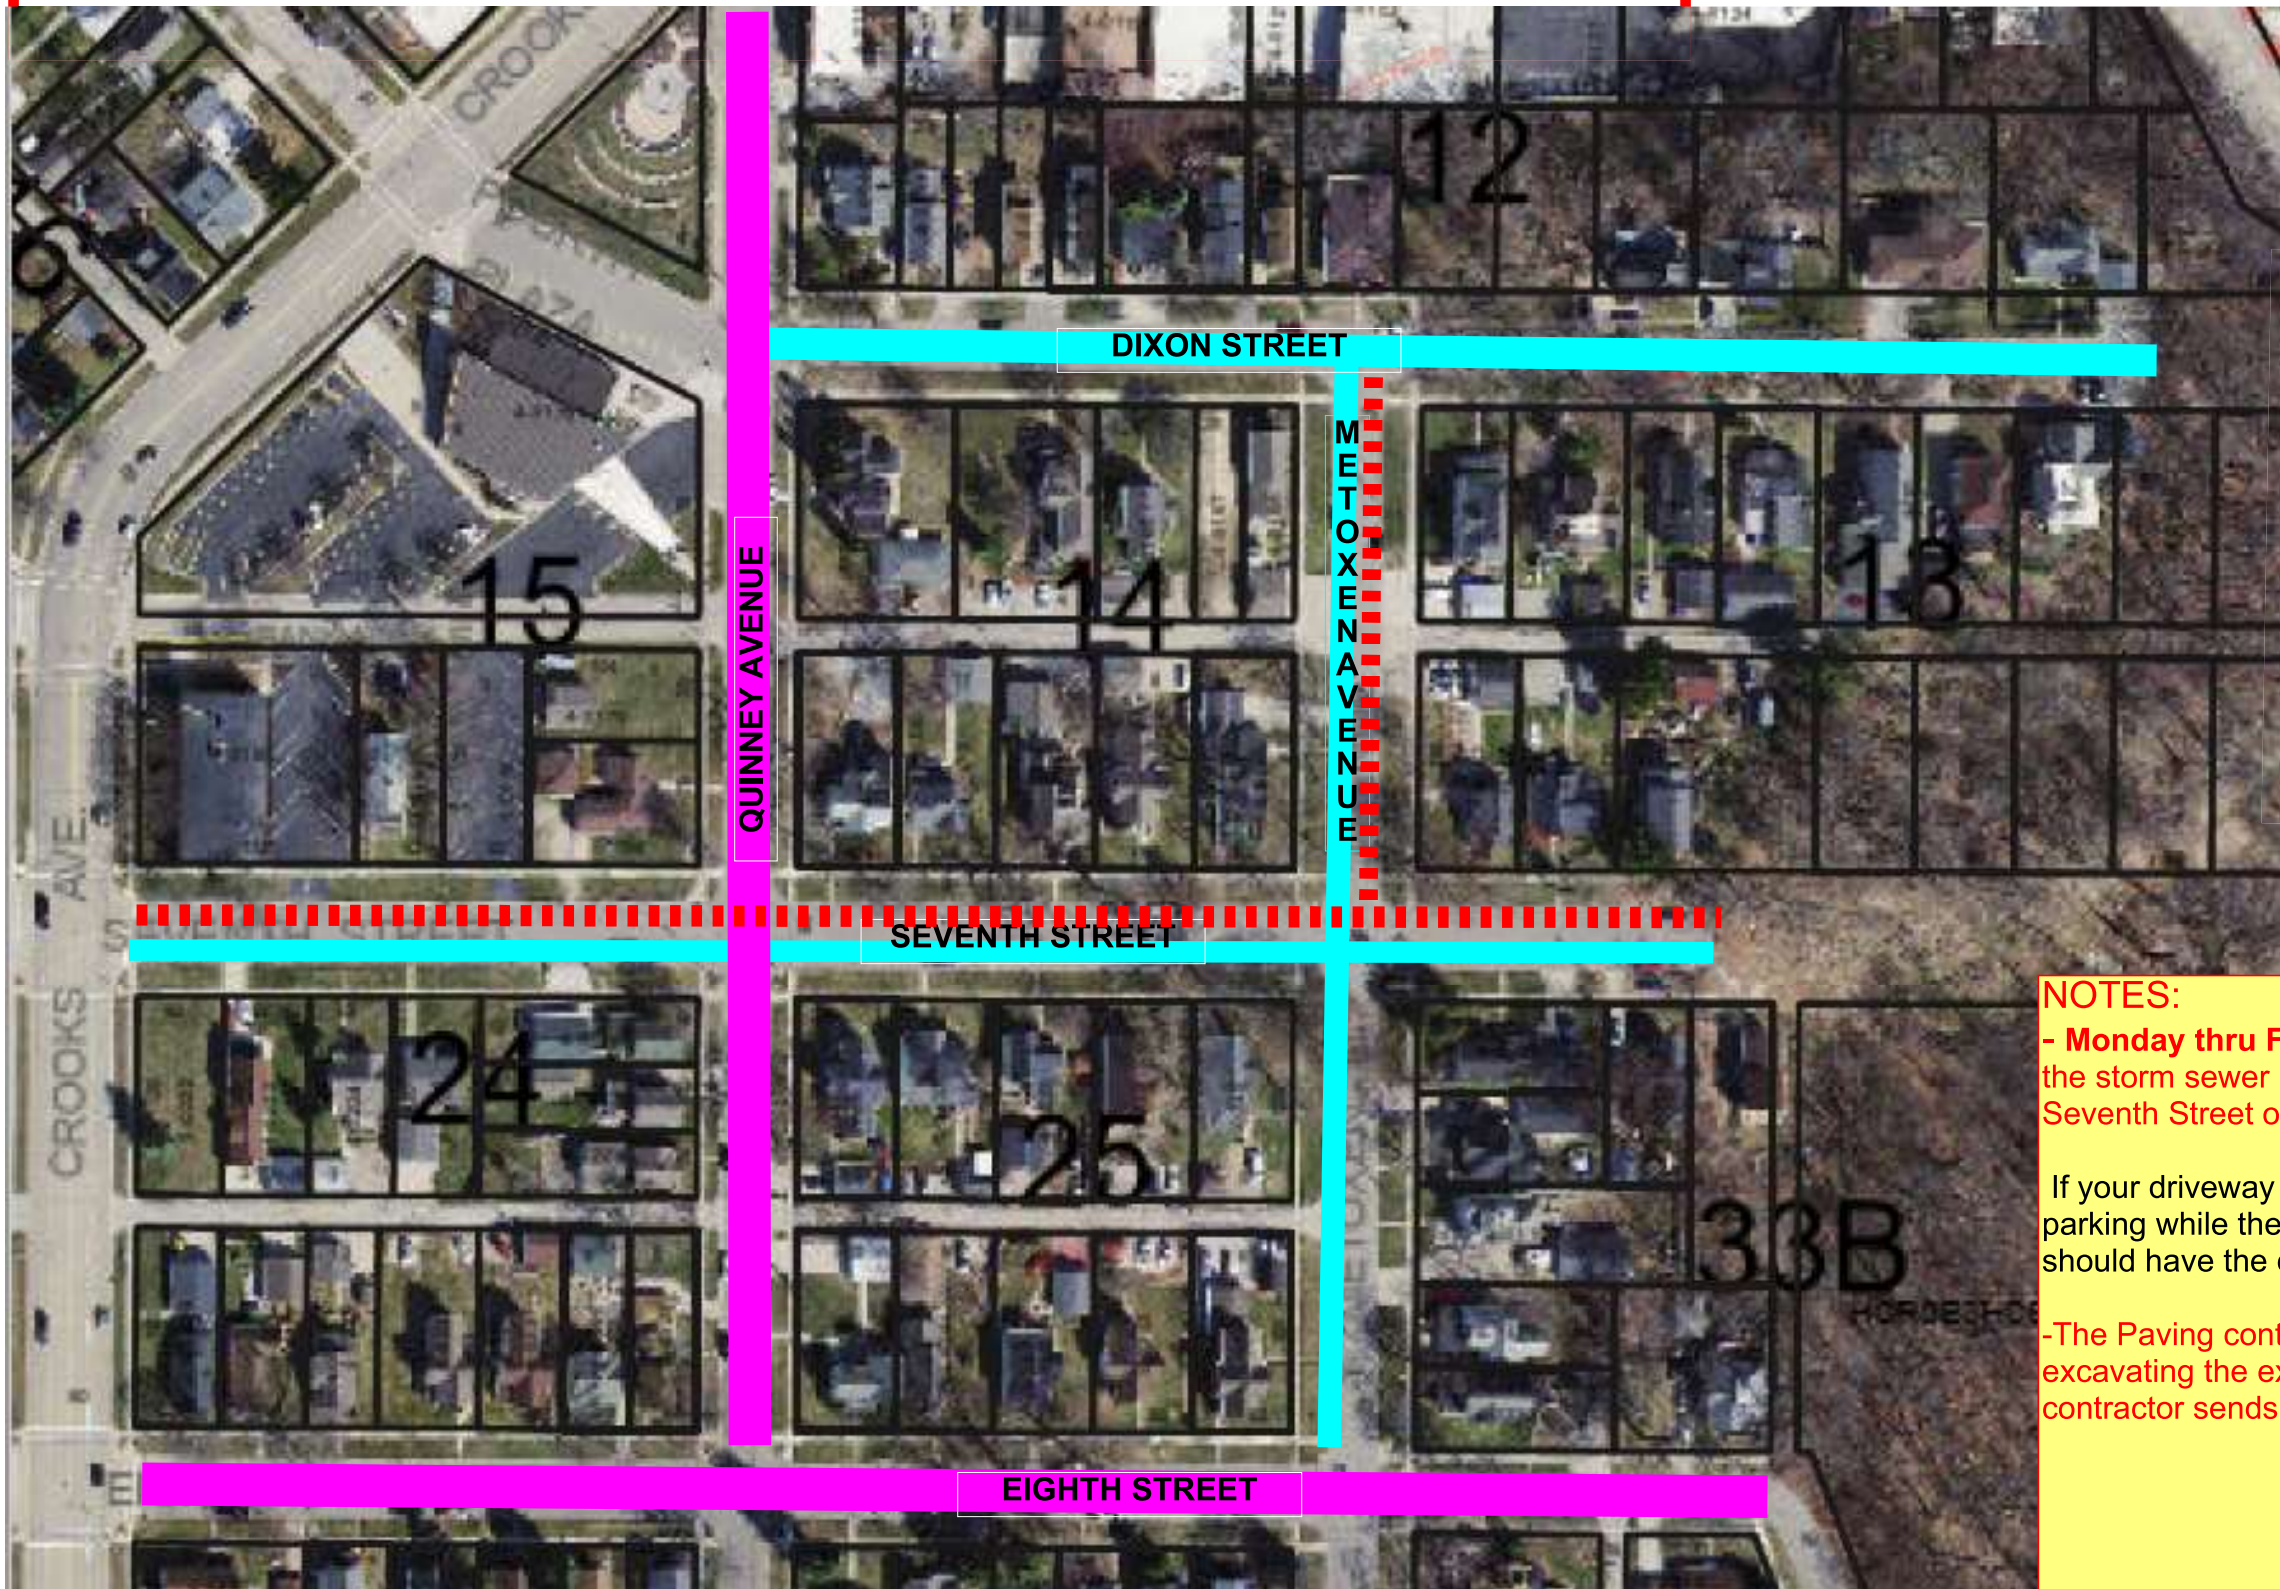

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDWALK/DRIVEWAY WORK
- RECOMMENDED PARKING
- NO PARKING = 
- TEMPORARY PARKING = 

NOTES:

- **Monday thru Friday** - The storm sewer contractor will continue relaying the storm sewer in Seventh Street. They will also install storm laterals along Seventh Street once the storm main has been installed.

If your driveway is along Seventh Street, you may need to find alternate parking while the sewer crew works in front of your lot. The sewer crew should have the driveways open for parking at the end of the work day.

-The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of July 17th. When the paving contractor sends an updated schedule, I will send out another update.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 WHITE DOVE, WHITE BIRCH, LODERBAUER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 7/3 - 7/7 -UPDATE



*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDEWALK/DRIVEWAY WORK
- RECOMMENDED PARKING
- NO PARKING = 
- TEMPORARY PARKING = 

- NOTES:**
- The Paving contractor is planning to start removing existing pavement and excavating the existing stone base on Loderbauer Road on July 5th. The contractor will then place base stone and grade the stone. This section of Loderbauer will be closed to traffic during this work.
 - The contractor will grade White Dove and White Birch starting June 29th. They will be setting iron stakes and a string line and then grade one side of the street. While the contractor is grading you will not be able to drive on White Birch or White Dove. In the evenings when they are not working they will provide access to the driveways.
 - Paving may take place the end of the second week of July or early the third week of July. You will not be able to drive on the new concrete for 7 days while it is curing and strengthening.
 - When the paving contractor sends an updated schedule, I will send out another update.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 7/3 - 7/7 - UPDATE



*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

RECOMMENDED PARKING

NO PARKING = 
TEMPORARY PARKING = 

NOTES:

-The Paving contractor started grading Greyhound Street, Boxer Street and Setter Drive on June 28th. They set iron stakes and a string line and then grade one side of the street. While the contractor is grading you will not be able to drive these roads. In the evening when they are not working, the contract should provide access to the driveways by dropping the string.

-Paving should start either later next week or early the week after next. You will not be able to drive on the new concrete for 7 days while it is curing and strengthening.

When the paving contractor sends an updated schedule, I will send out another update..

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

