


# PROJECT 1-23 METOXEN, DIXON, QUINNEY & SEVENTH

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 7/17 - 7/21 -UPDATE

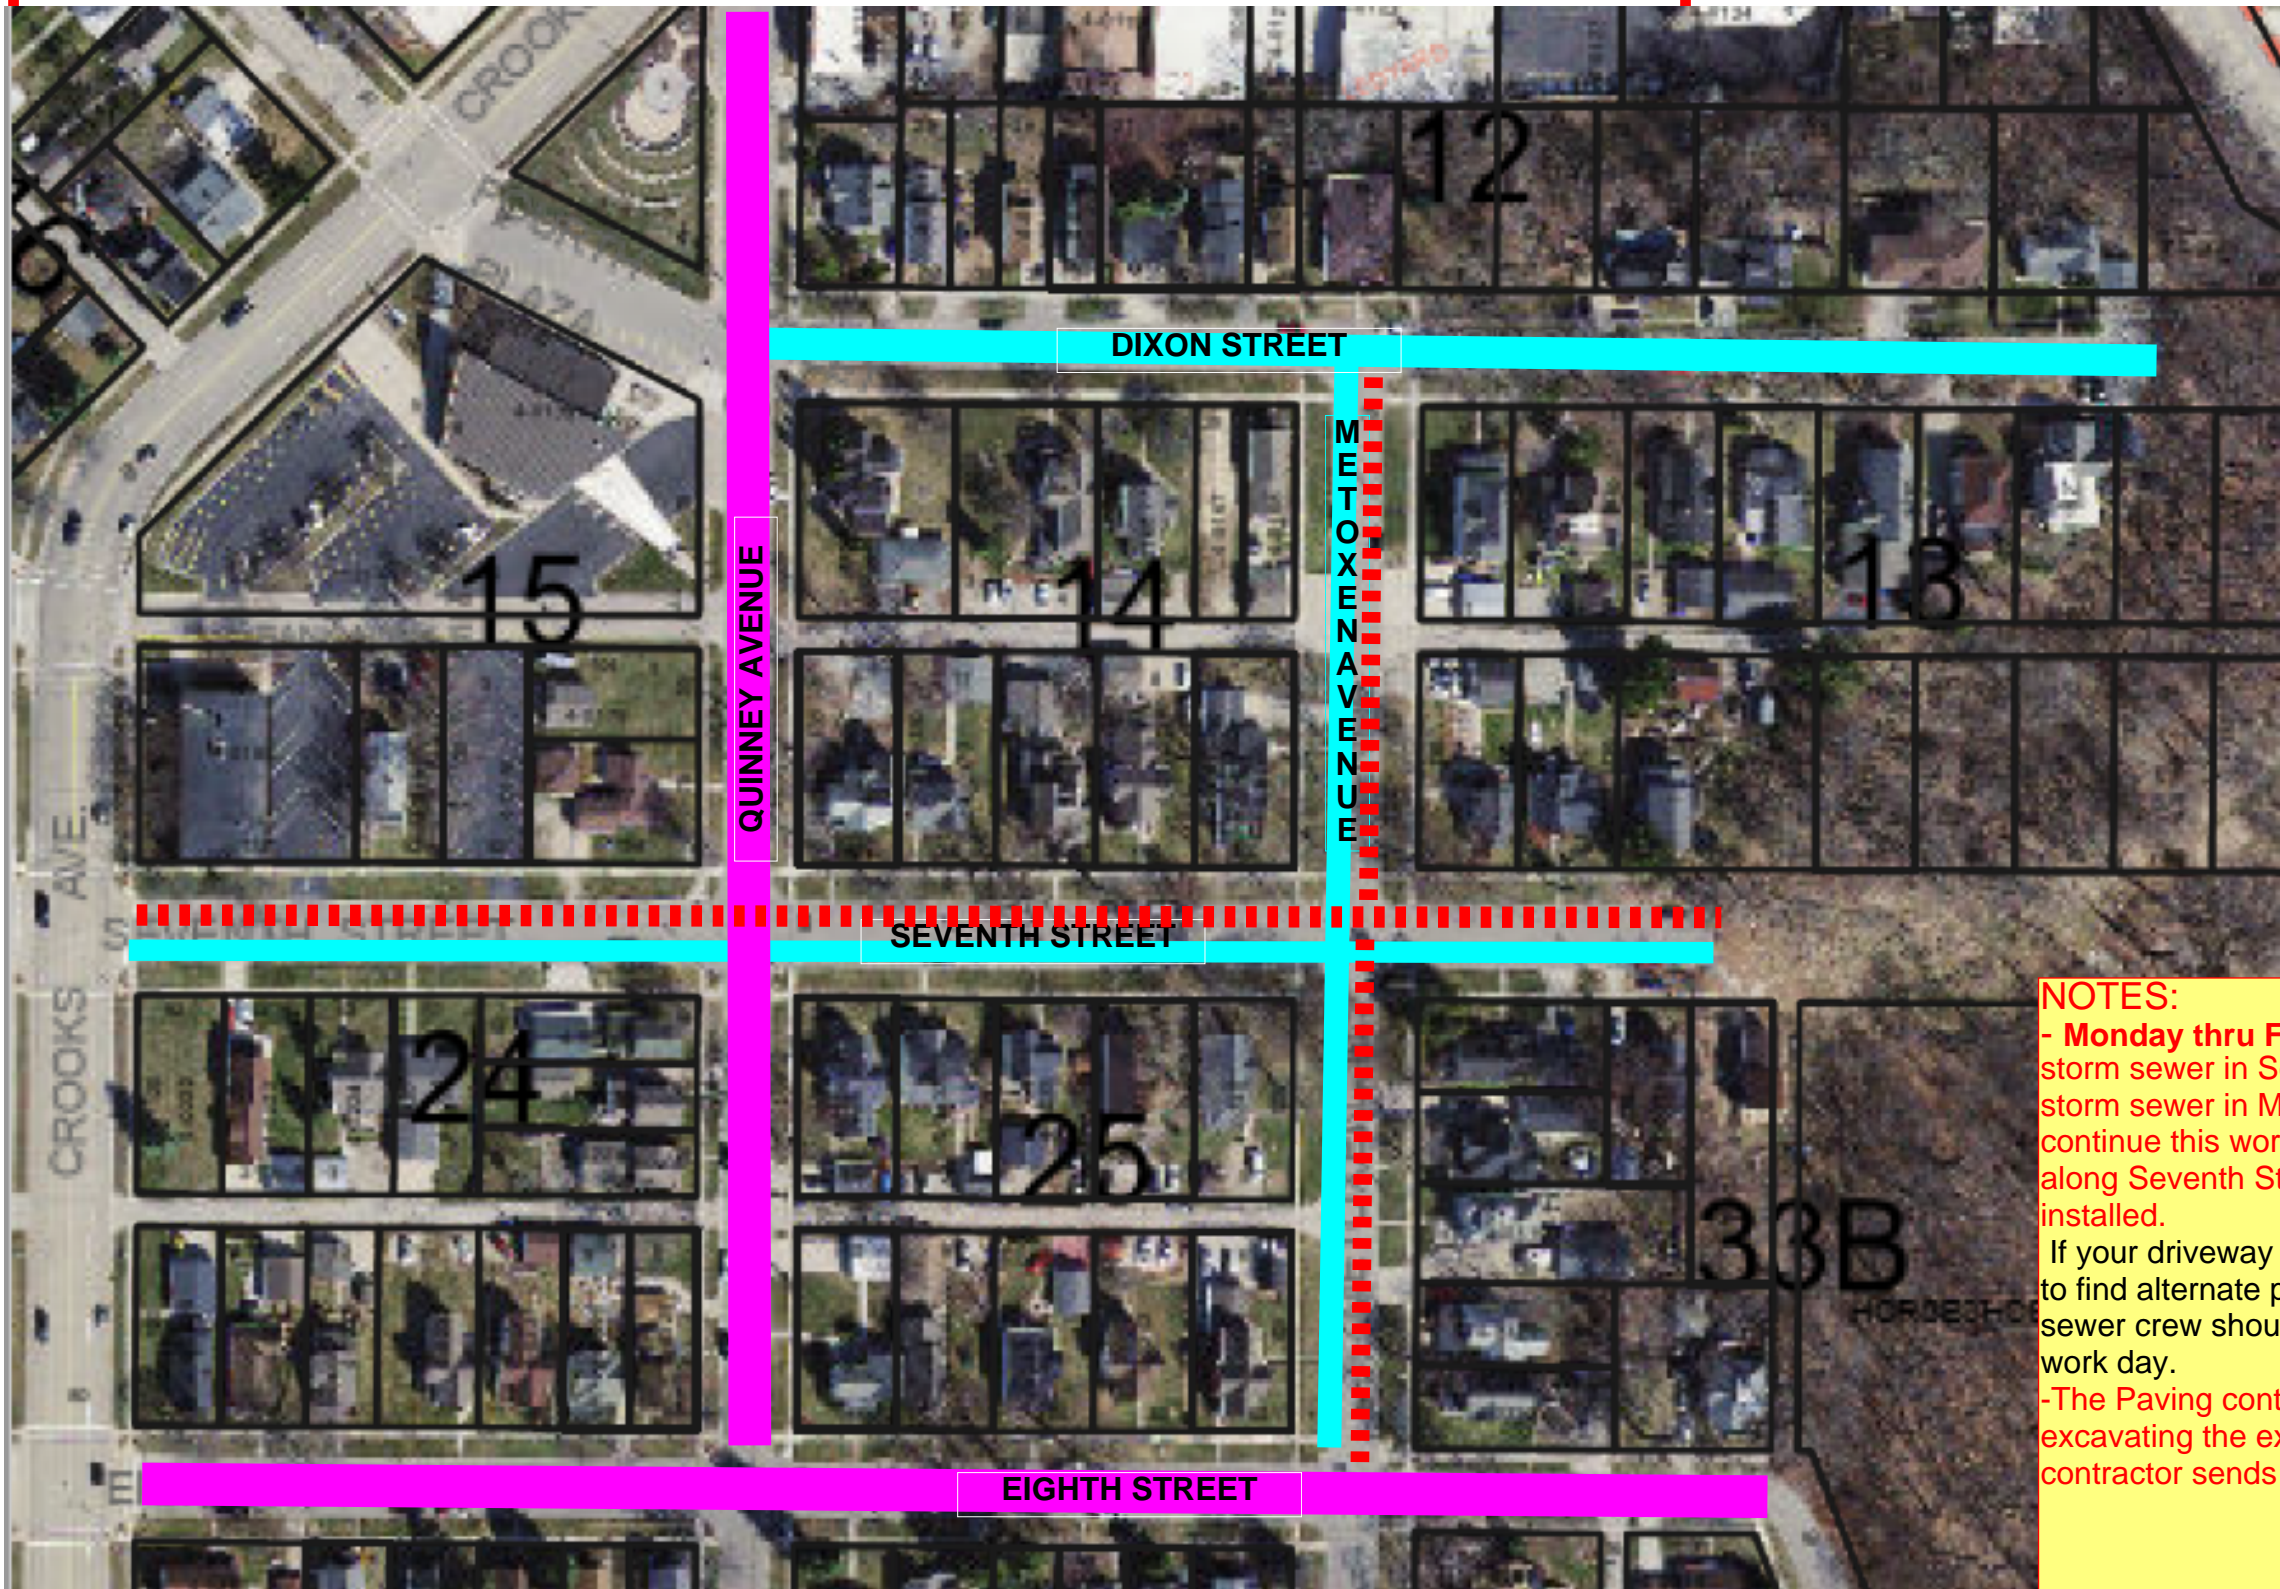

\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDEWALK/DRIVEWAY WORK
- RECOMMENDED PARKING
- NO PARKING = [Red dashed line]
- TEMPORARY PARKING = [Magenta bar]

**NOTES:**  
 - **Monday thru Friday** - The storm sewer contractor is finishing relaying the storm sewer in Seventh Street. The contractor has started work on the storm sewer in Metoxen Avenue going north from Seventh Street, they will continue this work week of July 17th. They will also install storm laterals along Seventh Street and Metoxen Avenue once the storm main has been installed.  
 If your driveway is along Seventh Street or Metoxen Avenue, you may need to find alternate parking while the sewer crew works in front of your lot. The sewer crew should have the driveways open for parking at the end of the work day.  
 -The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of July 24th When the paving contractor sends an updated schedule, I will send out another update.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at [jbodoh@kaukauna-wi.org](mailto:jbodoh@kaukauna-wi.org) to be added to the weekly email update list.



# PROJECT 1-23 WHITE DOVE, WHITE BIRCH, LODERBAUER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 7/17 - 7/21 -UPDATE



\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDEWALK/DRIVEWAY WORK
- RECOMMENDED PARKING
- NO PARKING = [Red dashed line]
- TEMPORARY PARKING = [Pink bar]

**NOTES:**


- The Paving contractor is planning to start removing existing pavement and excavating the existing stone base on Loderbauer Road the week of July 17th. The contractor will then place base stone and grade the stone. This section of Loderbauer will be closed to traffic during this work. The Loderbauer paving will take place after the stone has been placed and graded.
- The contractor is looking to pave the second lane of White Dove and White Birch early the week of July 17th, weather pending. While the contractor is paving you will not be able to drive on White Birch or White Dove. You will not be able to drive on the new concrete for 7 days while it is curing and strengthening.
- The first paved lanes of White dove and White Birch are open for traffic. The contractor will place gravel in each driveway so you can get out.
- When the paving contractor sends an updated schedule, I will send out another update.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at [jbodoh@kaukauna-wi.org](mailto:jbodoh@kaukauna-wi.org) to be added to the weekly email update list.



# PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 7/17 - 7/21 - UPDATE

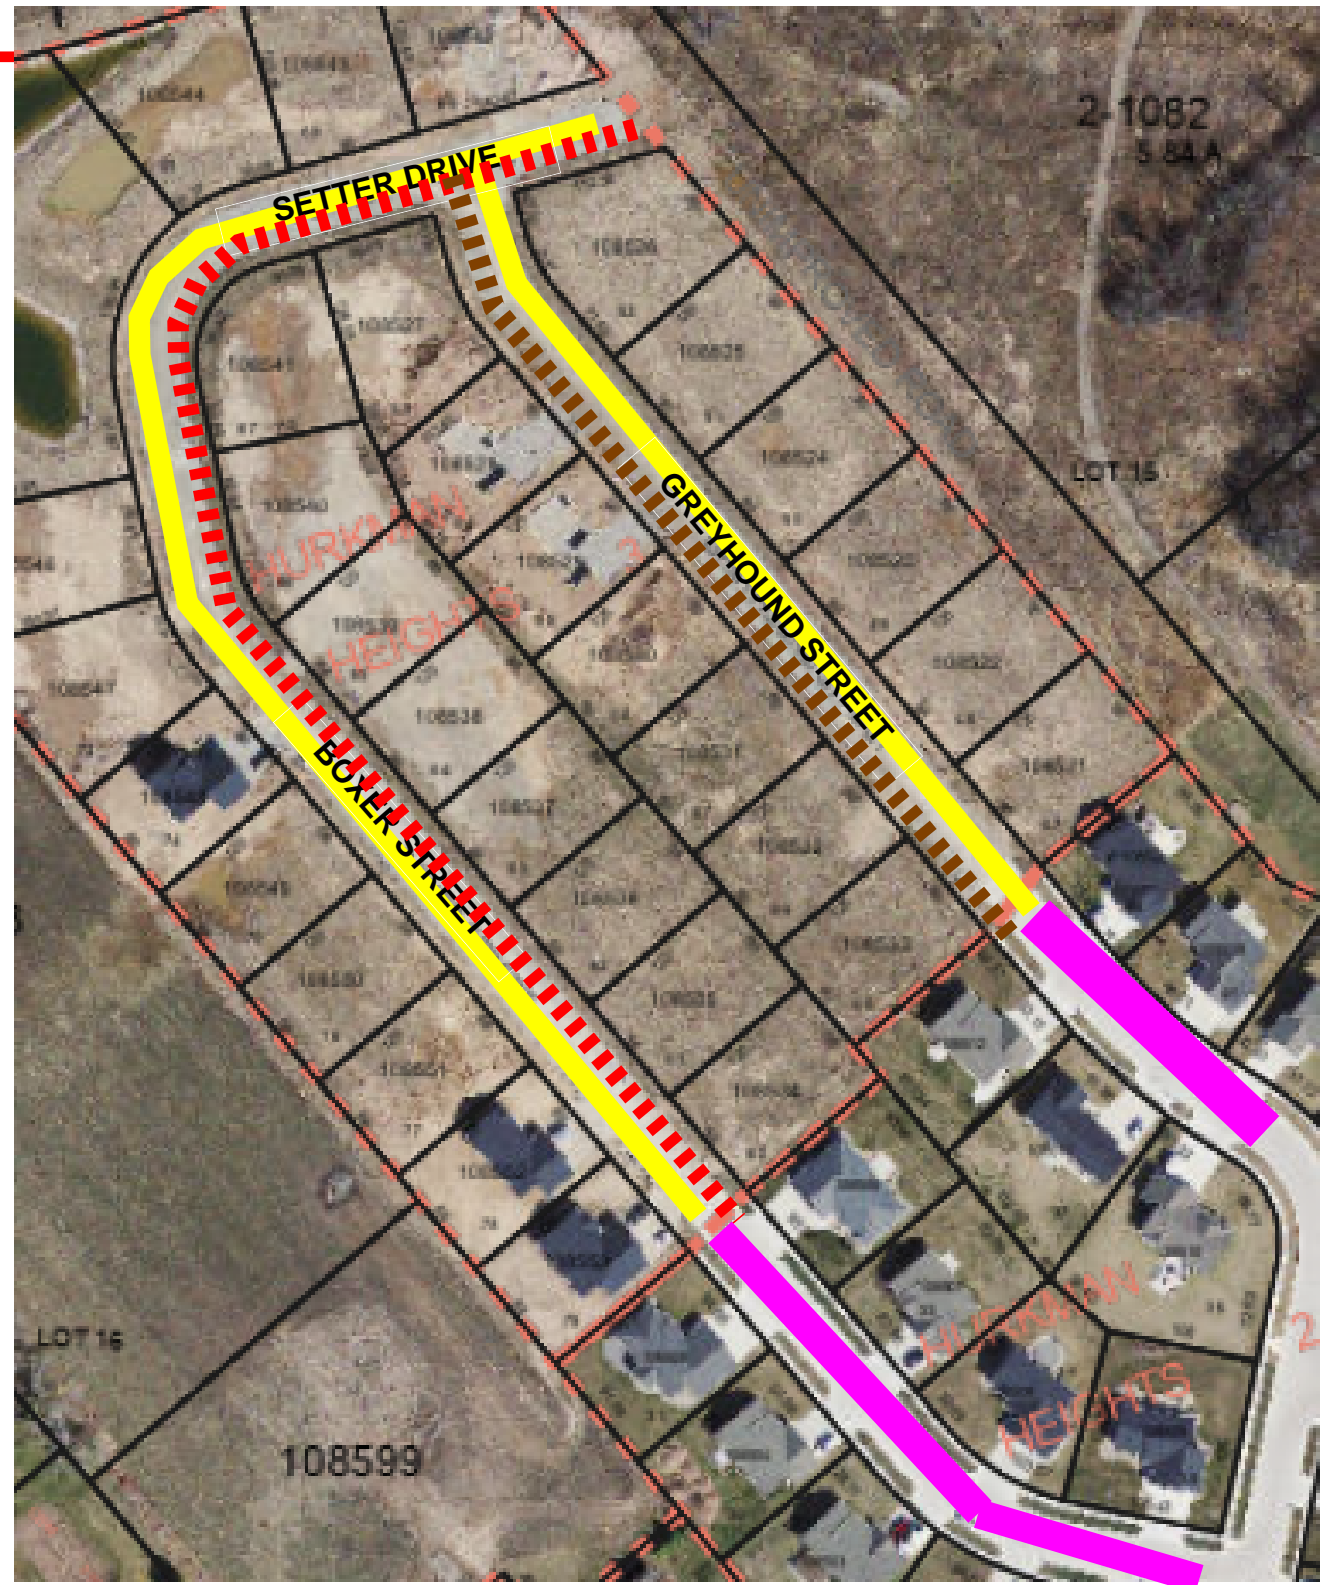

\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

RECOMMENDED PARKING

NO PARKING =   
TEMPORARY PARKING = 

## NOTES:

- The first lane of concrete pavement was open to traffic on July 12th.
  - The contractor will pave the second lane early the week of July 17th, weather pending. You will not be able to drive on the new concrete for 7 days while it is curing and strengthening.
  - After the second lane has cured and strengthened (about 7 days), the concrete contractor will start working on constructing the sidewalks and driveway aprons.
- When the paving contractor sends an updated schedule, I will send out another update..

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at [jbodoh@kaukauna-wi.org](mailto:jbodoh@kaukauna-wi.org) to be added to the weekly email update list.

# PROJECT 1-23 OAK & SCHULTHEIS

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 7/17 - 7/21



\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

RECOMMENDED PARKING

NO PARKING = 

TEMPORARY PARKING = 

## NOTES:


- The sewer contractor is planning to start the storm sewer work the week of July 24th.

-The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of August 14th. When the paving contractor sends an updated schedule, I will send out another update.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at [jbodoh@kaukauna-wi.org](mailto:jbodoh@kaukauna-wi.org) to be added to the weekly email update list.

# PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 7/17 - 7/21

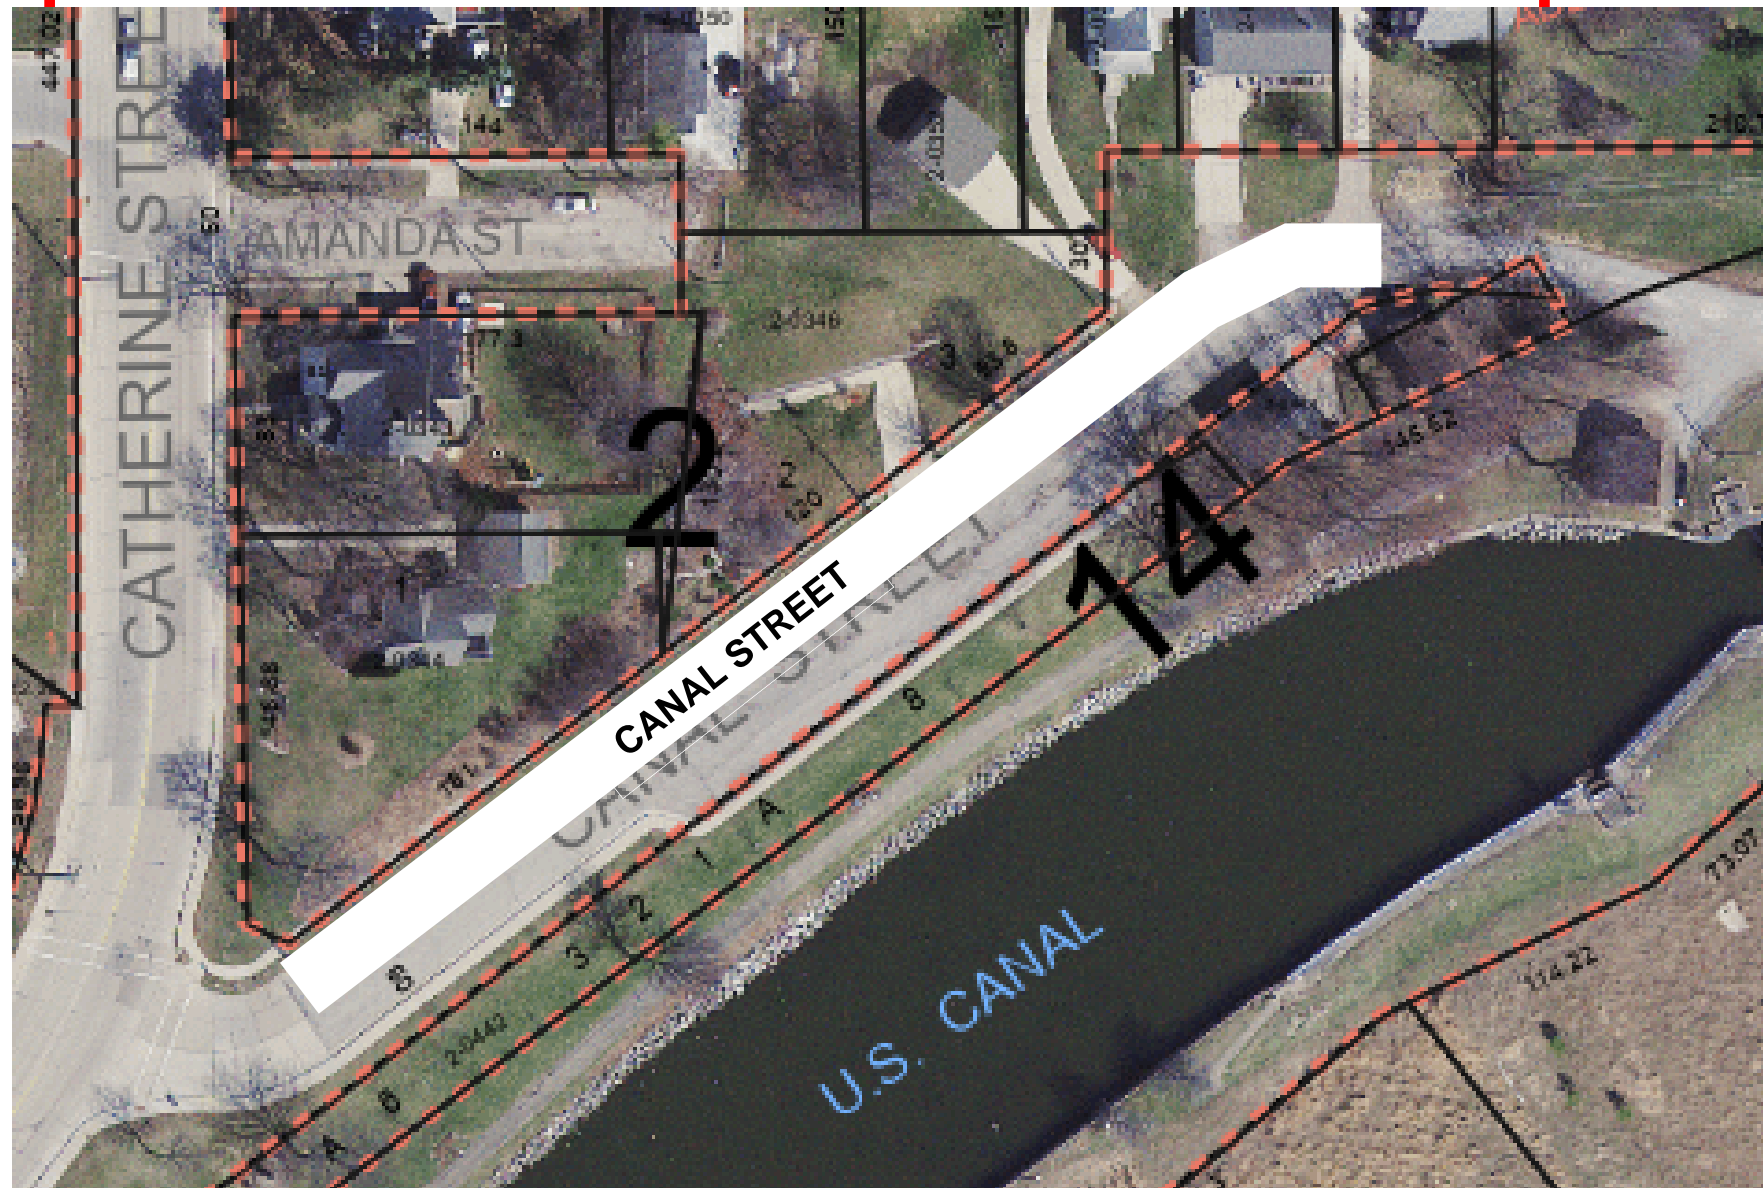

\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
  - STORM SEWER WORK
  - PAVMENT REMOVALS
  - GRADING
  - CONCRETE PAVING
  - SIDEWALK/DRIVEWAY WORK
  - RECOMMENDED PARKING
- NO PARKING = 
- TEMPORARY PARKING = 

## NOTES:

- The sewer contractor is planning to start the storm sewer work the week of July 31st
- The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of August 21th. When the paving contractor sends an updated schedule, I will send out another update.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at [jbodoh@kaukauna-wi.org](mailto:jbodoh@kaukauna-wi.org) to be added to the weekly email update list.
