


PROJECT 1-23 METOXEN, DIXON, QUINNEY & SEVENTH

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 7/24 - 7/28 -UPDATE

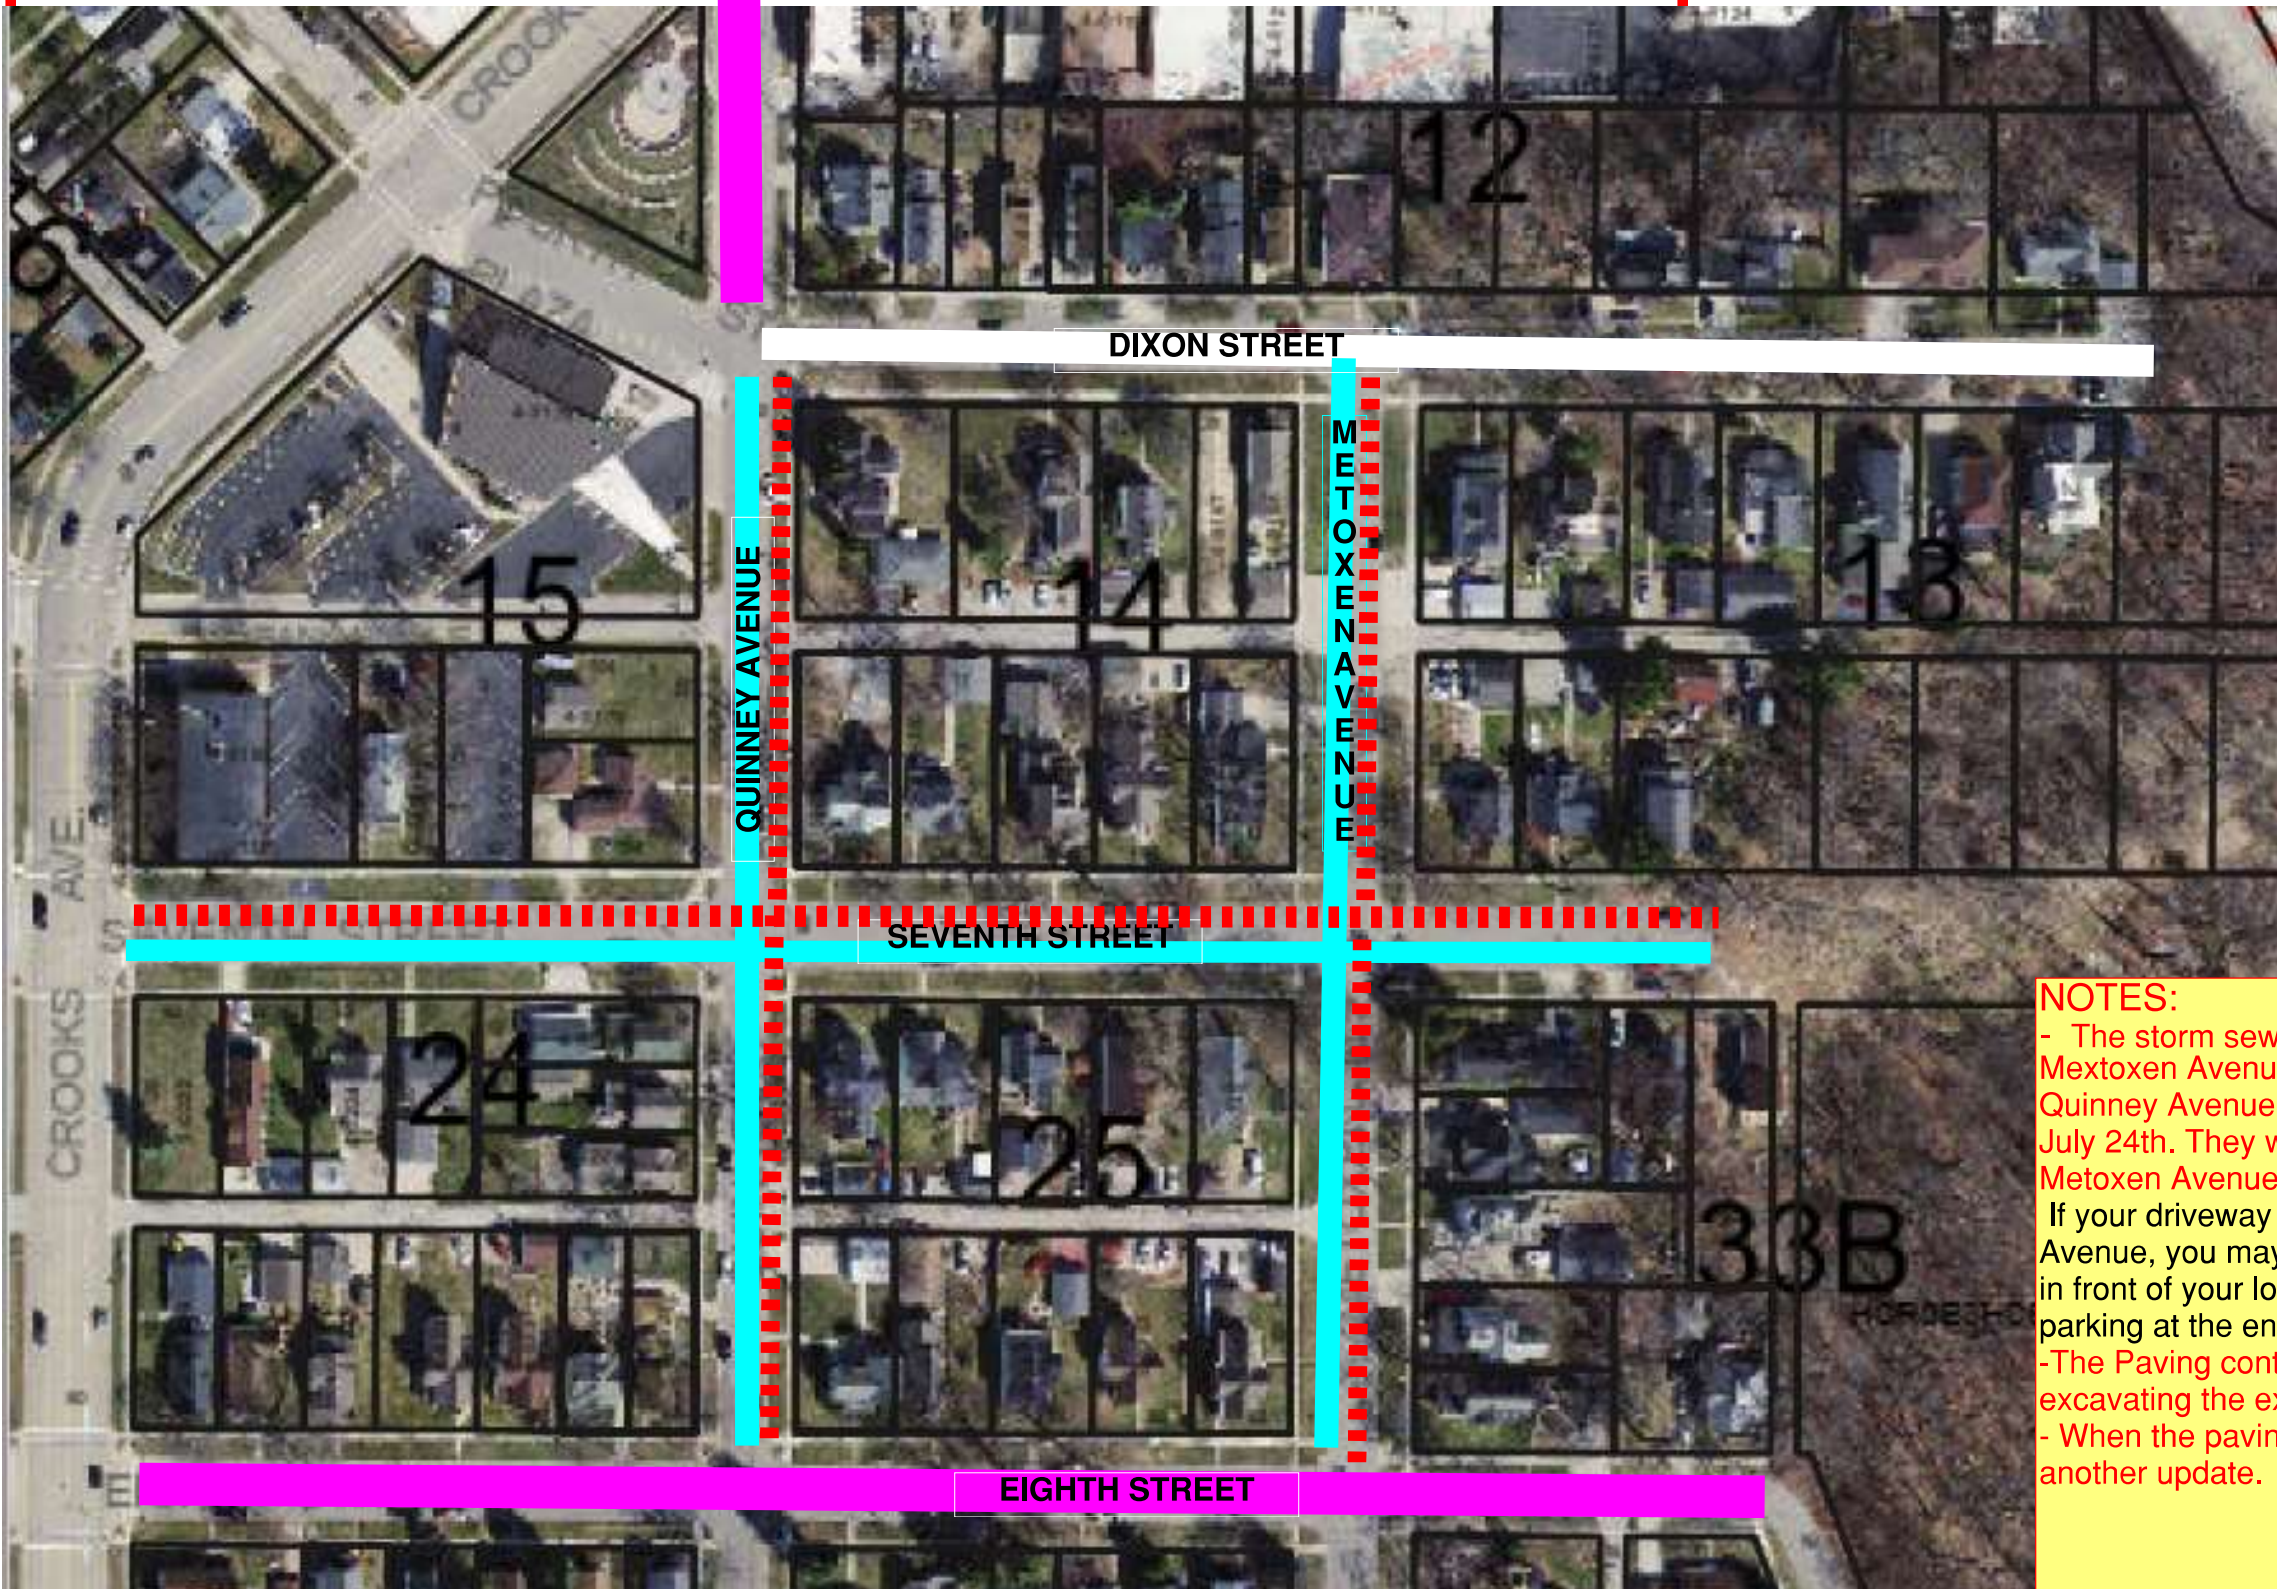

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDEWALK/DRIVEWAY WORK
- RECOMMENDED PARKING
- NO PARKING = [Red dashed line]
- TEMPORARY PARKING = [Magenta bar]

NOTES:

- The storm sewer contractor is finishing relaying the storm sewer along Mextoxen Avenue. The contractor will start work on the storm sewer in Quinney Avenue going north and south from Seventh Street the week of July 24th. They will also install storm laterals along Seventh Street and Metoxen Avenue once the storm main has been installed.
- If your driveway is along Seventh Street , Quinney Avenue or Metoxen Avenue, you may need to find alternate parking while the sewer crew works in front of your lot. The sewer crew should have the driveways open for parking at the end of the work day.
- The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of July 31st.
- When the paving contractor sends an updated schedule, I will send out another update.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 WHITE DOVE, WHITE BIRCH, LODERBAUER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 7/24 - 7/28 -UPDATE



*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDEWALK/DRIVEWAY WORK
- RECOMMENDED PARKING
- NO PARKING = [Red dashed line]
- TEMPORARY PARKING = [Pink bar]


NOTES:

- The week of July 31st, the sidewalk contractor will be working on backfilling behind the curb and constructing the sidewalk and driveway aprons.
- You will not be able to get into your driveway for 7 days after the sidewalk contractor constructs your driveway apron and the sidewalk that goes across your driveway. You can continue to park at the northern portion of White Birch and Red Fox Lane(see map to left.) while your driveway apron and sidewalk cure and harden.
- Shortly after the sidewalk and driveway aprons are complete, the landscaper should start the landscape work.
- When the paving contractor sends an updated schedule, I will send out another update.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 7/24 - 7/28 - UPDATE

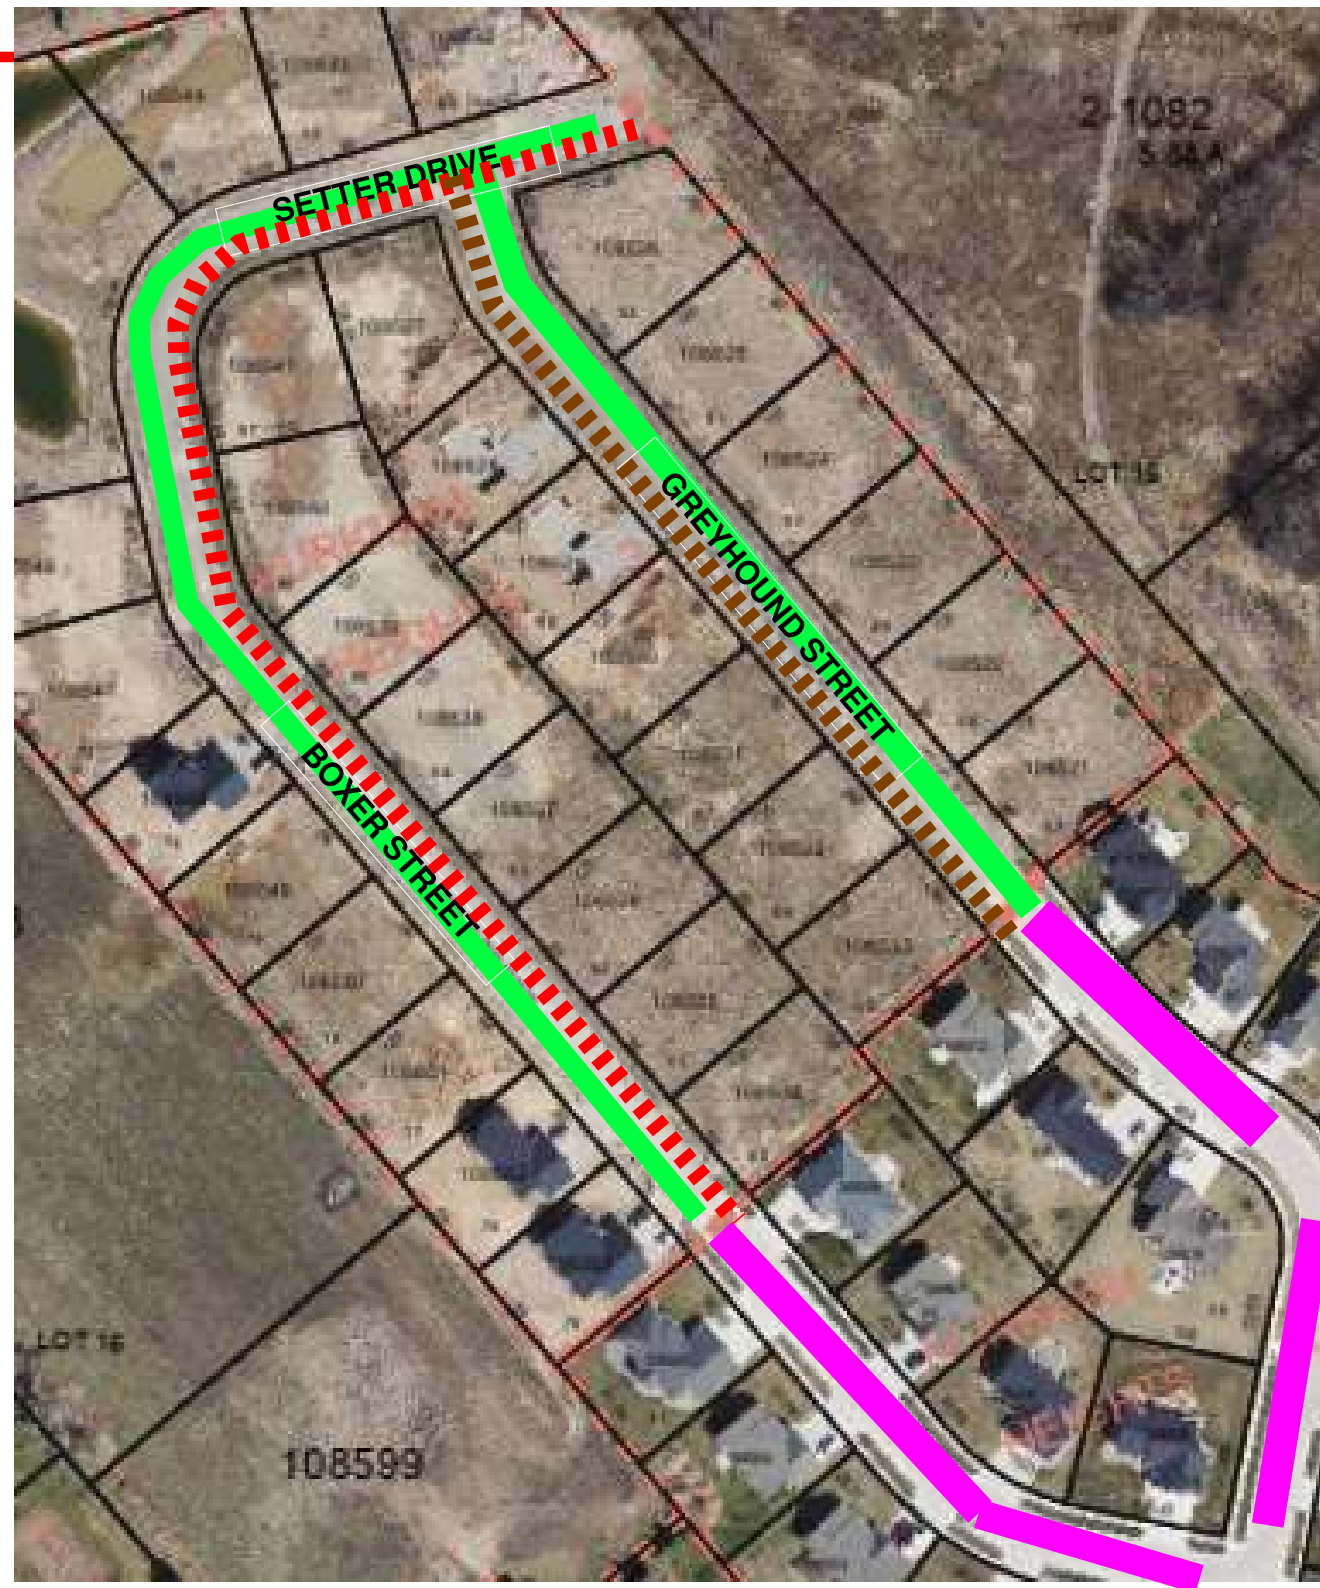

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

RECOMMENDED PARKING

NO PARKING = 
TEMPORARY PARKING = 


NOTES:

- The week of July 24th, the sidewalk contractor will be working on backfilling behind the curb and constructing the sidewalk and driveway aprons.
 - The concrete street contractor will be pouring some street at the intersection of Setter and Greyhound. You will not be able to drive on this concrete for Seven days while it hardens.
 - You will not be able to get into your driveway for 7 days after the sidewalk contractor constructs your driveway apron and the sidewalk that goes across your driveway. You can continue to park at the southern portion of Greyhound and Boxer (see map to left.) while your driveway apron and sidewalk cure and harden.
 - Shortly after the sidewalk and driveway aprons are complete, the landscaper should start the landscape work..
- When the paving contractor sends an updated schedule, I will send out another update..

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 7/24 - 7/28

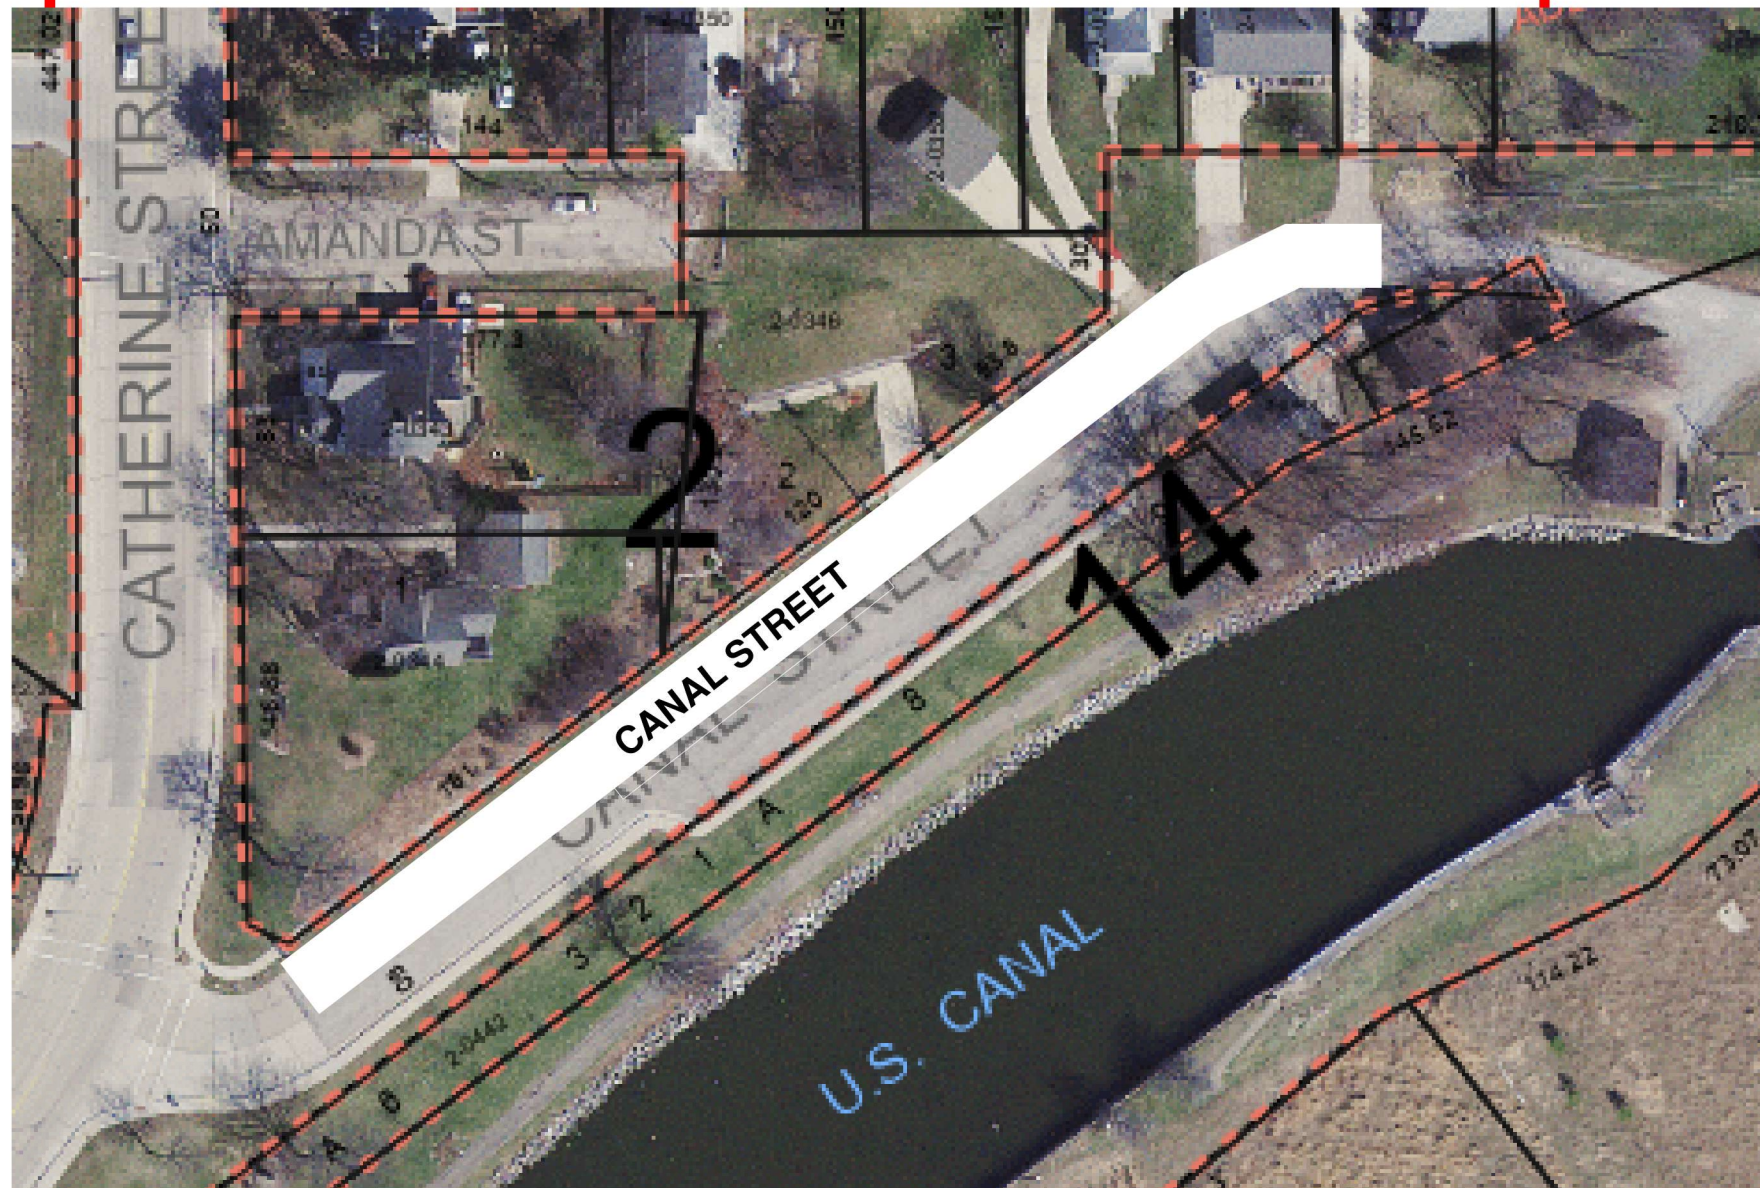

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDWALK/DRIVEWAY WORK
- RECOMMENDED PARKING
- NO PARKING = [Red dashed line]
- TEMPORARY PARKING = [Purple solid line]

NOTES:

- The sewer contractor is planning to start the storm sewer work the week of August 7th.
- The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of August 28th. When the paving contractor sends an updated schedule, I will send out another update.
- the Water Department will be relaying water main in Canal Street in the next two weeks. Their contractor should be handing out notices before the works starts.
