
PROJECT 2-23 (KENNETH AVENUE & 4TH STREET AREA UTILITY RELAY)


WEEKLY SCHEDULE UPDATE FOR THE WEEK OF JULY 31 - AUGUST 4

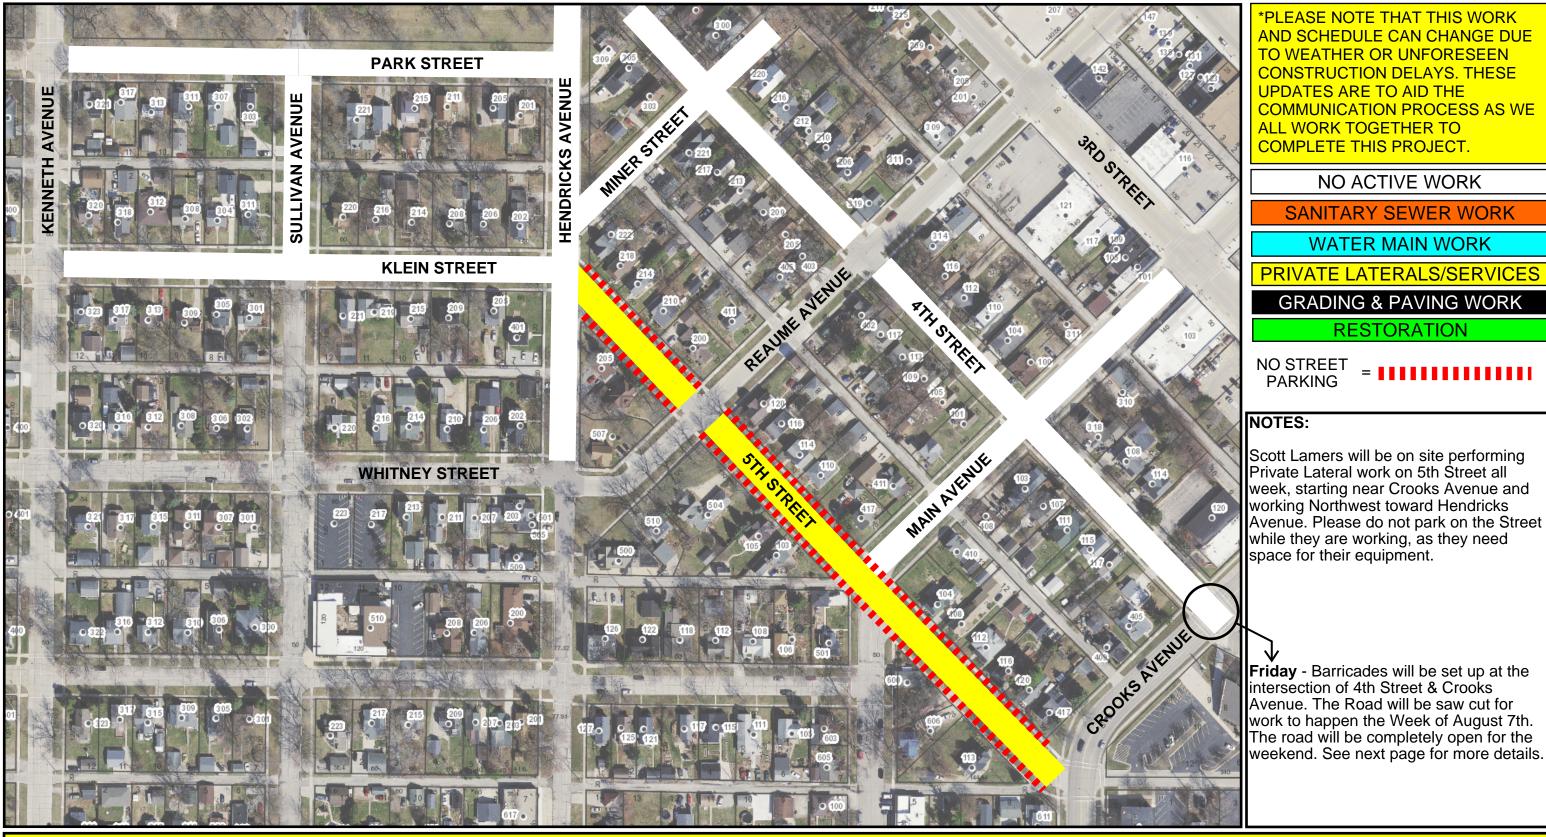

Thank You for joining the weekly email list! Encourage your neighbors to join too by sending an email to Taylor Conger at tconger@kaukauna.gov

PROJECT 2-23 (KENNETH AVENUE & 4TH STREET AREA UTILITY RELAY)

CROOKS AVENUE & 4TH STREET INTERSECTION CLOSURE FOR THE WEEK OF AUGUST 7TH

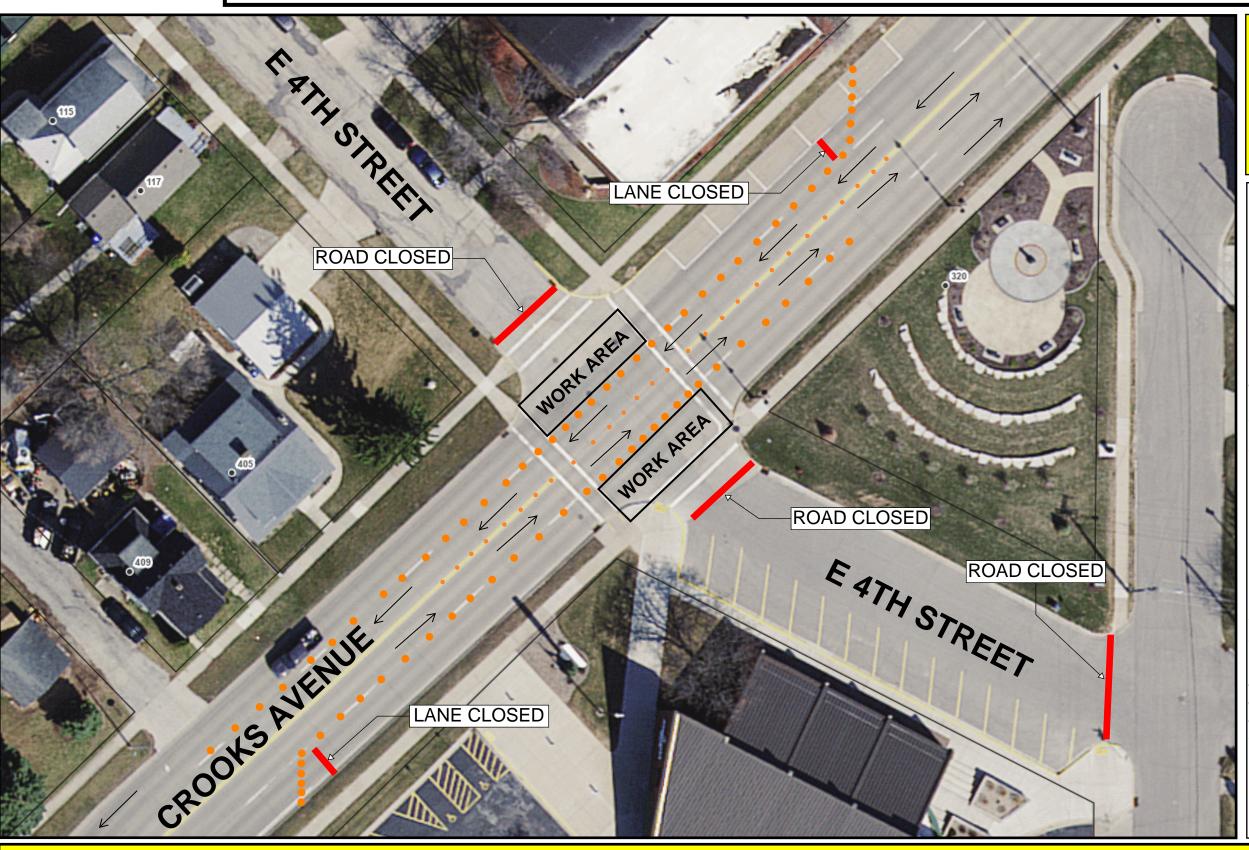

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

NOTES:

= Barrels

Friday August 4th - Barricades will be set up at the intersection of 4th Street & Crooks Avenue. The Road will be saw cut for work to happen the Week of August 7th. The road will be completely open for the weekend.

Monday August 7th - Road removal and excavation.

Tuesday August 8th - Underground Operation to connect the two digging work areas.

Wednesday - Friday August 9th to 11th Continue work as needed to complete. When work is complete, Concrete will be placed immediately after. The new concrete will take approximately 24 to 36 hours to cure to acceptable strength for road to be opened by the end of Friday.

3rd Street and 5th Street intersections will remain open. Use these to Detour 4th Street to access your property.

PLEASE DRIVE SLOWLY
THROUGH THESE WORK AREAS
TO KEEP EVERYBODY SAFE AS
THEY WORK TO COMPLETE THIS
WORK AS QUICKLY AS
POSSIBLE. THE FASTER THEY
GET THE WORK DONE, THE
SOONER THE ROAD CAN BE
REOPENED.
