


PROJECT 2-23 (KENNETH AVENUE & 4TH STREET AREA UTILITY RELAY)

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF AUGUST 21 - 25

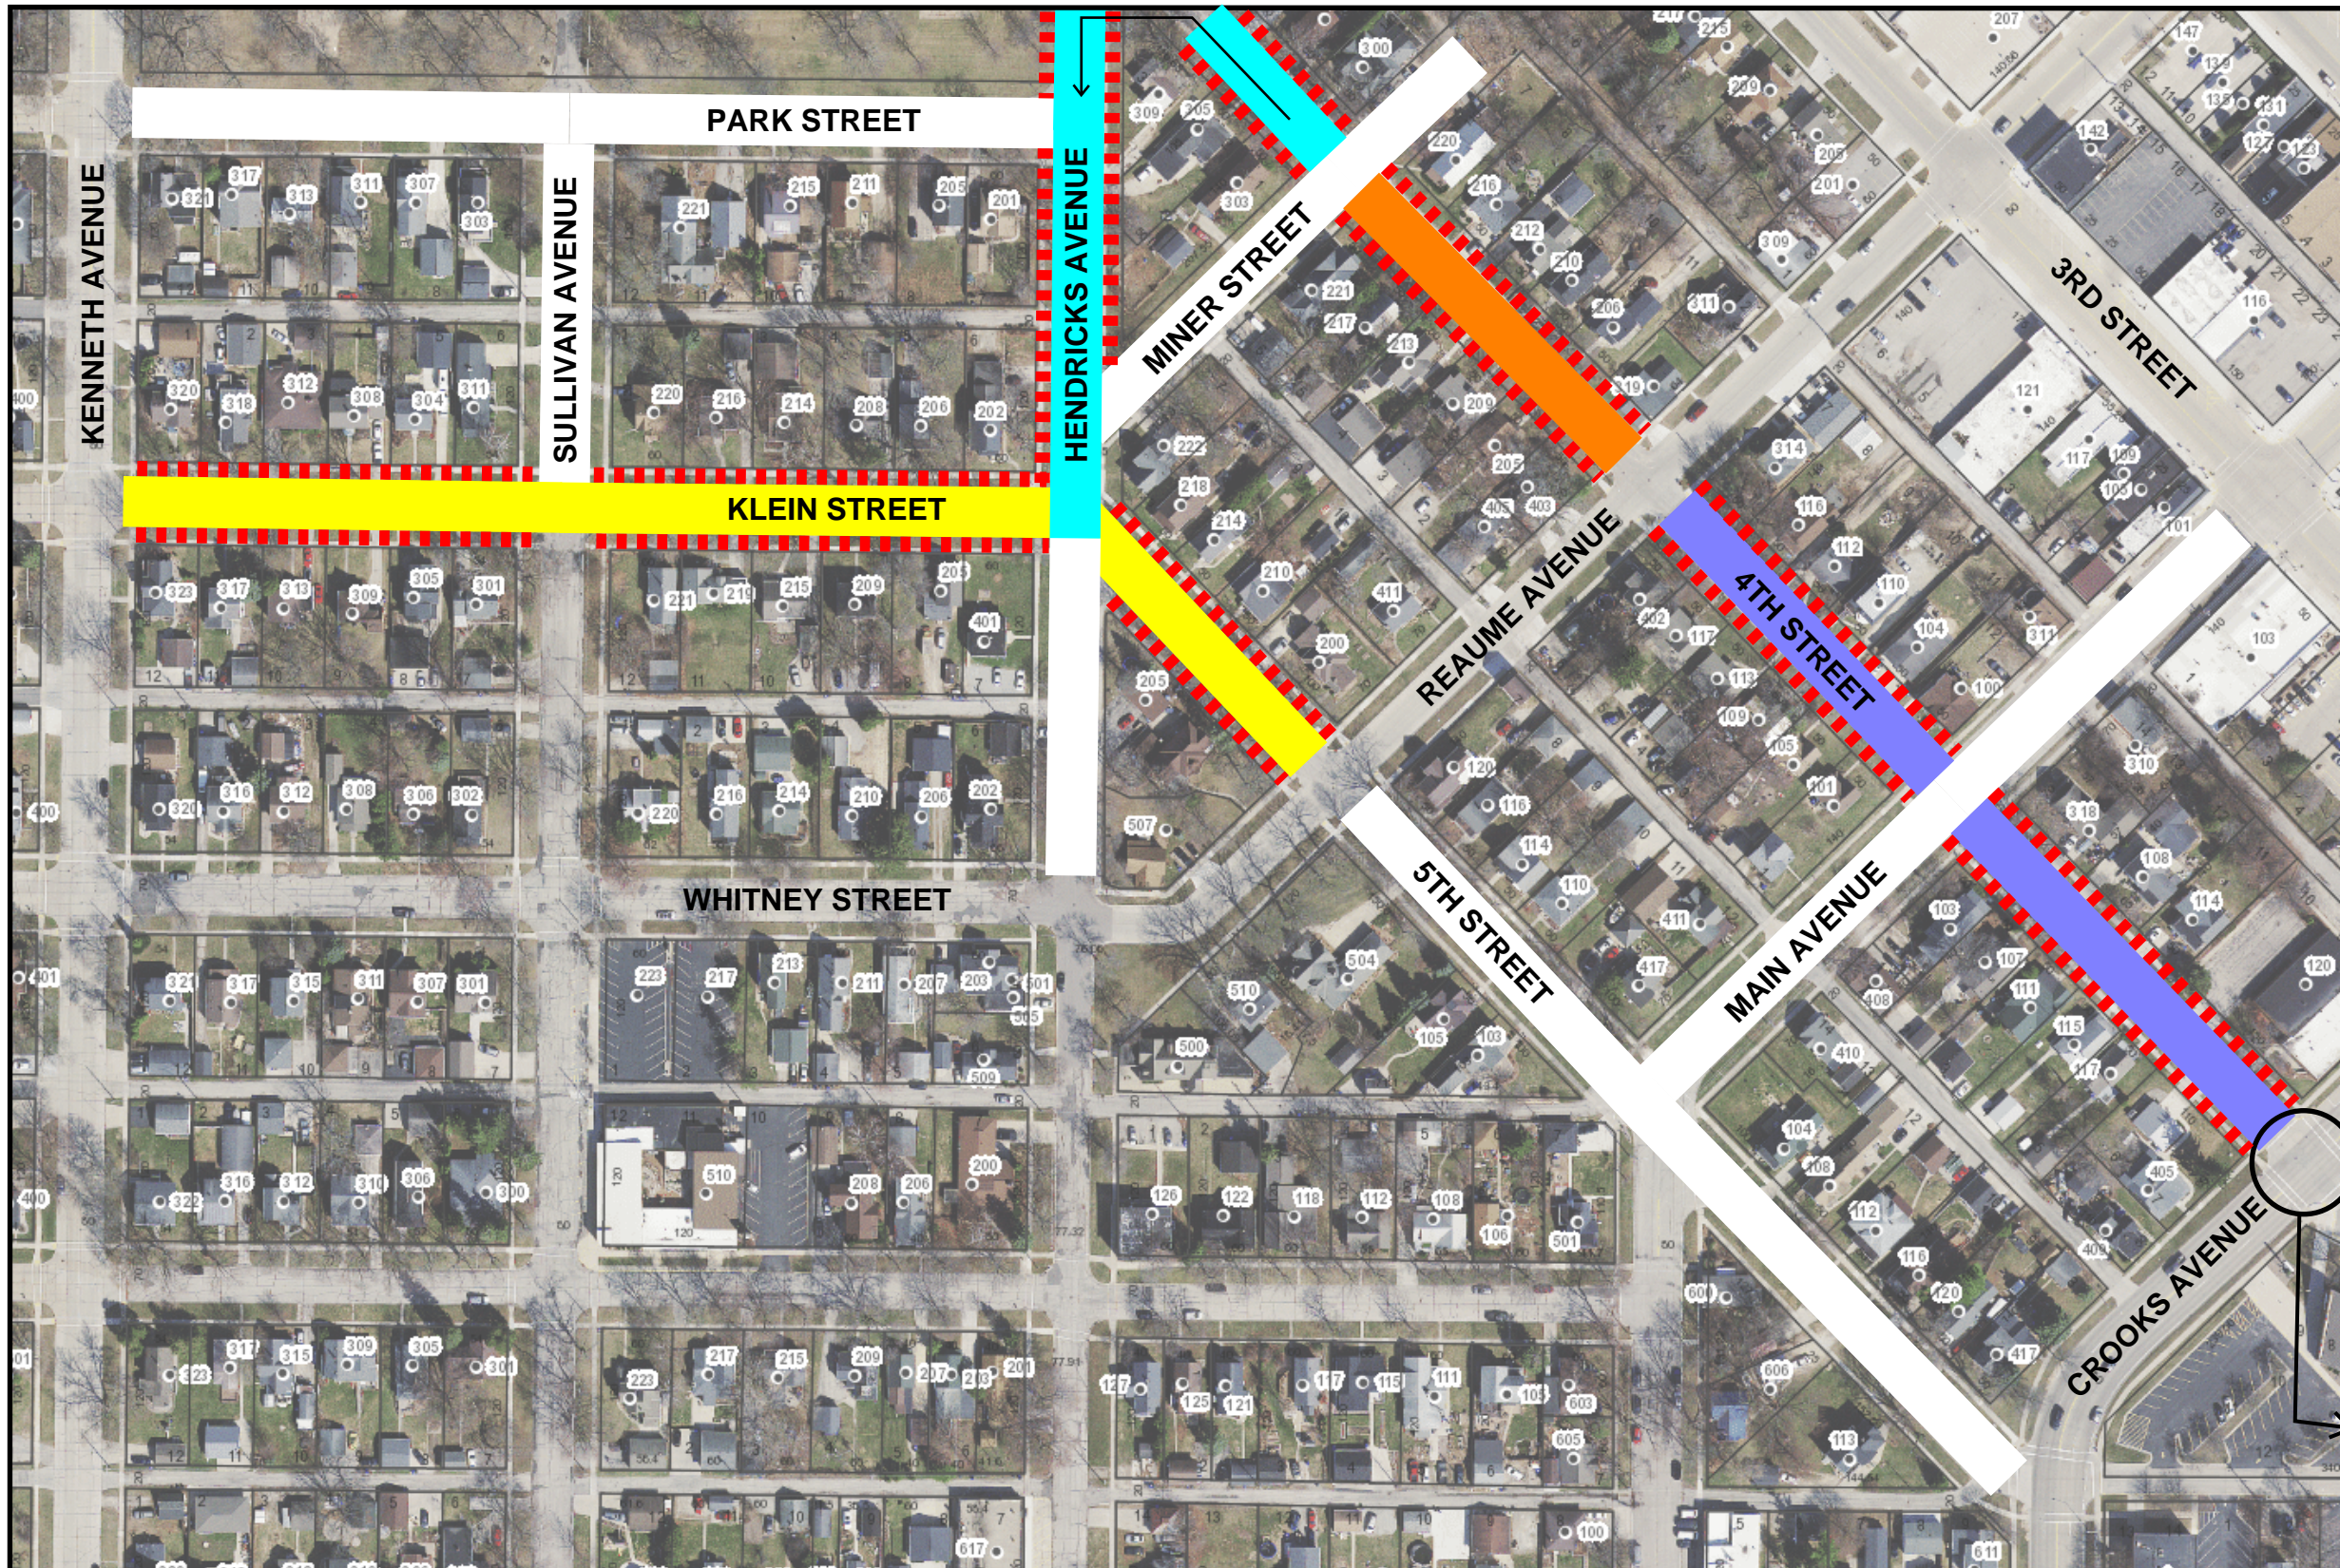

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- NO ACTIVE WORK
- SANITARY SEWER WORK
- WATER MAIN WORK
- PRIVATE LATERALS/SERVICES
- PUBLIC LATERALS/SERVICES
- RESTORATION
- GRADING & PAVING

NO STREET PARKING = [Red dashed line symbol]

NOTES:

Carl Bowers will have 2 crews on site next week. One crew will be constructing the new water main on 4th Street between Miner and Hendricks then down Hendricks Avenue working south. If they get this far, they will work on sanitary sewer on 4th Street starting at Reaume working Northwest. The other crew will be working on laterals and services from the road to the sidewalks.

Scott Lamers will continue working on private laterals and services on 5th Street, then onto Klein as they work their way west. They occasionally need to jump around due to scheduling.

Al Dix will be replacing the remaining concrete in Crooks Avenue on Monday or Tuesday next week. Crooks Avenue will be open over the weekend.
