


PROJECT 2-23 (KENNETH AVENUE & 4TH STREET AREA UTILITY RELAY)

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF AUGUST 28 - SEPTEMBER 1

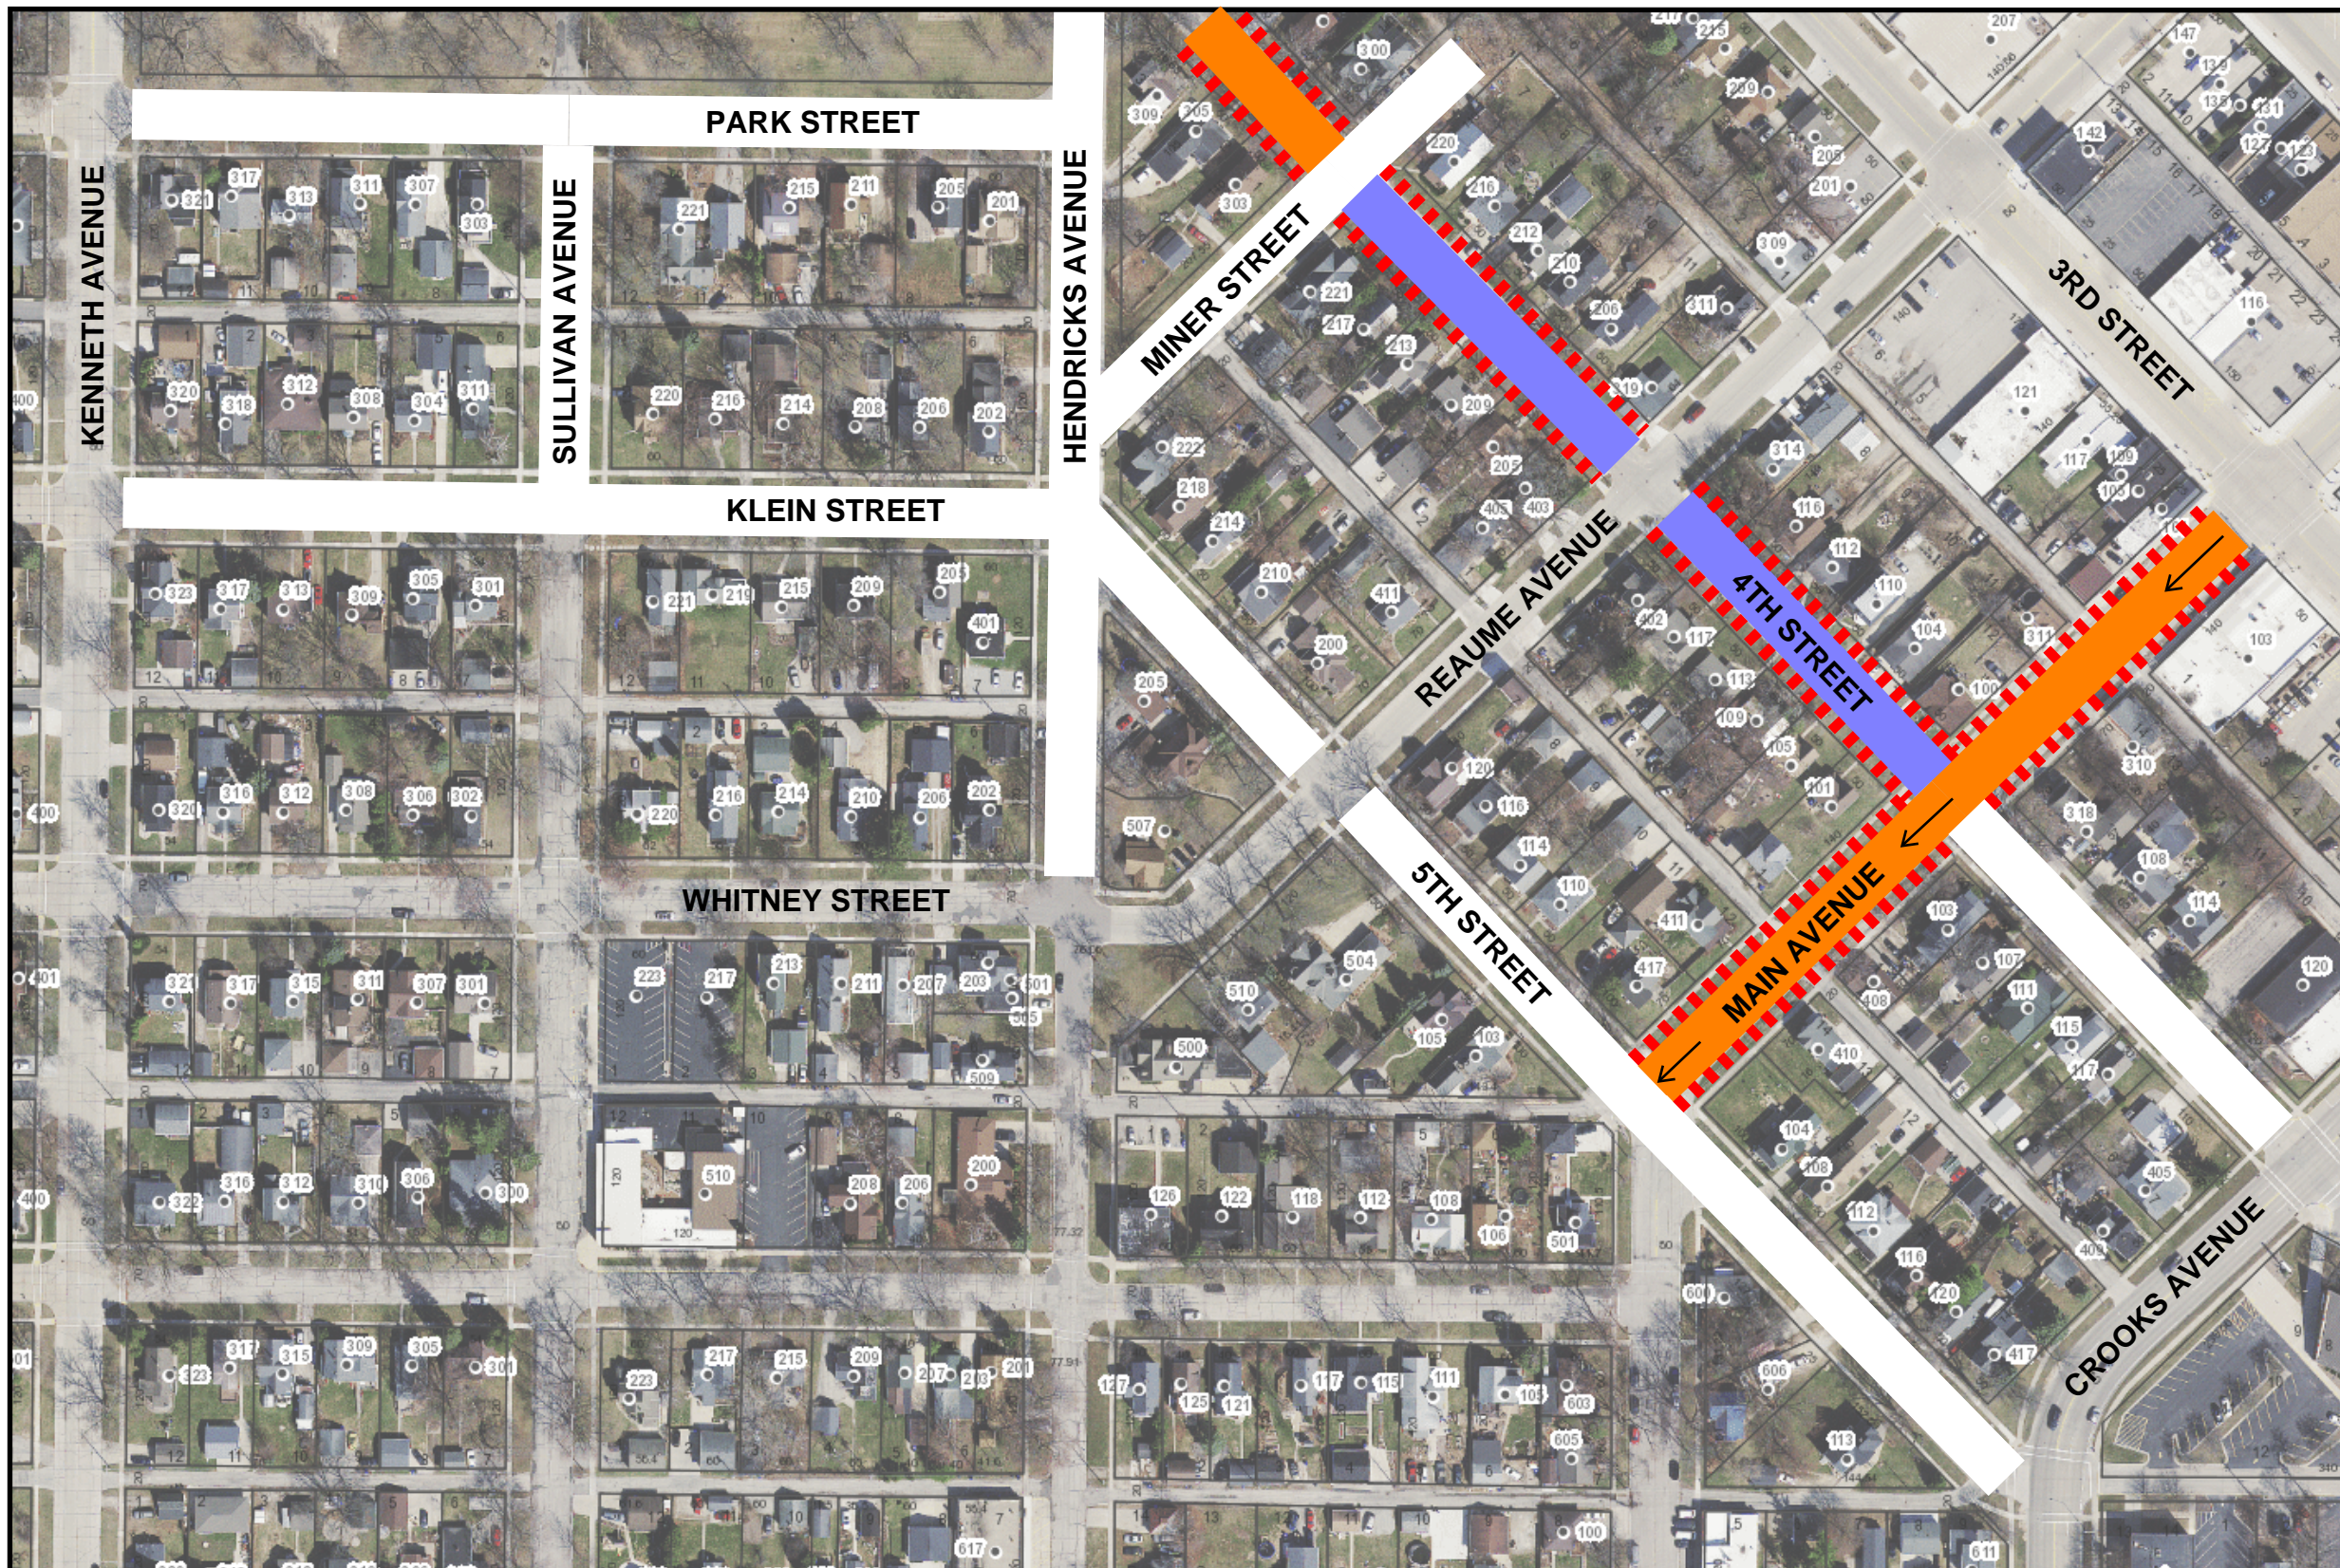

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- NO ACTIVE WORK
- SANITARY SEWER WORK
- WATER MAIN WORK
- PRIVATE LATERALS/SERVICES
- PUBLIC LATERALS/SERVICES
- RESTORATION
- GRADING & PAVING
- NO STREET PARKING = [Red dashed line symbol]

NOTES:
Carl Bowers will have 2 crews on site next week. One crew will be finishing some sanitary sewer work on W. 4th Street near Hendricks. Once complete, they will be working on the sanitary sewer on Main Avenue, starting near 3rd Street working to the Southwest. The second crew will continue working on Public Laterals & Services on 4th Street.
Scott Lamers will NOT be on site next week.
