


# PROJECT 1-23 METOXEN, DIXON, QUINNEY & SEVENTH

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 8/7 - 8/11 -UPDATE

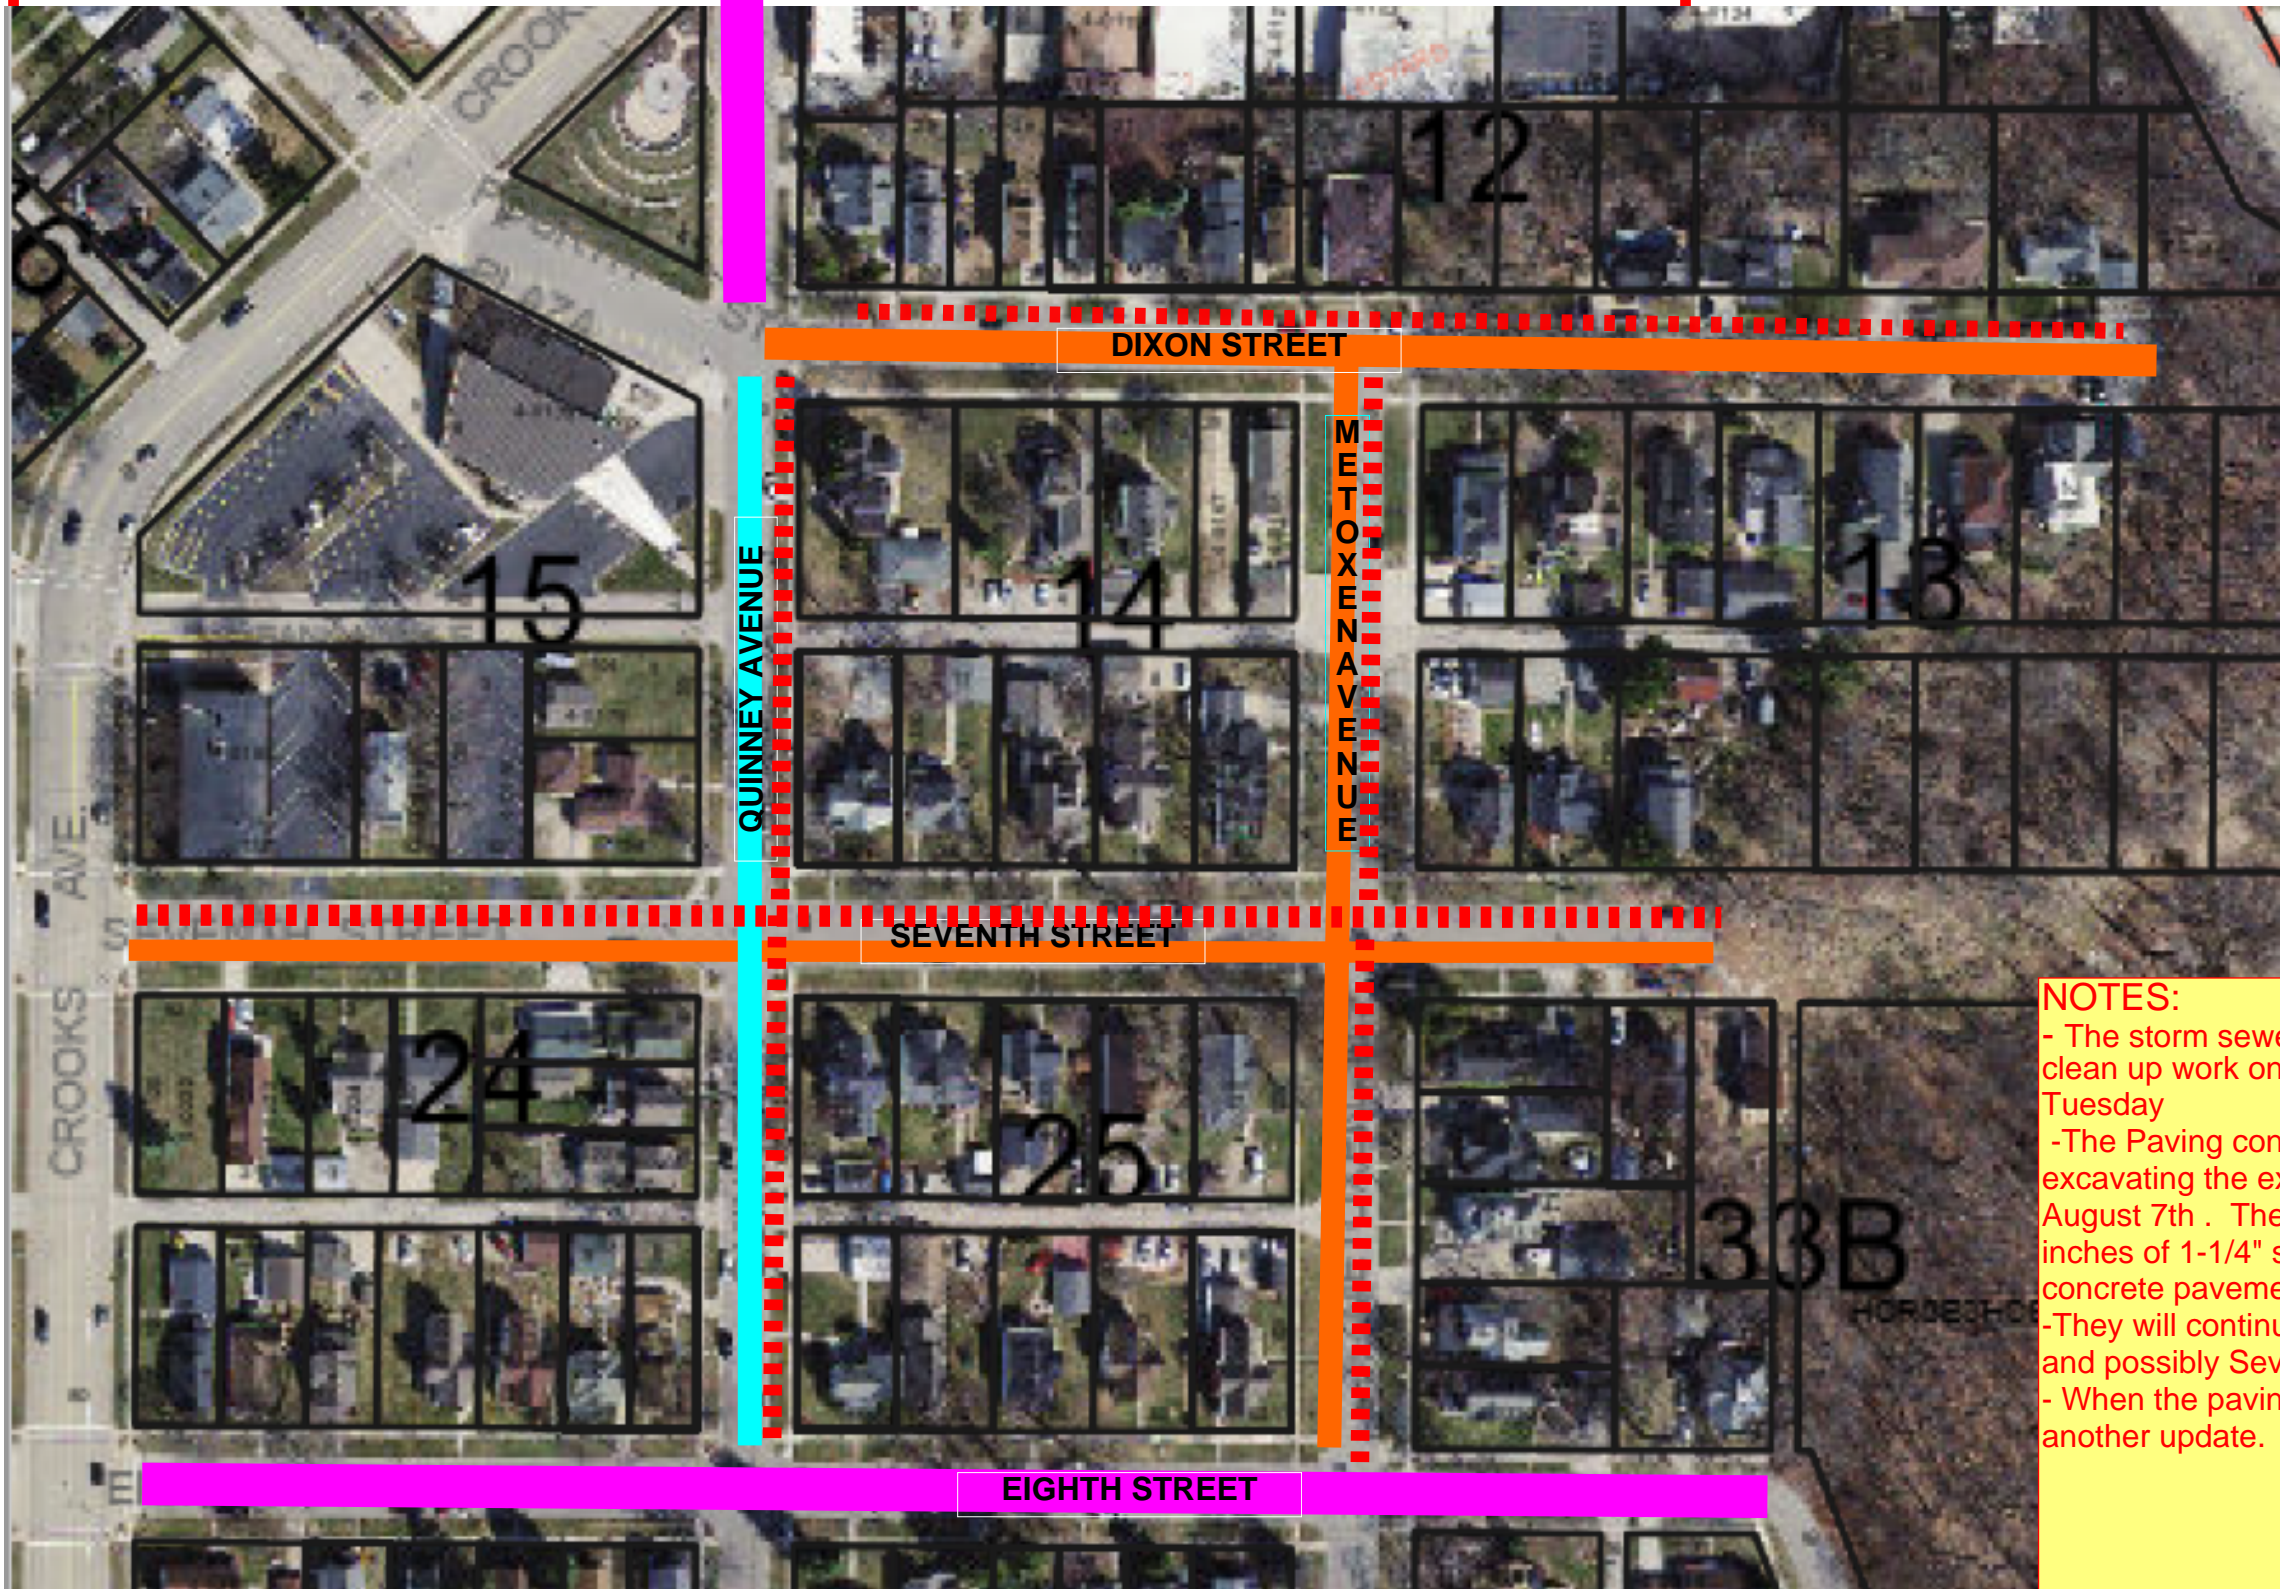

\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDWALK/DRIVEWAY WORK
- RECOMMENDED PARKING
- NO PARKING = [Red dashed line]
- TEMPORARY PARKING = [Magenta bar]

**NOTES:**

- The storm sewer contractor has a few storm laterals to install and some clean up work on the project. They should be done with this work by Tuesday
- The Paving contractor will continue removing existing pavement, excavating the existing stone base, and placing new road stone the week of August 7th . The new road stone consists of 6 inches of 3" stone with 6 inches of 1-1/4" stone on top of the 3" stone. There will be 6 inches of concrete pavement on the stone with 6 inch high curb.
- They will continue on Dixon Street. They will also work on Metoxen Avenue and possibly Seventh Street the week of August 7th.
- When the paving contractor sends an updated schedule, I will send out another update.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at [jbodoh@kaukauna-wi.org](mailto:jbodoh@kaukauna-wi.org) to be added to the weekly email update list.

# PROJECT 1-23 WHITE DOVE, WHITE BIRCH, LODERBAUER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 8/7 - 8/11-UPDATE



\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDEWALK/DRIVEWAY WORK
- RECOMMENDED PARKING
- NO PARKING = [Red dashed line]
- TEMPORARY PARKING = [Pink bar]


## NOTES:

- The week of August 7th, the sidewalk contractor will continue working on constructing the sidewalk and driveway aprons. Monday the contractor will place 3 segments of curb & gutter in the open area in the intersection of White Dove and White Birch. This area will eventually be paved with asphalt.
- You will not be able to get into your driveway for 7 days after the sidewalk contractor constructs your driveway apron and the sidewalk that goes across your driveway. You can continue to park at the northern portion of White Birch and Red Fox Lane(see map to left.) while your driveway apron and sidewalk cure and harden.
- Shortly after the sidewalk and driveway aprons are complete, the landscaper should start the landscape work.
- The street paving contractor will be paving the second lane of Loderbauer Road on Monday. This lane will be closed for 7 days while it cures and strengthens.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at [jbodoh@kaukauna-wi.org](mailto:jbodoh@kaukauna-wi.org) to be added to the weekly email update list.

# PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 8/7 - 8/11 - UPDATE

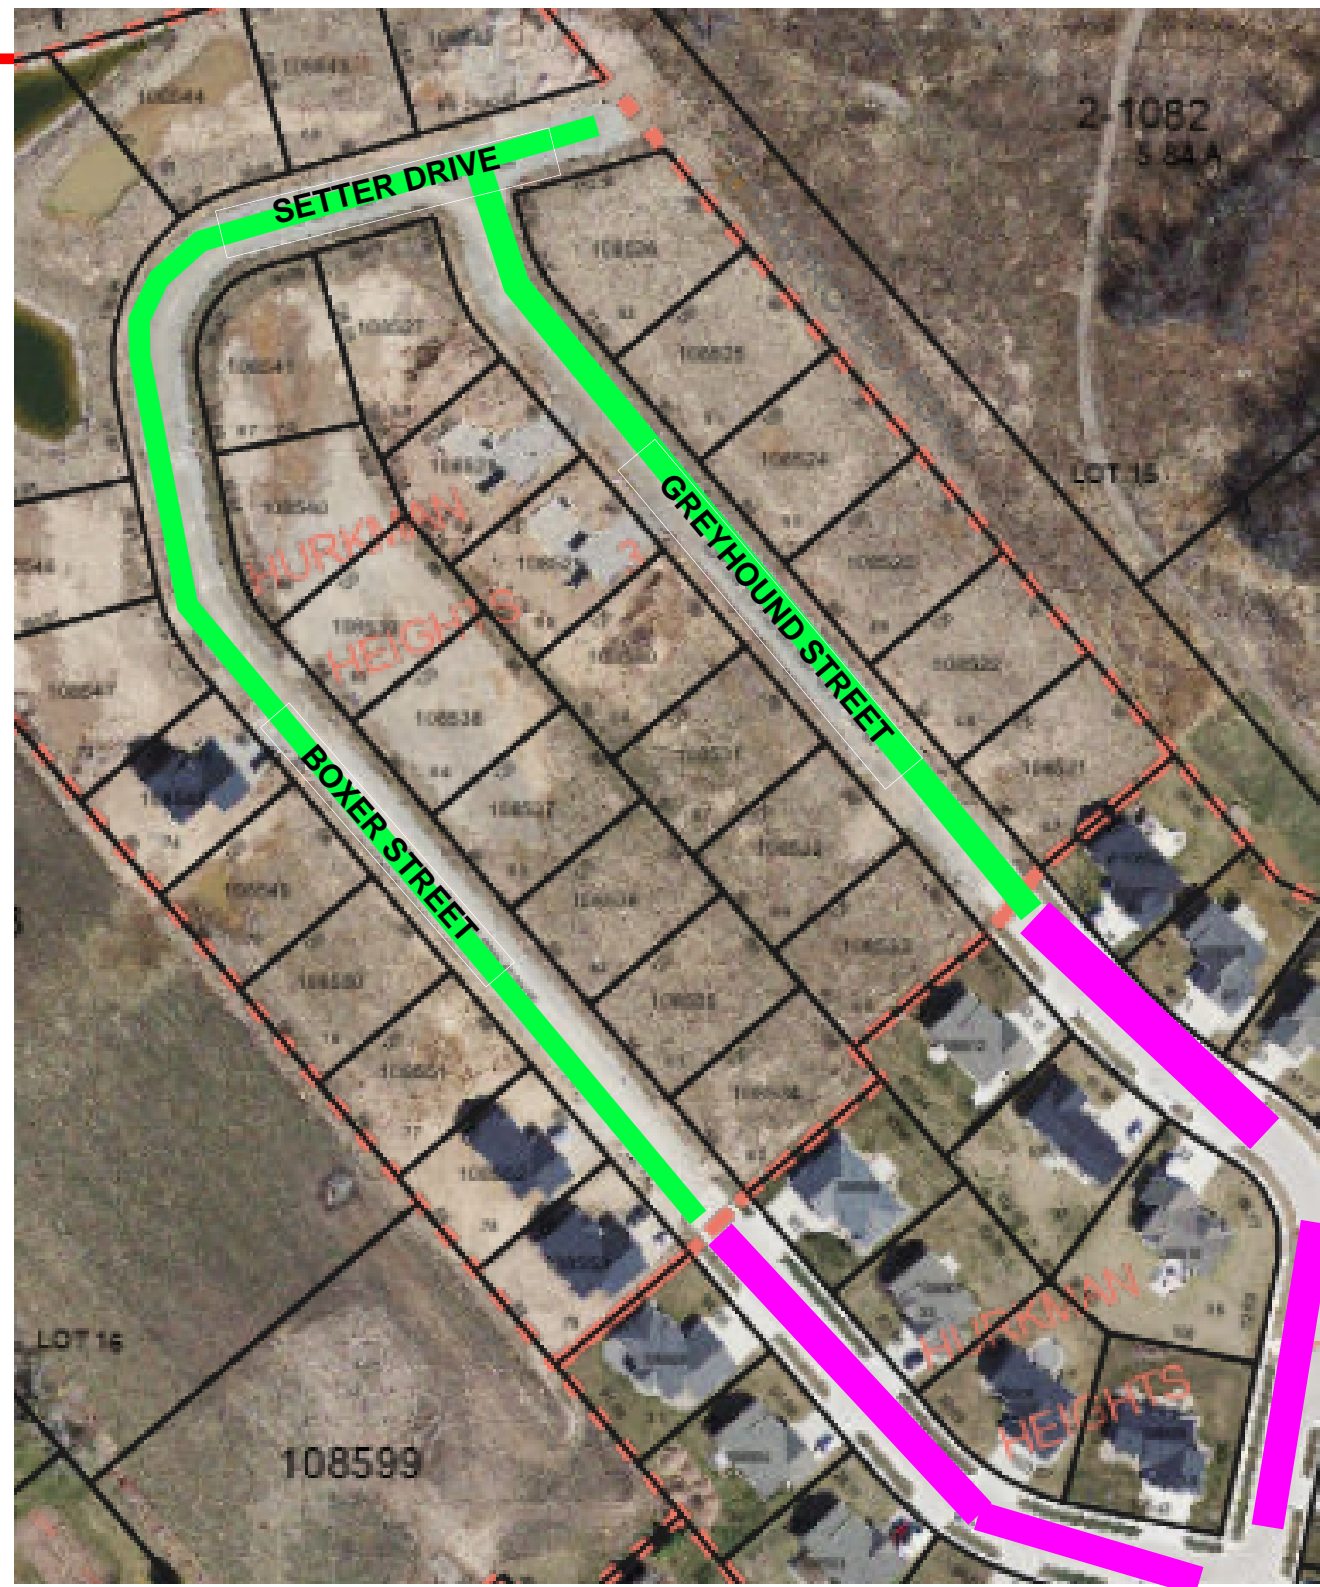

\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

RECOMMENDED PARKING

NO PARKING =   
 TEMPORARY PARKING = 

## NOTES:

- The week of August 7th, the sidewalk contractor will continue working on constructing the sidewalk and driveway aprons.
  - The concrete street contractor will be pouring some street at the intersection of Setter and Greyhound on Monday. You will not be able to drive on this concrete for Seven days while it hardens.
  - You will not be able to get into your driveway for 7 days after the sidewalk contractor constructs your driveway apron and the sidewalk that goes across your driveway. You can continue to park at the southern portion of Greyhound and Boxer (see map to left.) while your driveway apron and sidewalk cure and harden.
  - Shortly after the sidewalk and driveway aprons are complete, the landscaper should start the landscape work..
- When the paving contractor sends an updated schedule, I will send out another update..
- The curved section connecting Setter and Boxer that was not paved in concrete, will be paved in asphalt later this summer.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at [jbodoh@kaukauna-wi.org](mailto:jbodoh@kaukauna-wi.org) to be added to the weekly email update list.

# PROJECT 1-23 OAK & SCHULTHEIS

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 8/7 - 8/11



\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDEWALK/DRIVEWAY WORK
- RECOMMENDED PARKING


NO PARKING = |||||  
 TEMPORARY PARKING =

**NOTES:**

- The sewer contractor is planning to start the storm sewer work the week of August 7th.
- The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of August 21st.
- When the paving contractor sends an updated schedule, I will send out another update.

# PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 8/7 - 8/11

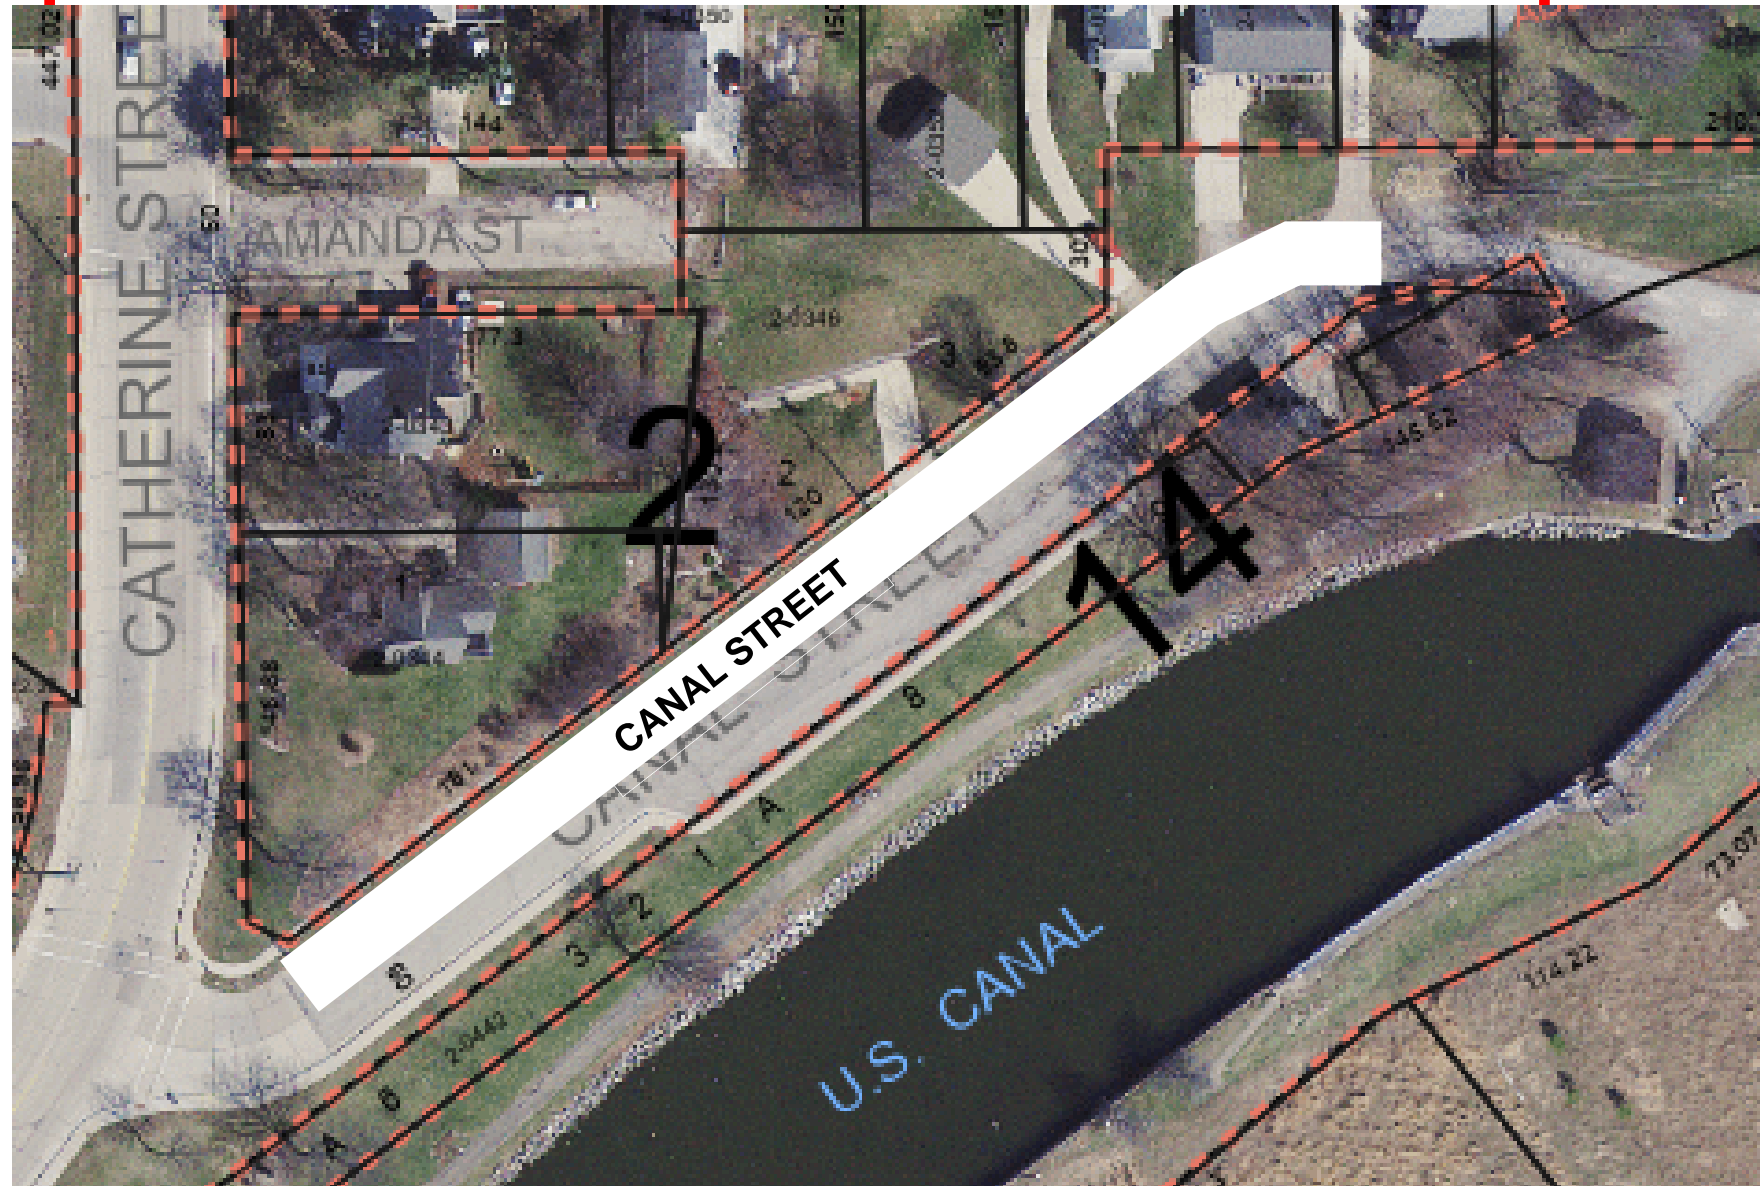

\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDEWALK/DRIVEWAY WORK
- RECOMMENDED PARKING
- NO PARKING = [Red dashed line]
- TEMPORARY PARKING = [Purple solid line]


**NOTES:**

- The sewer contractor is planning to start the storm sewer work the week of August 21st.
- The Paving contractor is planning to start removing existing pavement and excavating the existing stone base the week of August 28th. When the paving contractor sends an updated schedule, I will send out another update.
- the Water Department' contractor will be boring across the navigation canal for the next week. The contractor will then relay the water main in Canal Street which will take about a week. The water main project should be done by mid August. Their contractor should be handing out notices before the works starts.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at [jbodoh@kaukauna-wi.org](mailto:jbodoh@kaukauna-wi.org) to be added to the weekly email update list.

# PROJECT 2-23 (KENNETH AVENUE & 4TH STREET AREA UTILITY RELAY)

CROOKS AVENUE & 4TH STREET INTERSECTION CLOSURE FOR THE WEEK OF AUGUST 7TH

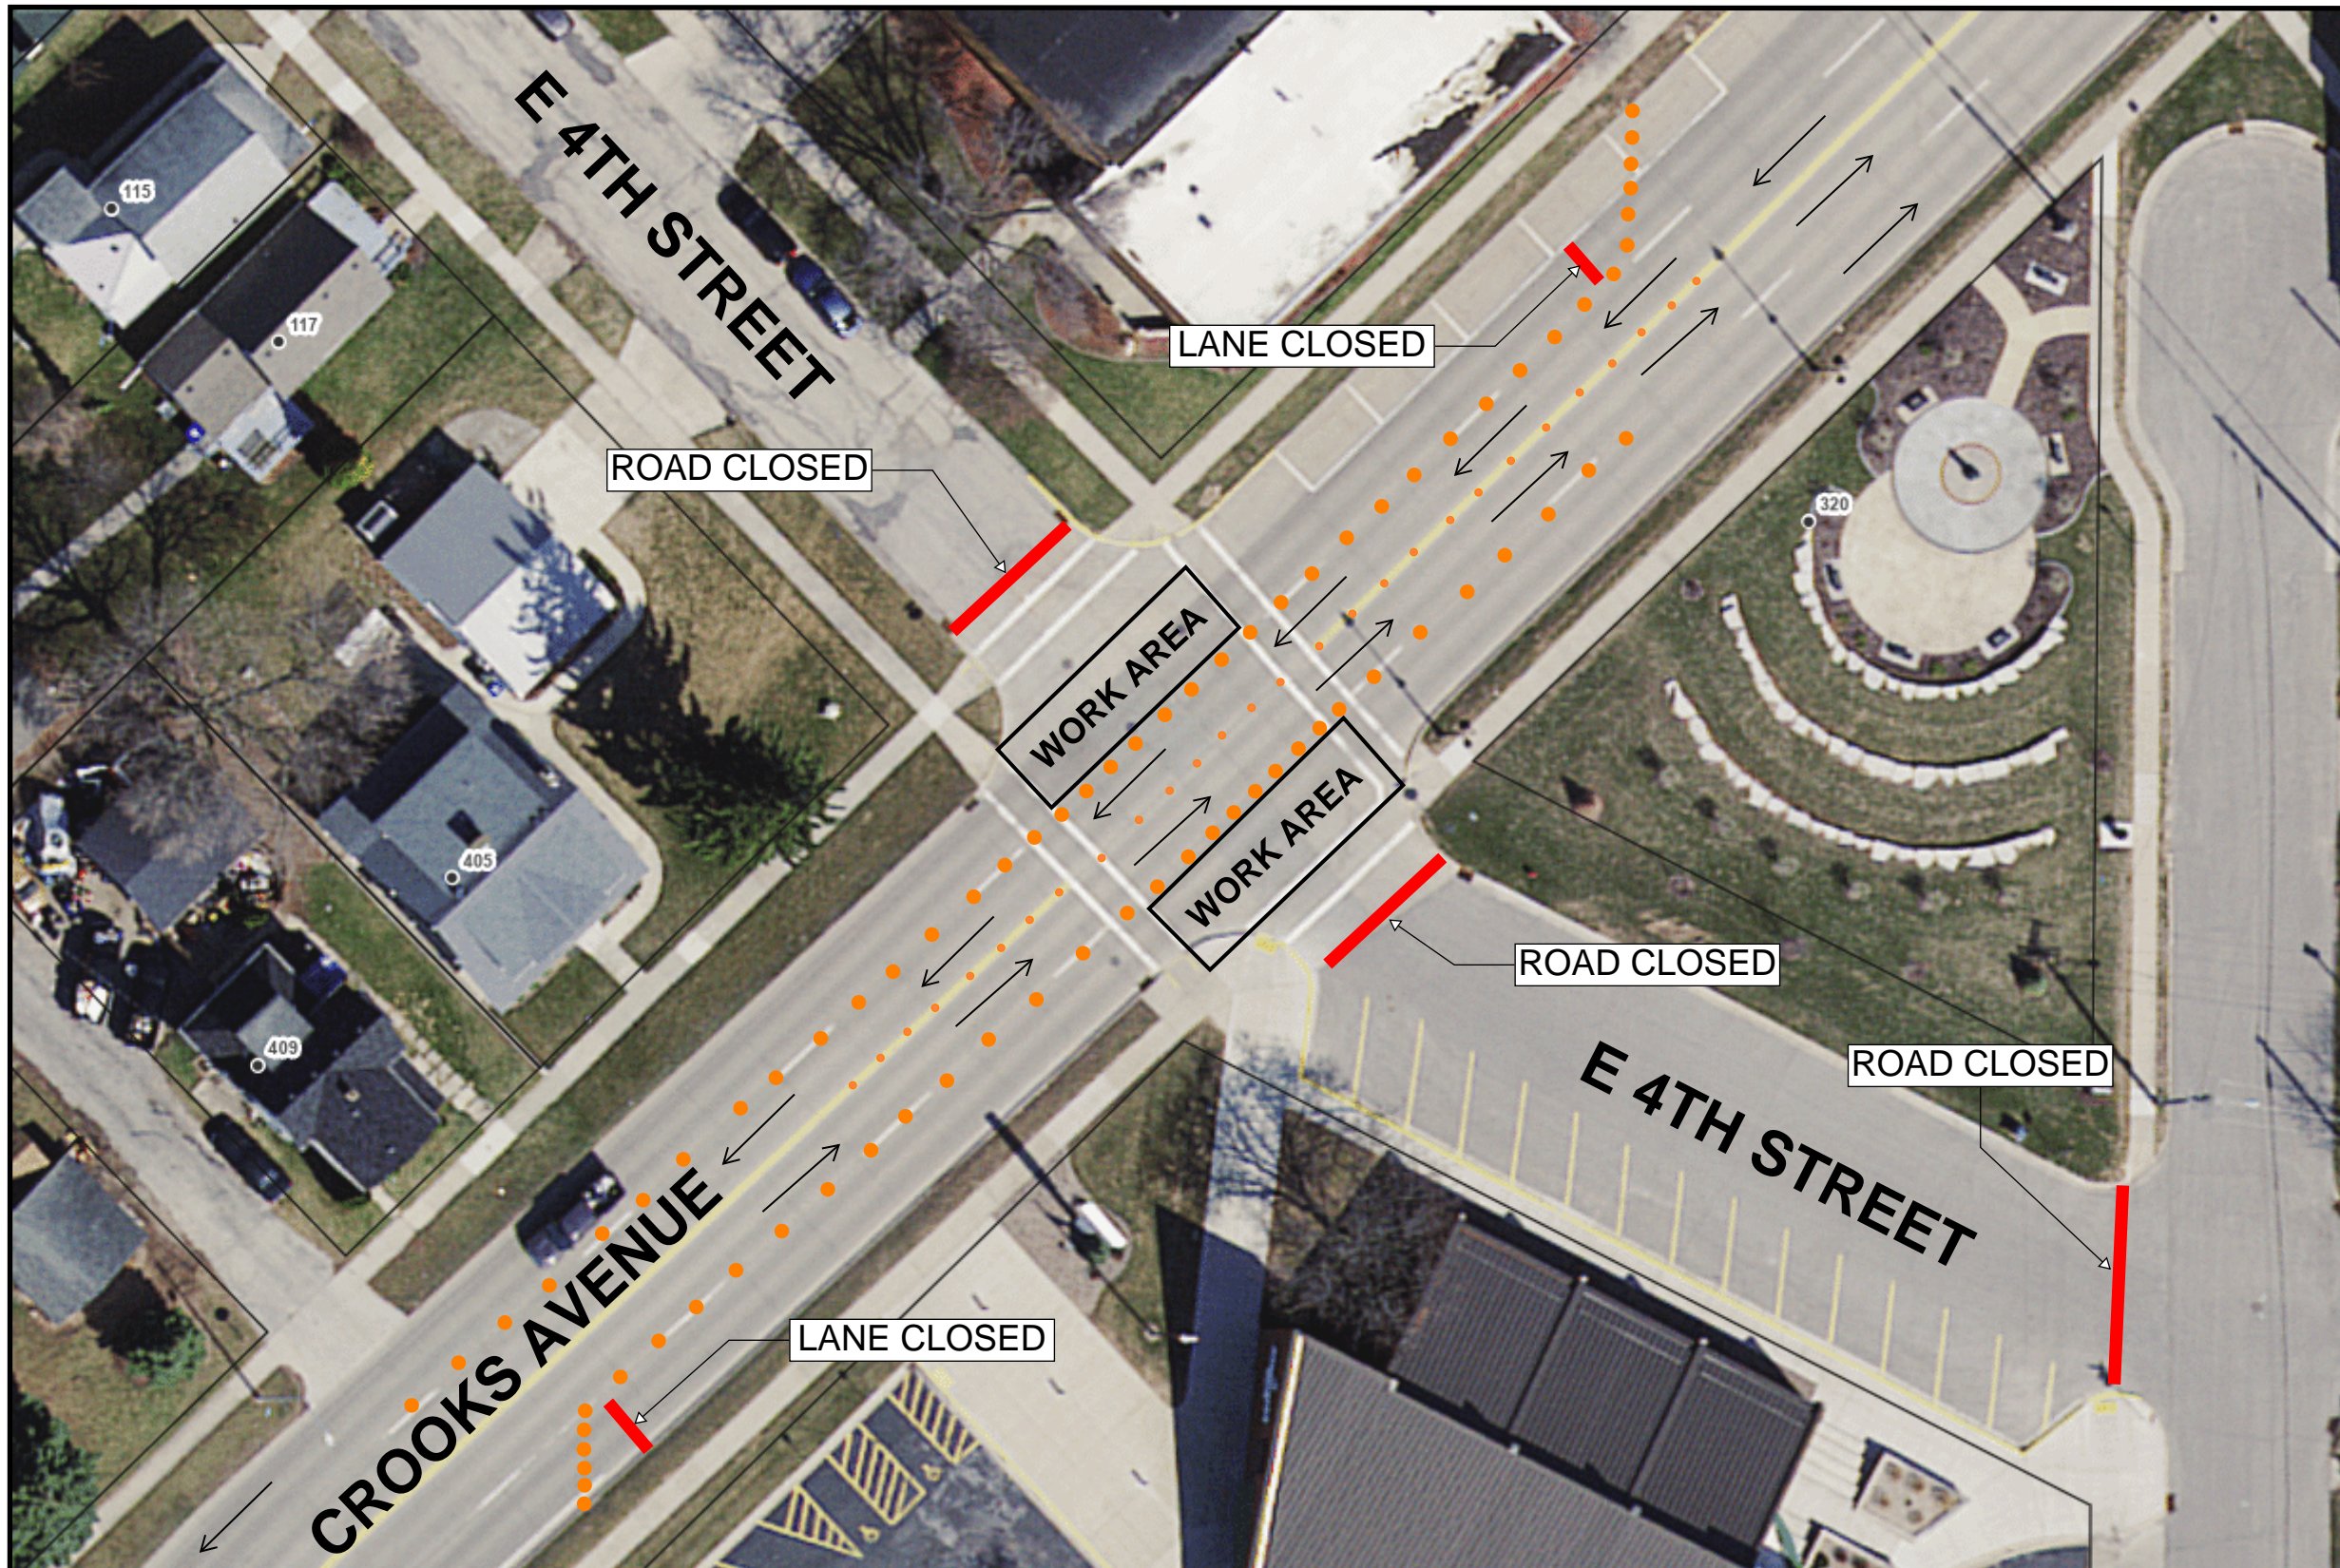

\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

**NOTES:** ● = Barrels  
**Friday August 4th** - Barricades will be set up at the intersection of 4th Street & Crooks Avenue. The Road will be saw cut for work to happen the Week of August 7th. The road will be completely open for the weekend.

**Monday August 7th** - Road removal and excavation.

**Tuesday August 8th** - Underground Operation to connect the two digging work areas.

**Wednesday - Friday August 9th to 11th** Continue work as needed to complete. When work is complete, Concrete will be placed immediately after. The new concrete will take approximately 24 to 36 hours to cure to acceptable strength for road to be opened by the end of Friday.

3rd Street and 5th Street intersections will remain open. Use these to Detour 4th Street to access your property.

**PLEASE DRIVE SLOWLY THROUGH THESE WORK AREAS TO KEEP EVERYBODY SAFE AS THEY WORK TO COMPLETE THIS WORK AS QUICKLY AS POSSIBLE. THE FASTER THEY GET THE WORK DONE, THE SOONER THE ROAD CAN BE REOPENED.**
