


PROJECT 2-23 (KENNETH AVENUE & 4TH STREET AREA UTILITY RELAY)

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF SEPTEMBER 11 - 15

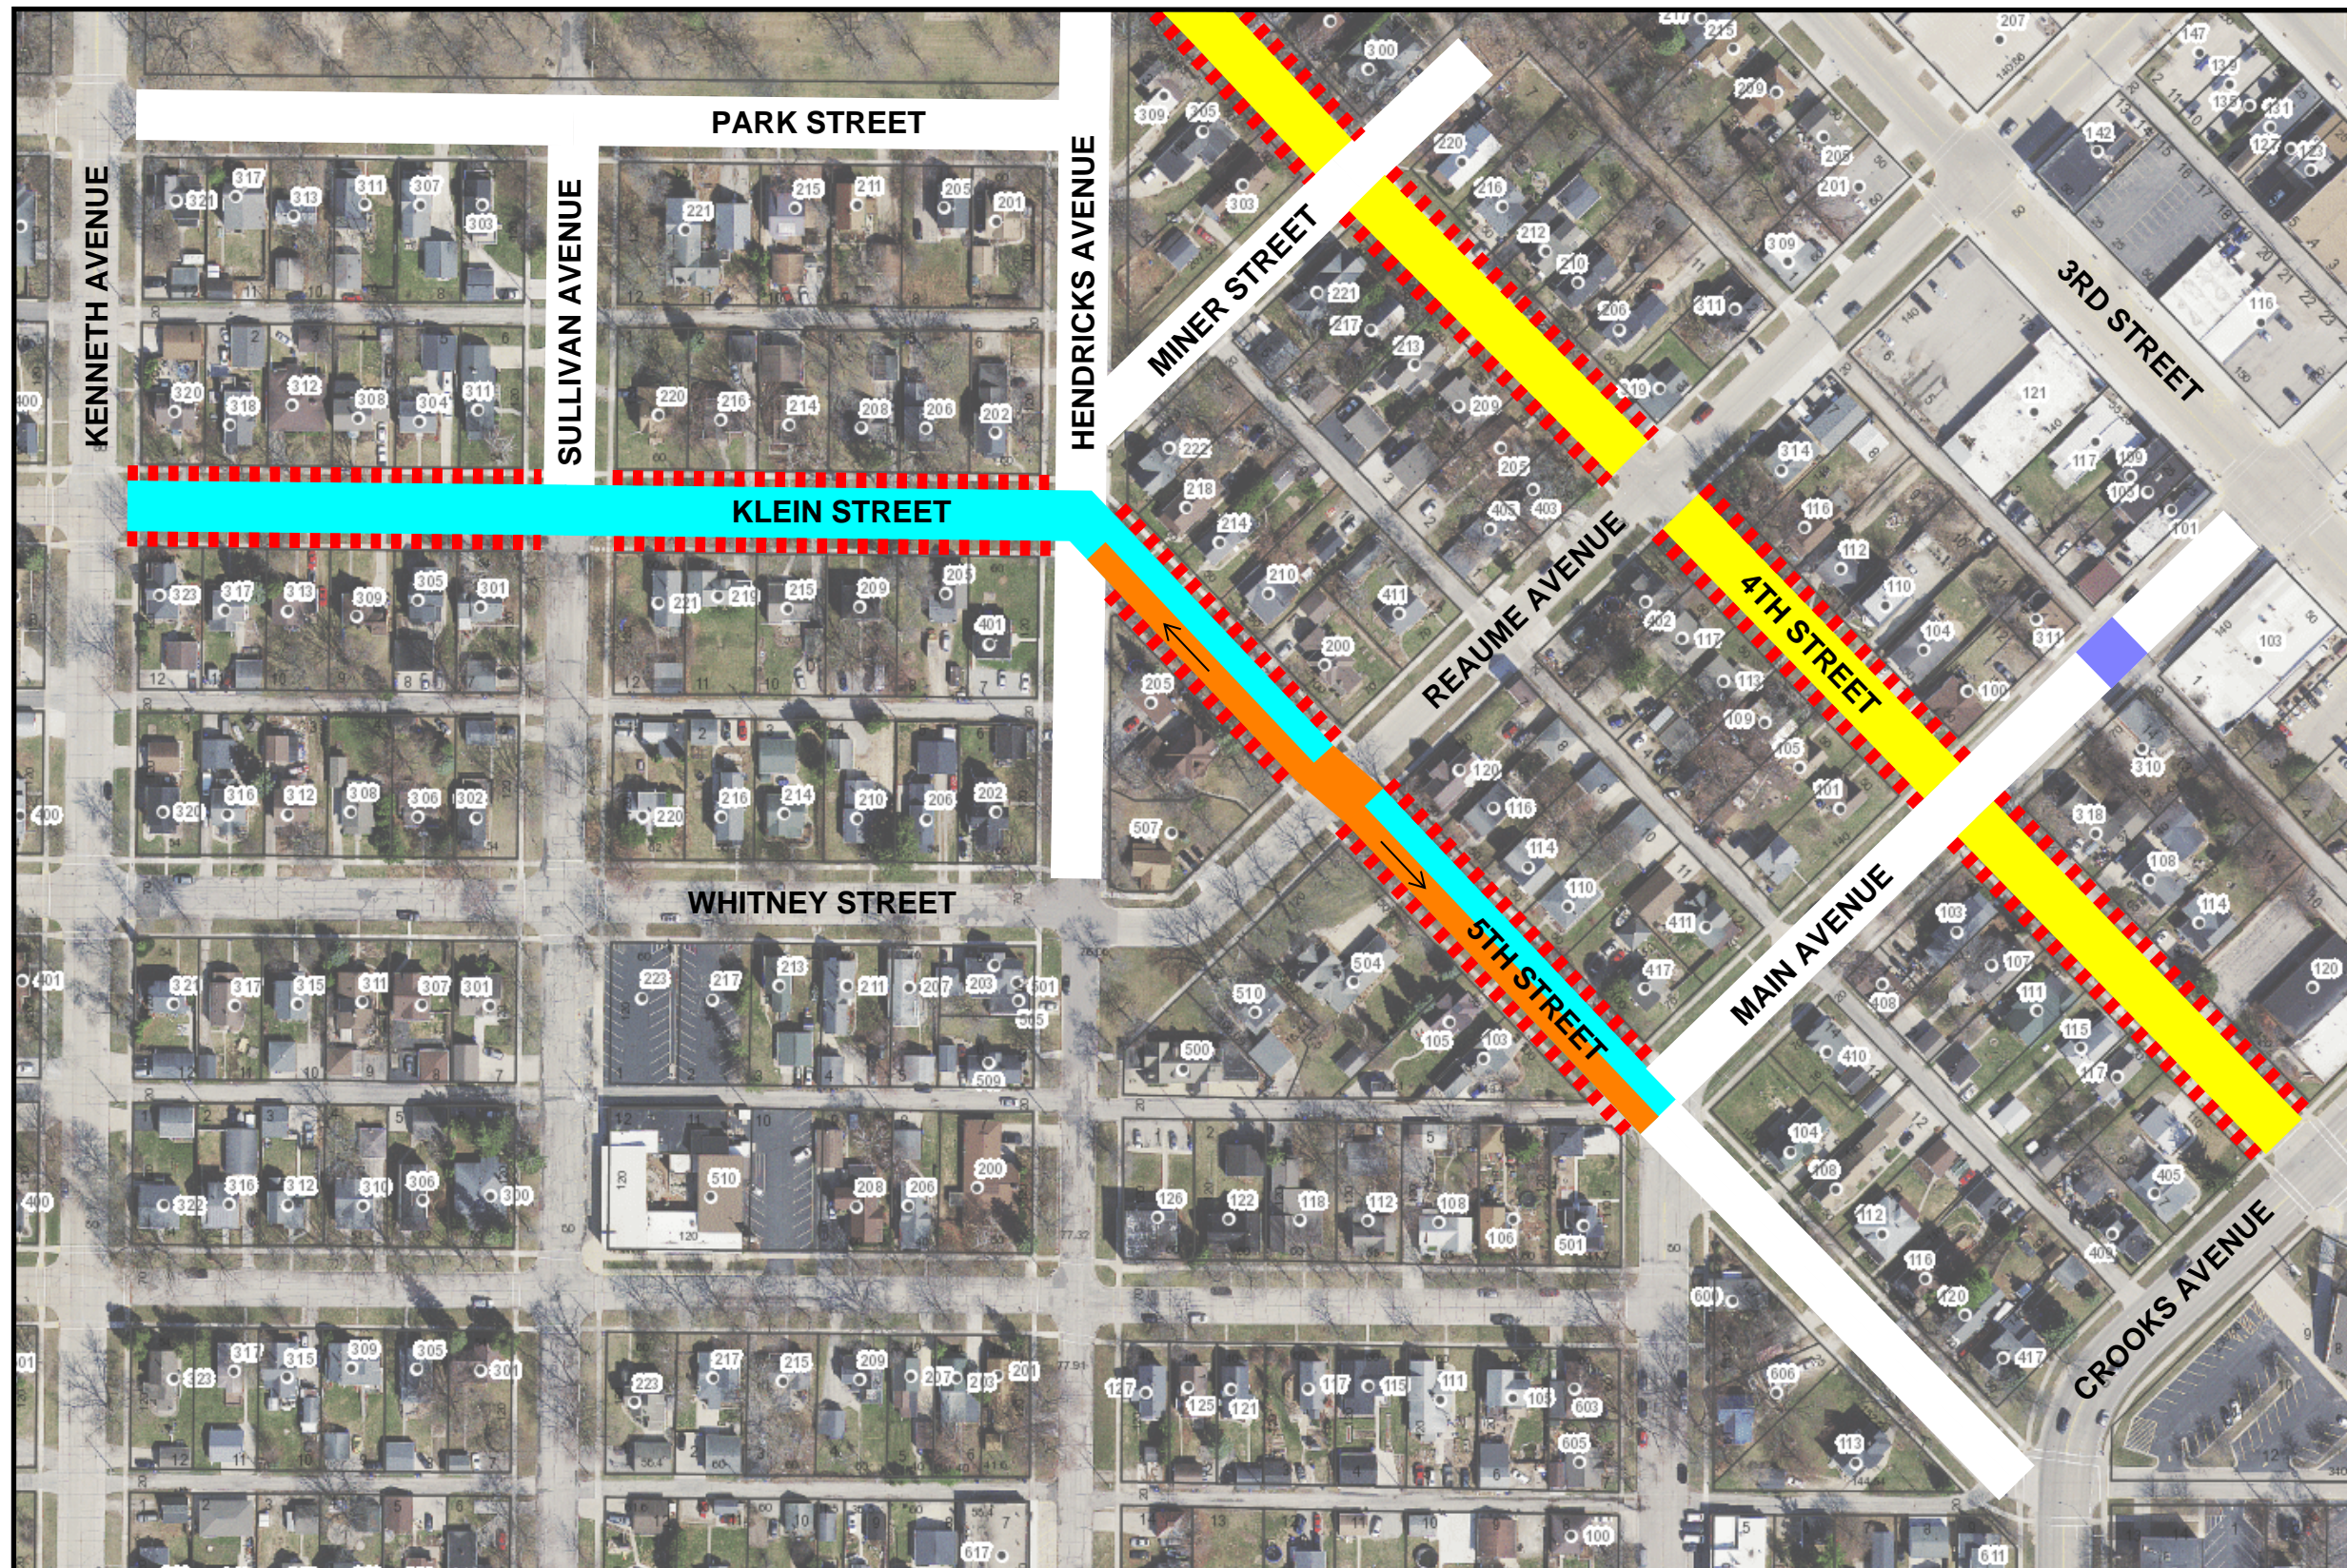

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- NO ACTIVE WORK
- SANITARY SEWER WORK
- WATER MAIN WORK
- PRIVATE LATERALS/SERVICES
- PUBLIC LATERALS/SERVICES
- RESTORATION
- GRADING & PAVING

NO STREET PARKING = [Red dashed line symbol]

NOTES:

Carl Bowers will only have 1 crew on site next week. They will be working on Water Main on 5th Street and Klein Street to start the week, then will finish the last Public lateral on Main Avenue. After that they will be working on Sanitary Sewer Main on 5th Street between Main Avenue and Hendricks Avenue.

Scott Lamers will be back on site next week, working on Private Sanitary Laterals and Water Services on 4th Street.

Once 4th Street Private Lateral work has been completed, asphalt pavement will be placed shortly after.
