
PROJECT 1-23 METOXEN, DIXON, QUINNEY & SEVENTH

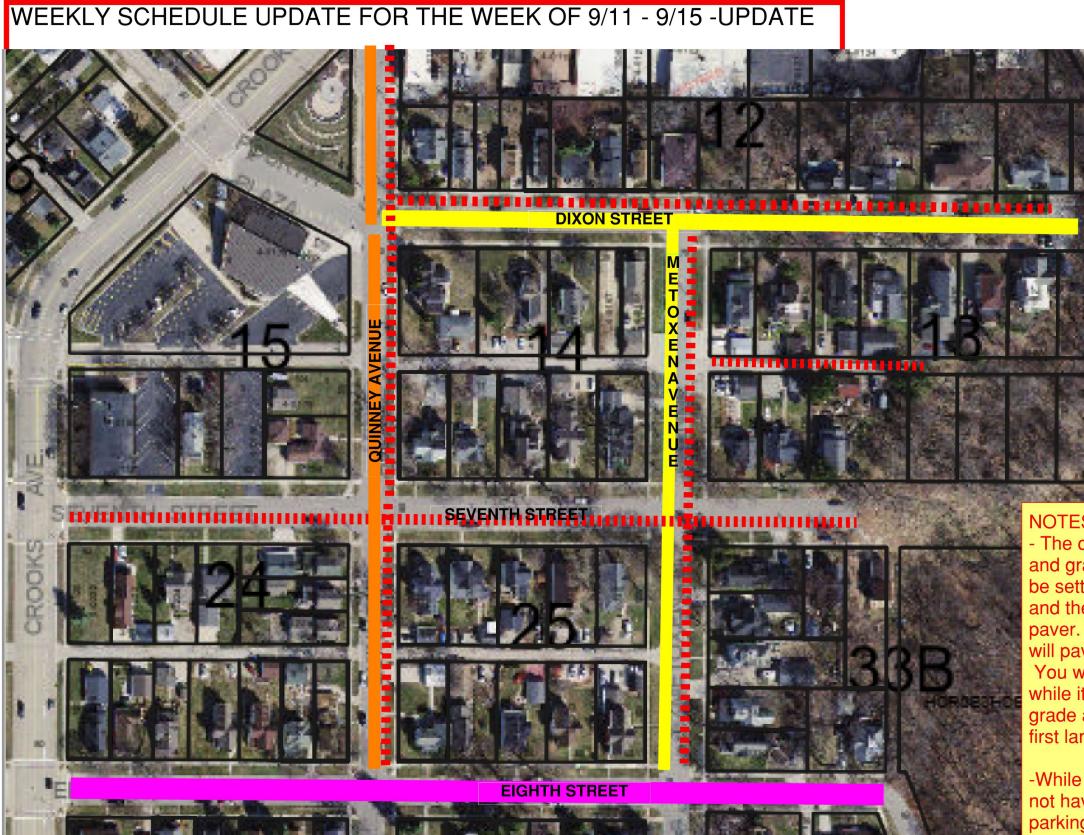

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

RECOMMENDED PARKING

TEMPORARY PARKING =

NOTES:

- The contractor the contractor will start start the the trimming and grading work on Dixon and Metoxen on Friday. They will be setting a string along Dixon along the south side of Dixon and the west side of Metoxen for the trimming machine and the paver. Later during the week of September 11, the contractor will pave the south side of Dixon and the west side of Metoxen. You will not be able to drive on the new concrete for 7 days while it is curing and strengthening. The contractor will trim, grade and pave the other lanes on Dixon and Metoxen once the first lanes are open for traffic.

-While this work is happening in front of your property you will not have access to your driveway. Please find an alternate parking space while this work is happening.

PROJECT 1-23 WHITE DOVE, WHITE BIRCH, LODERBAUER





*PLEASE NOTE THAT THIS
WORK AND SCHEDULE CAN
CHANGE DUE TO WEATHER OR
UNFORESEEN CONSTRUCTION
DELAYS. THESE UPDATES ARE
TO AID THE COMMUNICATION
PROCESS AS WE ALL WORK
TOGETHER TO COMPLETE THIS
PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

ASPHALT PAVING

SIDEWALK/DRIVEWAY WORK

RECOMMENDED PARKING

TEMPORARY PARKING =

NOTES:

-Later during the week of September 11th, the contractor will be doing the landscape restoration work on White Dove, White Birch and Loderbauer. They will seed, mulch and place erosion mat in the terraces and behind the sidewalks. Once the landscaper is finished, you can replace your mailboxes.

PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 9/11 - 9/15 -UPDATE



*PLEASE NOTE THAT THIS
WORK AND SCHEDULE CAN
CHANGE DUE TO WEATHER OR
UNFORESEEN CONSTRUCTION
DELAYS. THESE UPDATES ARE
TO AID THE COMMUNICATION
PROCESS AS WE ALL WORK
TOGETHER TO COMPLETE THIS
PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

RECOMMENDED PARKING

NO PARKING = TEMPORARY PARKING =

NOTES:

- The week of September 11th, the contractor will be filling in the terrace (between the sidewalk and curb) on Greyhound, Setter and Boxer. Once the terraces are filled in and graded, the landscaper will place topsoil, grass seed, mulch and erosion mat later in the week. Once the landscaper is finished, you can replace your mailboxes.

PROJECT 1-23 OAK & SCHULTHEIS

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 9/11 - 9/15 -UPDATE



*PLEASE NOTE THAT THIS
WORK AND SCHEDULE CAN
CHANGE DUE TO WEATHER OR
UNFORESEEN CONSTRUCTION
DELAYS. THESE UPDATES ARE
TO AID THE COMMUNICATION
PROCESS AS WE ALL WORK
TOGETHER TO COMPLETE THIS
PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

RECOMMENDED PARKING


TEMPORARY PARKING =

NOTES:

- The contractor is planning to start excavating Oak Street and Schulthies Street the week of September 11th. Once the streets have been excavated, the contractor will be placing road stone in the excavation and grading the stone.
- -While this work is happening in front of your property you will not have access to your driveway. Please find alternate parking while this work is happening.

PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 9/11 - 9/15 -UPDATE

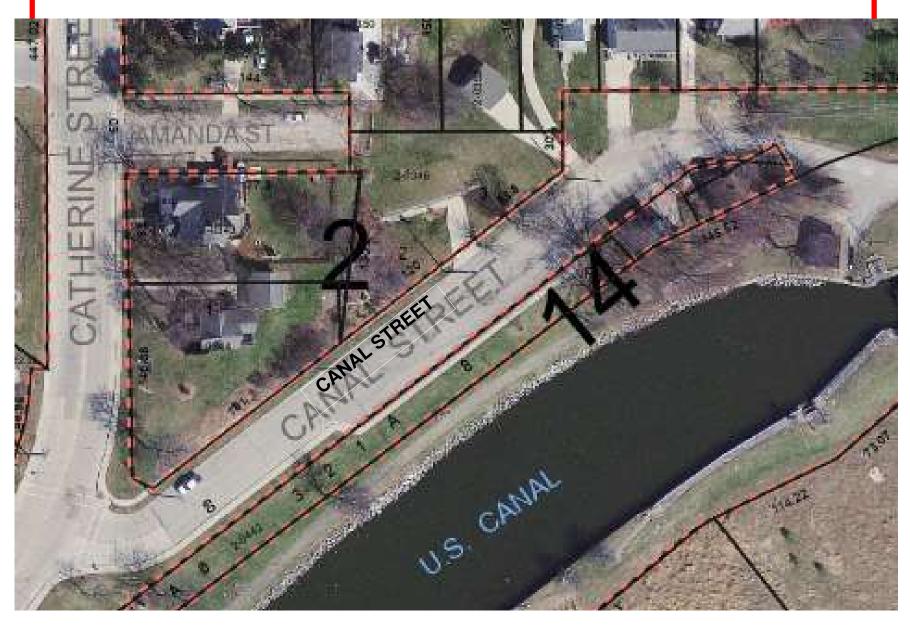

*PLEASE NOTE THAT THIS
WORK AND SCHEDULE CAN
CHANGE DUE TO WEATHER OR
UNFORESEEN CONSTRUCTION
DELAYS. THESE UPDATES ARE
TO AID THE COMMUNICATION
PROCESS AS WE ALL WORK
TOGETHER TO COMPLETE THIS
PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

RECOMMENDED PARKING

NO PARKING = TEMPORARY PARKING =

NOTES:

- The contractor has the excavation, stone placement and grading work scheduled to start the week of September 18th.
