


PROJECT 2-23 (KENNETH AVENUE & 4TH STREET AREA UTILITY RELAY)

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF SEPTEMBER 18 - 22

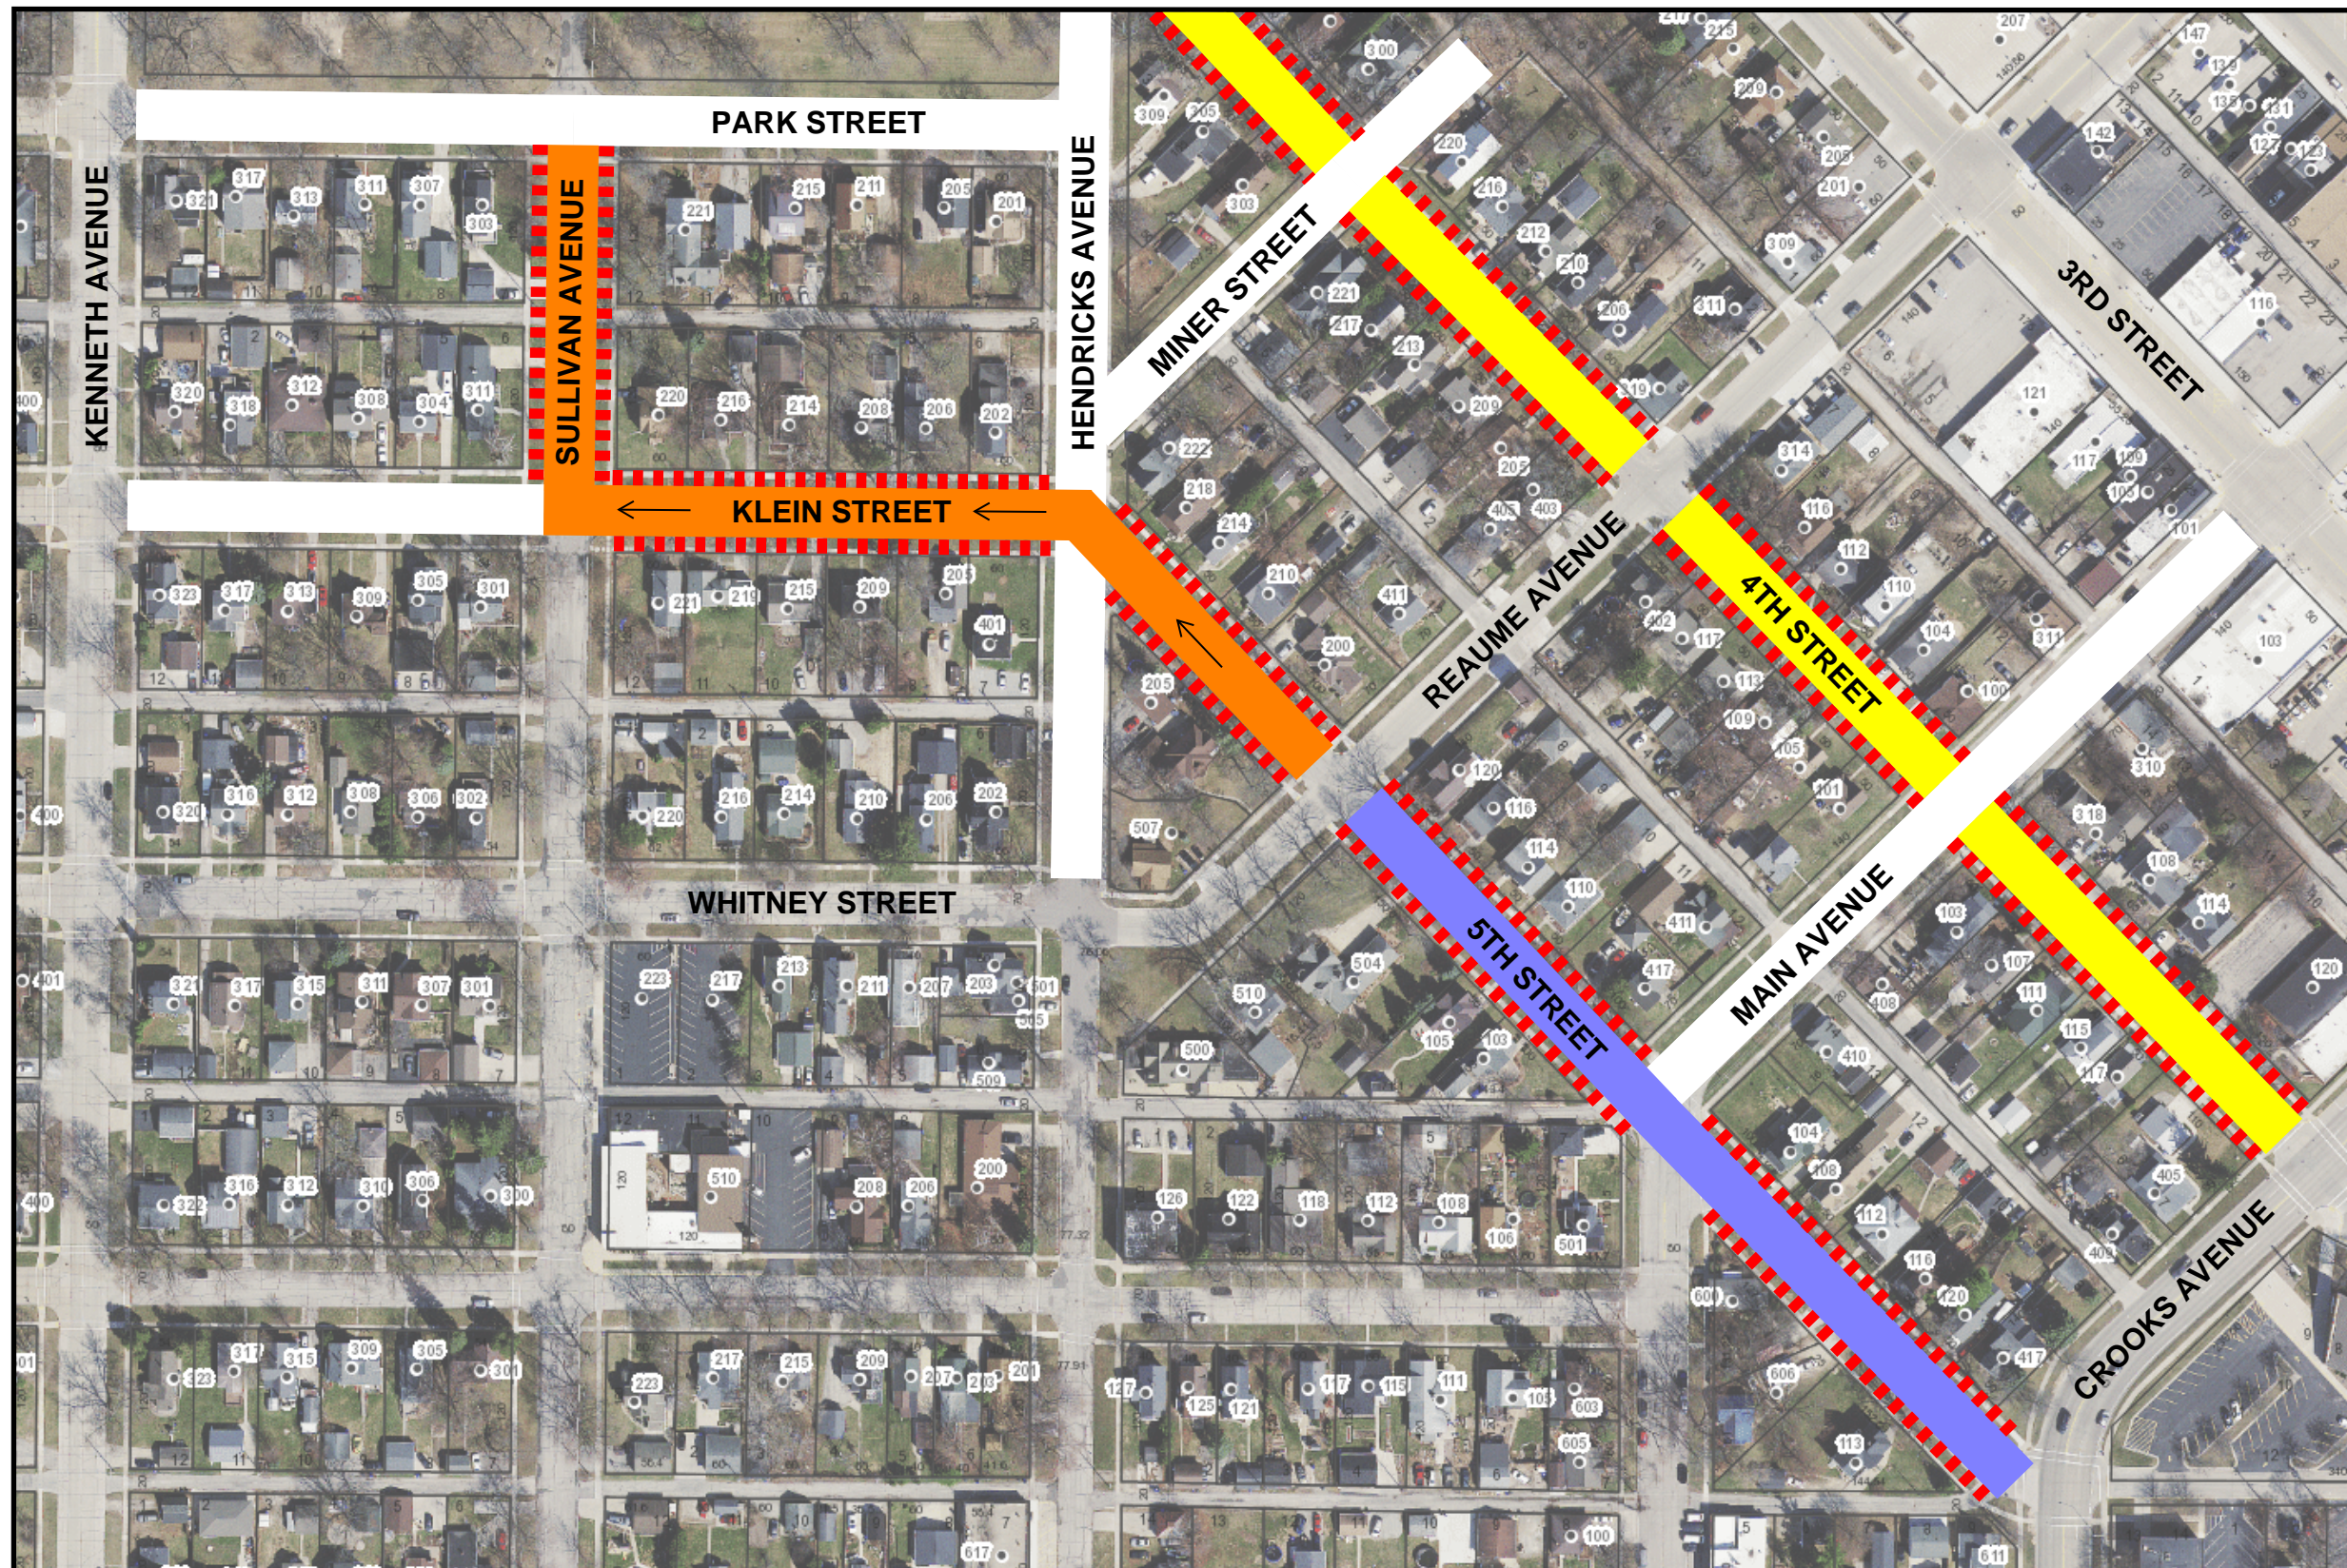

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- NO ACTIVE WORK
- SANITARY SEWER WORK
- WATER MAIN WORK
- PRIVATE LATERALS/SERVICES
- PUBLIC LATERALS/SERVICES
- RESTORATION
- GRADING & PAVING

NO STREET PARKING = [Red dashed line symbol]

NOTES:

Carl Bowers will be bringing the 2nd crew back to the job site next week. The Main crew will be working on the Sanitary Sewer Main on 5th Street, then on Klein, then up Sullivan. The 2nd crew will be working on Public Laterals & Services on 5th Street between Crooks and Reaume.

Scott Lamers will continue working on Private Laterals & Services on 4th Street.
