


PROJECT 2-23 (KENNETH AVENUE & 4TH STREET AREA UTILITY RELAY)

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF SEPTEMBER 25 - 29

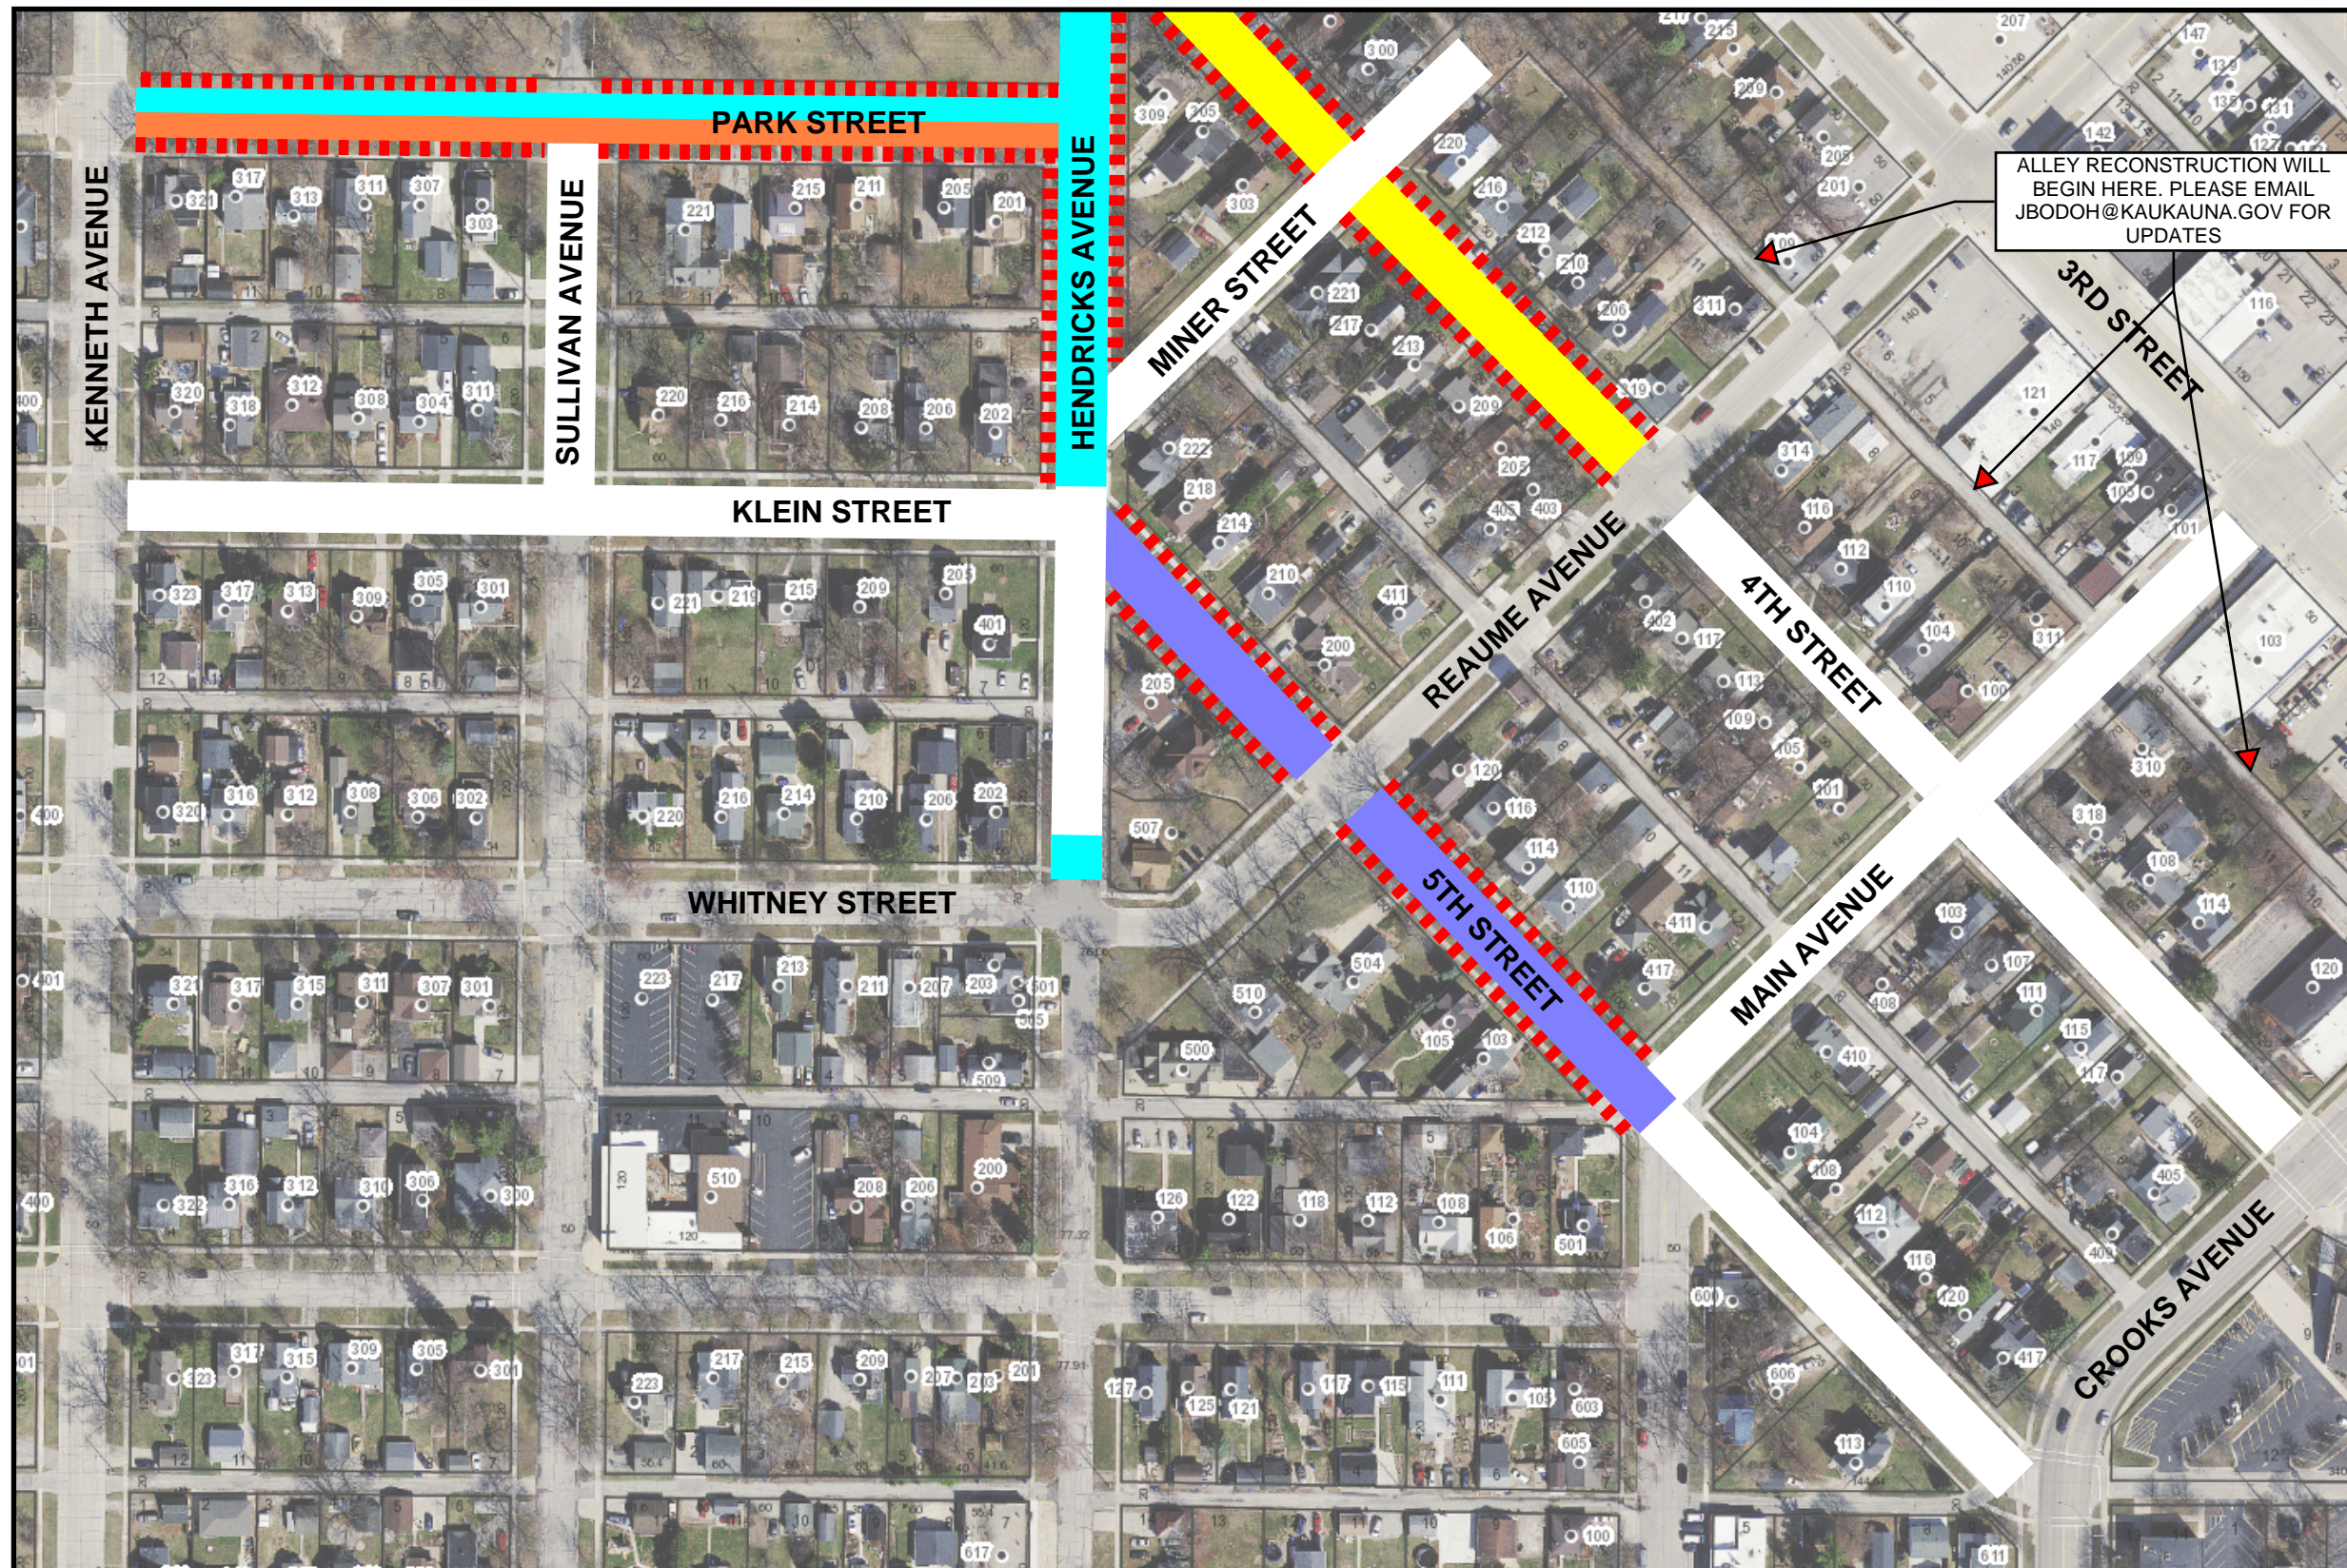

ALLEY RECONSTRUCTION WILL BEGIN HERE. PLEASE EMAIL JBODOH@KAUKAUNA.GOV FOR UPDATES

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- NO ACTIVE WORK
- SANITARY SEWER WORK
- WATER MAIN WORK
- PRIVATE LATERALS/SERVICES
- PUBLIC LATERALS/SERVICES
- RESTORATION
- GRADING & PAVING

NO STREET PARKING = [Red dashed line symbol]

NOTES:

Carl Bowers will have 2 crews on site. The Main Line Crew will be working on Water Main construction on Hendricks and Park Street to start the week, then will switch to Sanitary Sewer Relay work on Park Street after that. The 2nd Crew will continue to work on Public Laterals & Services on 5th Street. There may be additional Water Main work as needed in other locations.

Scott Lamers will continue working on Private Laterals & Services on 4th Street.

Northeast Asphalt will be on site FRIDAY to begin removing extra asphalt on 4th Street, Main Avenue, and a portion of 5th Street. This work will limit road parking so please park in your driveways on Friday if you live on 4th, 5th, and Main.
