


PROJECT 2-23 (KENNETH AVENUE & 4TH STREET AREA UTILITY RELAY)

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF SEPTEMBER 4 - 8

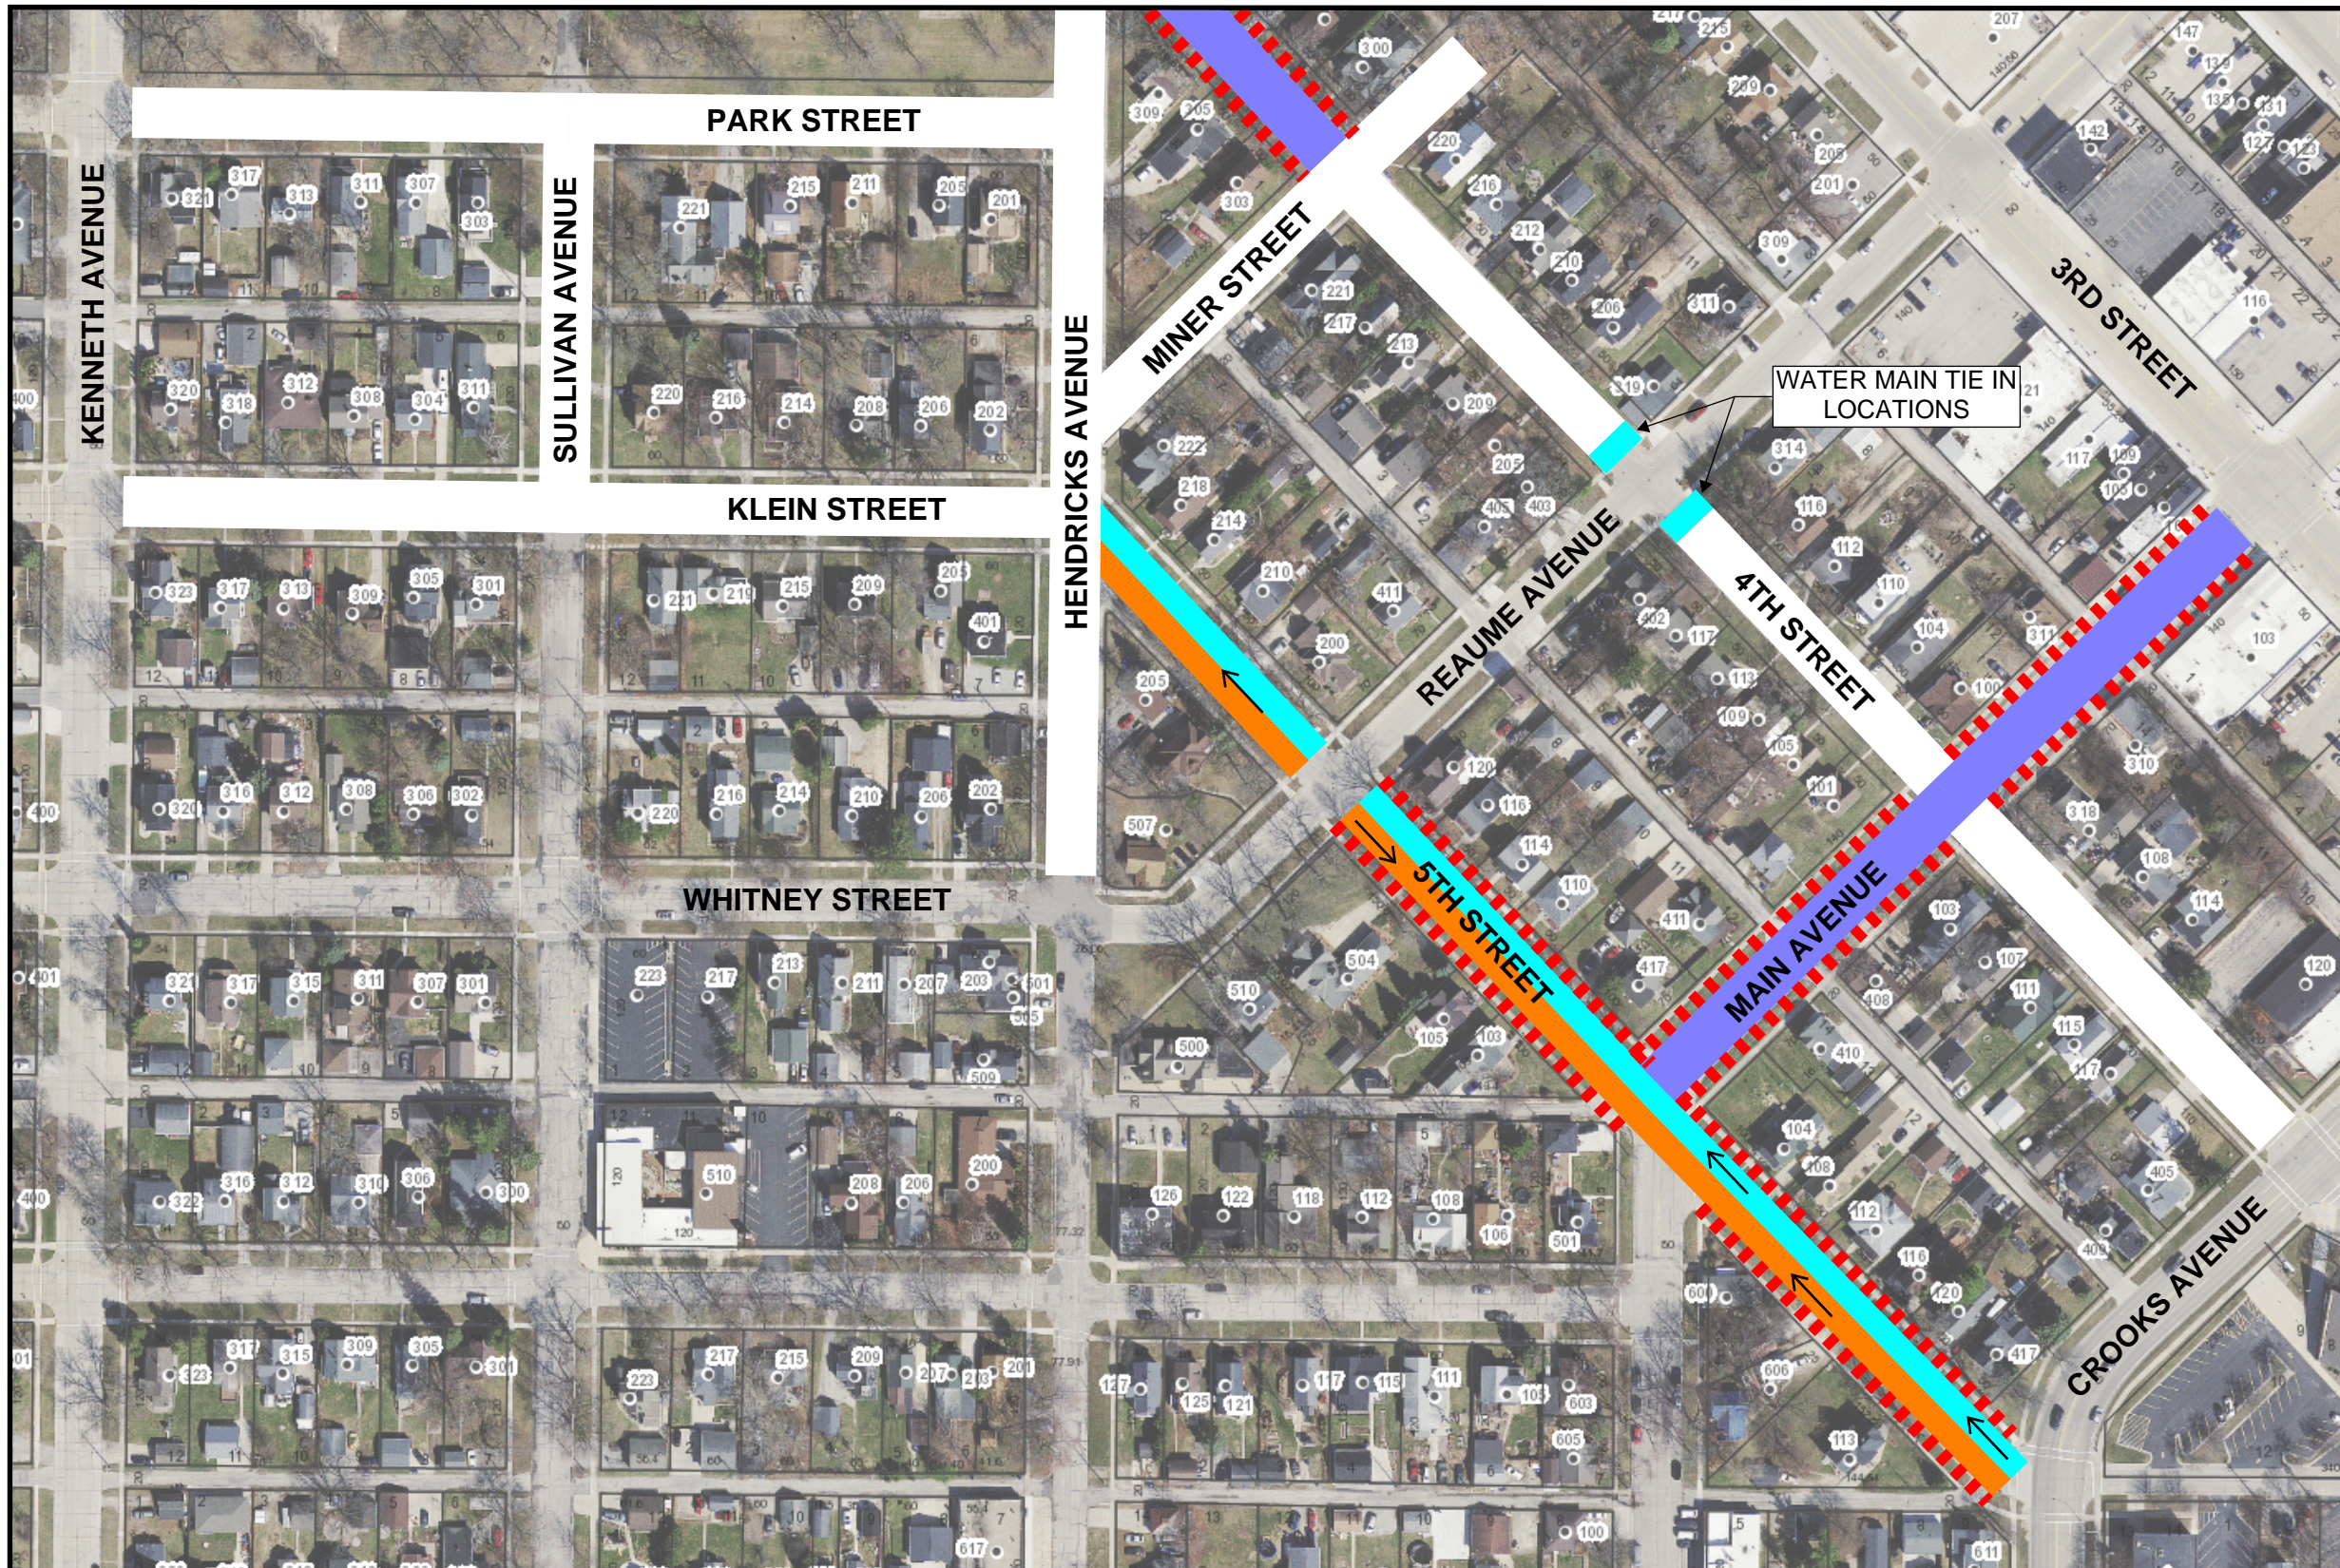

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- NO ACTIVE WORK
- SANITARY SEWER WORK
- WATER MAIN WORK
- PRIVATE LATERALS/SERVICES
- PUBLIC LATERALS/SERVICES
- RESTORATION
- GRADING & PAVING

NO STREET PARKING = [Red dashed line symbol]

NOTES:

Monday - No Work. Holiday.

Carl Bowers will have 2 crews on site next week. One crew is going to start the week by completing some final water main connections near the intersection of Reaume and 4th Street. Then they will be working on Water Main Construction and Sanitary Sewer Relay on 5th Street. They will do the water first, then the sewer. If both get completed between Crooks and Main they will continue with Water Main Construction west of Main Avenue. The second crew will continue working on public laterals and services.

Scott Lamers will NOT be on site next week. When they do return they will be working on Private Laterals/Services on 4th Street. They should be reaching out to your shortly if they haven't already.
