




# PROJECT 1-23 METOXEN, DIXON, QUINNEY & SEVENTH

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 10/23 - 10/27 UPDATE

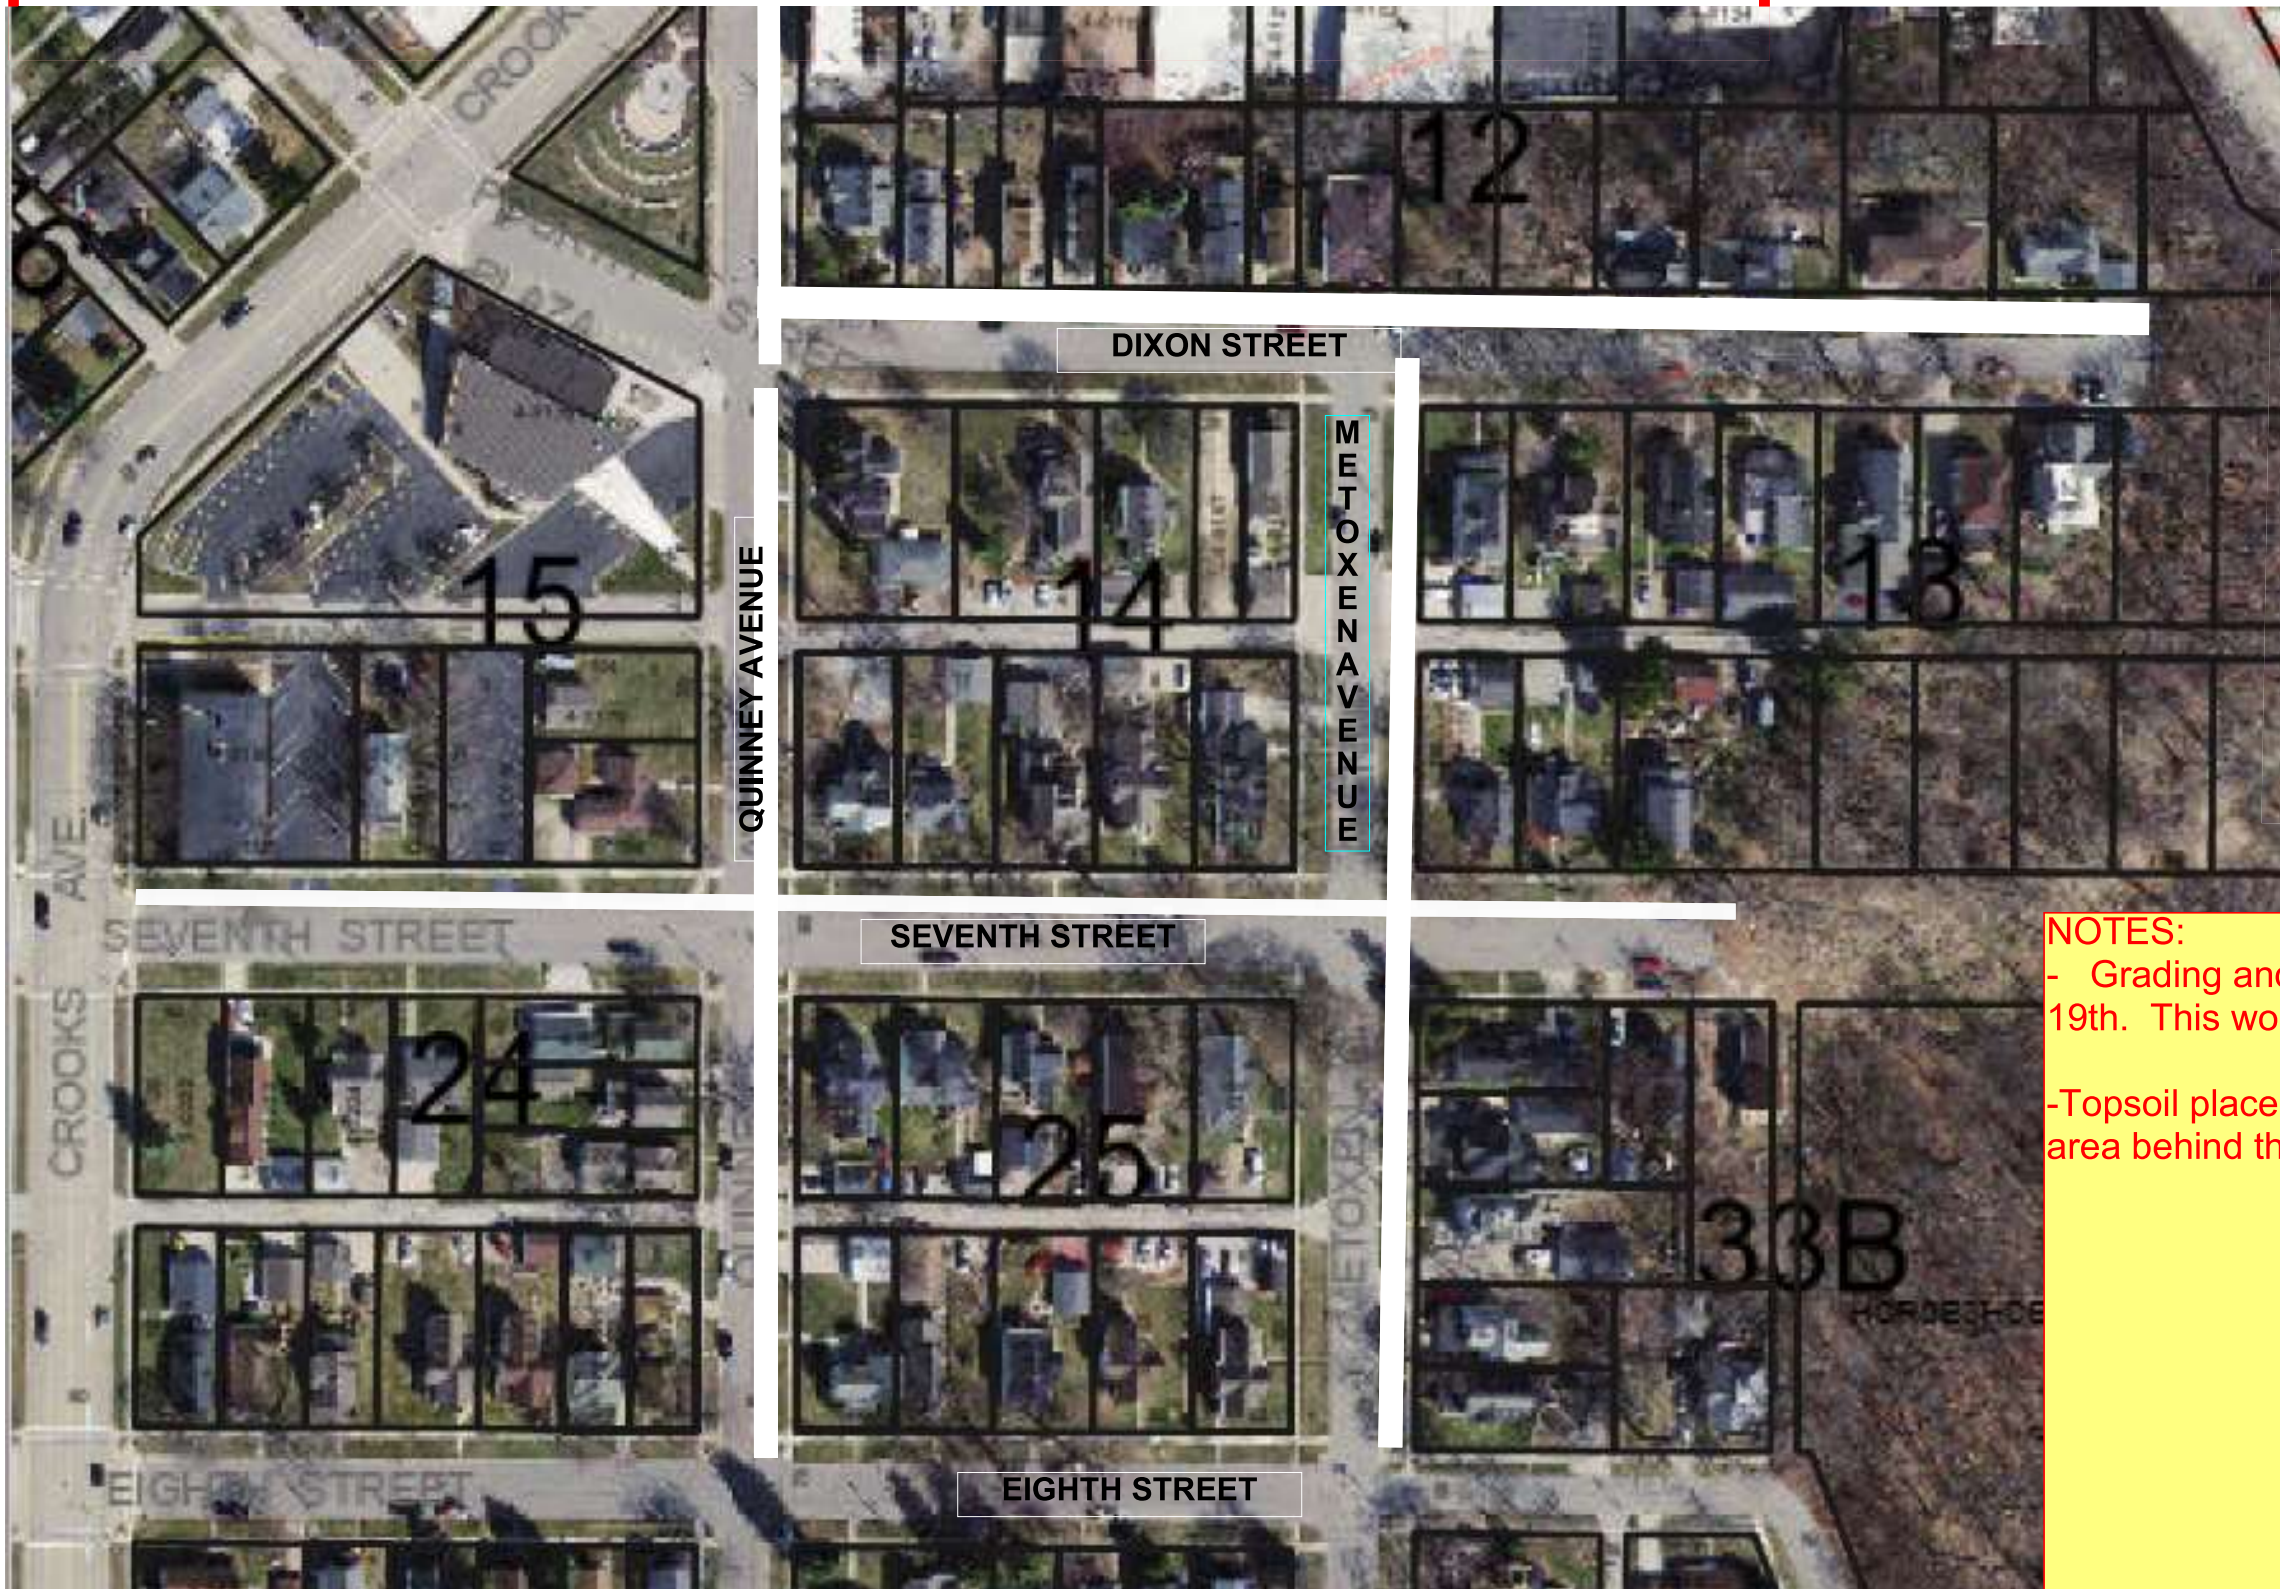

\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDEWALK/DRIVEWAY WORK
- RECOMMENDED PARKING
- NO PARKING = 
- TEMPORARY PARKING = 

**NOTES:**  
 - Grading and Backfilling behind the curb started on October 19th. This work will continue next week.  
 -Topsoil placement and landscaping should take place after the area behind the curb is backfilled and graded.

# PROJECT 1-23 WHITE DOVE, WHITE BIRCH, LODERBAUER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 10/23 - 10/27-UPDATE



\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- ASPHALT PAVING
- SIDEWALK/DRIVEWAY WORK
- RECOMMENDED PARKING
- NO PARKING = [Red dashed line]
- TEMPORARY PARKING = [Pink solid line]

**NOTES:**  
 -The landscaping is complete. Please water the new landscaping to help the grass grow. Mailboxes can be replaced. Please install your mailboxes according to the Post Office's mailbox requirements.

# PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 10/23 - 10/27 -UPDATE



\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

RECOMMENDED PARKING

NO PARKING =   
TEMPORARY PARKING = 

## NOTES:

- The landscaping in the terraces on Greyhound, Setter and Boxer is complete, except for one lot. Please water the new landscaping to help the grass grow. Mailboxes can be replaced. Please install your mailboxes according to the Post Office's mailbox requirements.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at [jbodoh@kaukauna-wi.org](mailto:jbodoh@kaukauna-wi.org) to be added to the weekly email update list.

# PROJECT 1-23 OAK & SCHULTHEIS

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 10/23 - 10/27-UPDATE



\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDEWALK/DRIVEWAY WORK
- RECOMMENDED PARKING

NO PARKING =   
TEMPORARY PARKING = 

**NOTES:**  
- The contractor will be paving the north lane of Oak and the east lane of Schulteis possibly later the week of October 23rd if weather allows. There will be a few hand pours after the lanes are poured.  
-While this work is happening in front of your property you will not have access to your driveway. Please find alternate parking while this work is taking place.  
-Sidewalk and driveway apron replacement should take place after the street is complete.

# PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 10/23 - 10/27 -UPDATE



\*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
  - STORM SEWER WORK
  - PAVMENT REMOVALS
  - GRADING
  - CONCRETE PAVING
  - SIDEWALK/DRIVEWAY WORK
  - RECOMMENDED PARKING
- NO PARKING = 
- TEMPORARY PARKING = 

## NOTES:

- The contractor has most of the street poured. They will be hand pouring the parking lanes later in the week of October 23rd if weather allows.
- Please stay off the new concrete for about 7 days while the concrete cures and strengthens. You may have to find alternative parking while this work takes place.
- The concrete contractor may start the driveway apron and sidewalk work the week of October 23rd.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at [jbodoh@kaukauna-wi.org](mailto:jbodoh@kaukauna-wi.org) to be added to the weekly email update list.
