


PROJECT 1-23 METOXEN, DIXON, QUINNEY & SEVENTH

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 10/9 - 10/13-UPDATE

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

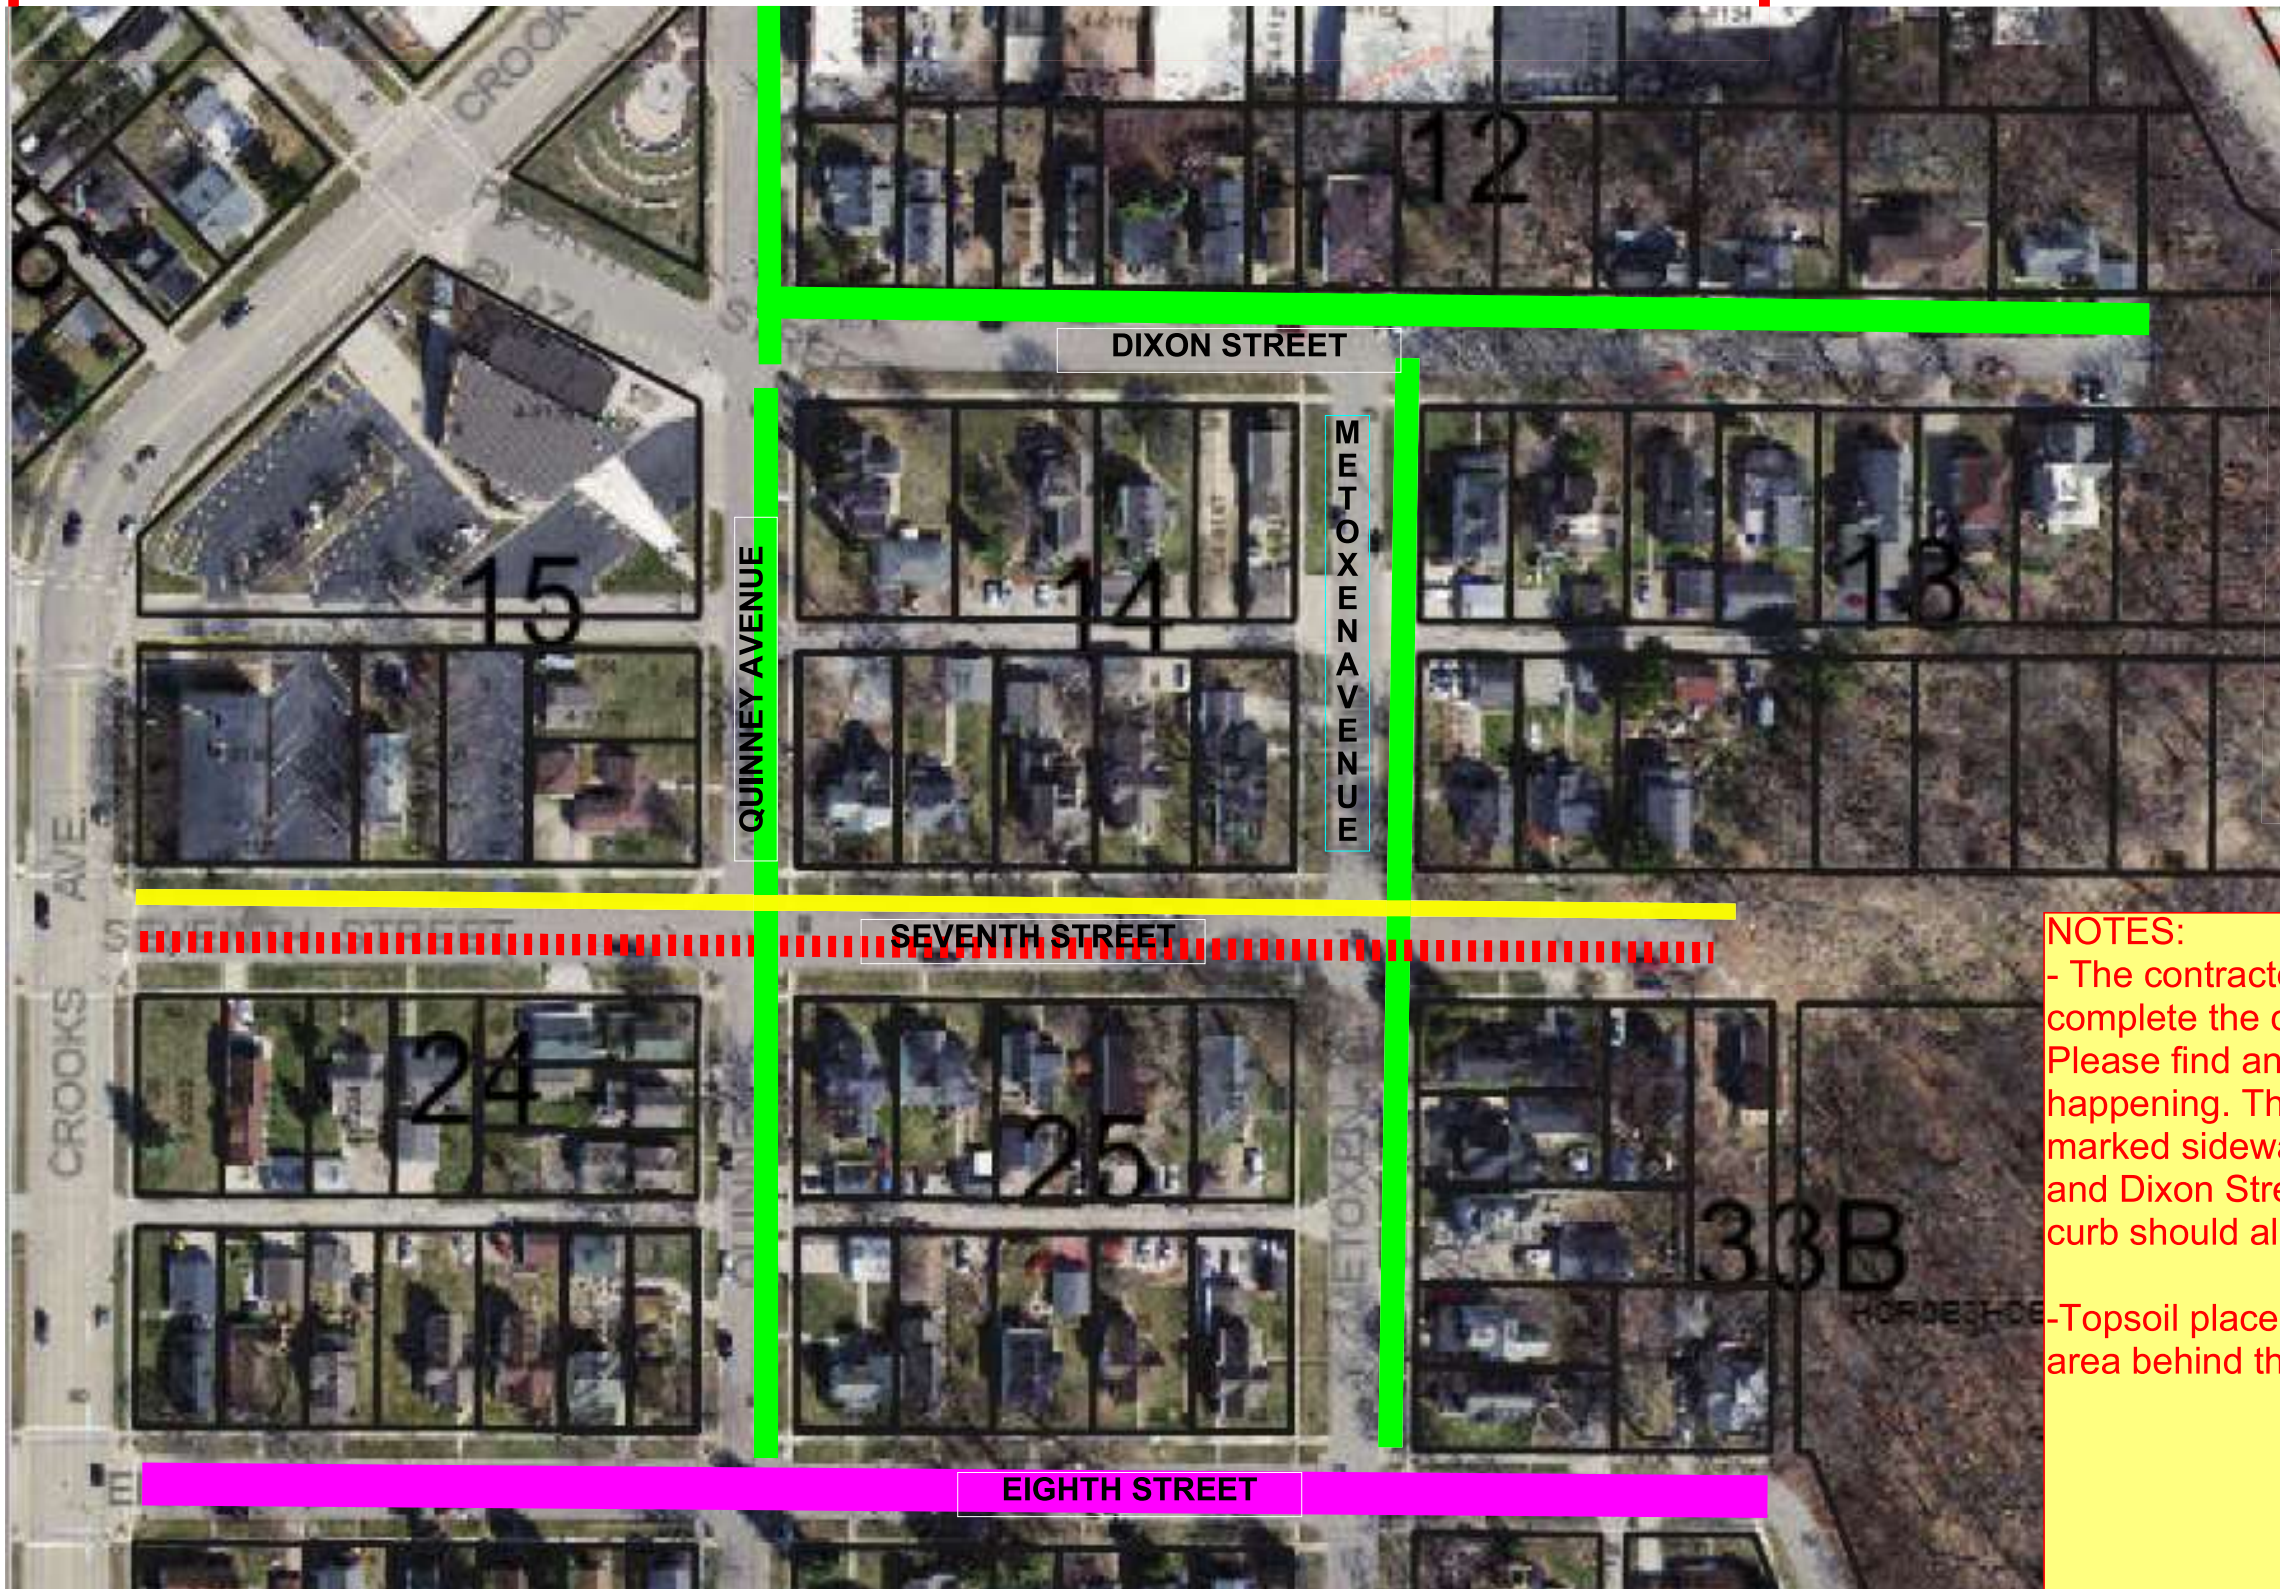

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDWALK/DRIVEWAY WORK
- RECOMMENDED PARKING
- NO PARKING = [Red dashed line]
- TEMPORARY PARKING = [Pink bar]

NOTES:
 - The contractor will be doing handpours along Seventh Street to complete the concrete street work the week of October 9th. Please find an alternate parking space while this work is happening. The sidewalk contractor will continue replacing the marked sidewalks along the Quinney Avenue, Metoxen Avenue and Dixon Street the week of October 9th. Backfilling behind the curb should also be taking place the week of October 9th.
 -Topsoil placement and landscaping should take place after the area behind the curb is backfilled.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 WHITE DOVE, WHITE BIRCH, LODERBAUER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 10/9 - 10/13-UPDATE

*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.



OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

ASPHALT PAVING

SIDEWALK/DRIVEWAY WORK

RECOMMENDED PARKING

NO PARKING = 

TEMPORARY PARKING = 

NOTES:

-The landscaping is complete. Please water the new landscaping to help the grass grow. Mailboxes can be replaced. Please install your mailboxes according to the Post Office's mailbox requirements.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 GREYHOUND, BOXER & SETTER

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 10/9 - 10/13 -UPDATE



*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

RECOMMENDED PARKING

NO PARKING = 
TEMPORARY PARKING = 

NOTES:

- The landscaping in the terraces on Greyhound, Setter and Boxer is complete, except for one lot. Please water the new landscaping to help the grass grow. Mailboxes can be replaced. Please install your mailboxes according to the Post Office's mailbox requirements.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 OAK & SCHULTHEIS

WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 10/9 - 10/13-UPDATE



*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

OPEN TO TRAFFIC

STORM SEWER WORK

PAVMENT REMOVALS

GRADING

CONCRETE PAVING

SIDEWALK/DRIVEWAY WORK

RECOMMENDED PARKING

NO PARKING = 

TEMPORARY PARKING = 


NOTES:

- The contractor will be doing the final grading on Oak and Schulteis the week of October 16th. Concrete paving should take place shortly after that.
- While this work is happening in front of your property you will not have access to your driveway. Please find alternate parking while this work is taking place.
- We will be working with both the Concrete Street contractor and Alley Contractor to make sure that parking is available.



Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.

PROJECT 1-23 GREYHOUND, BOXER & SETTER

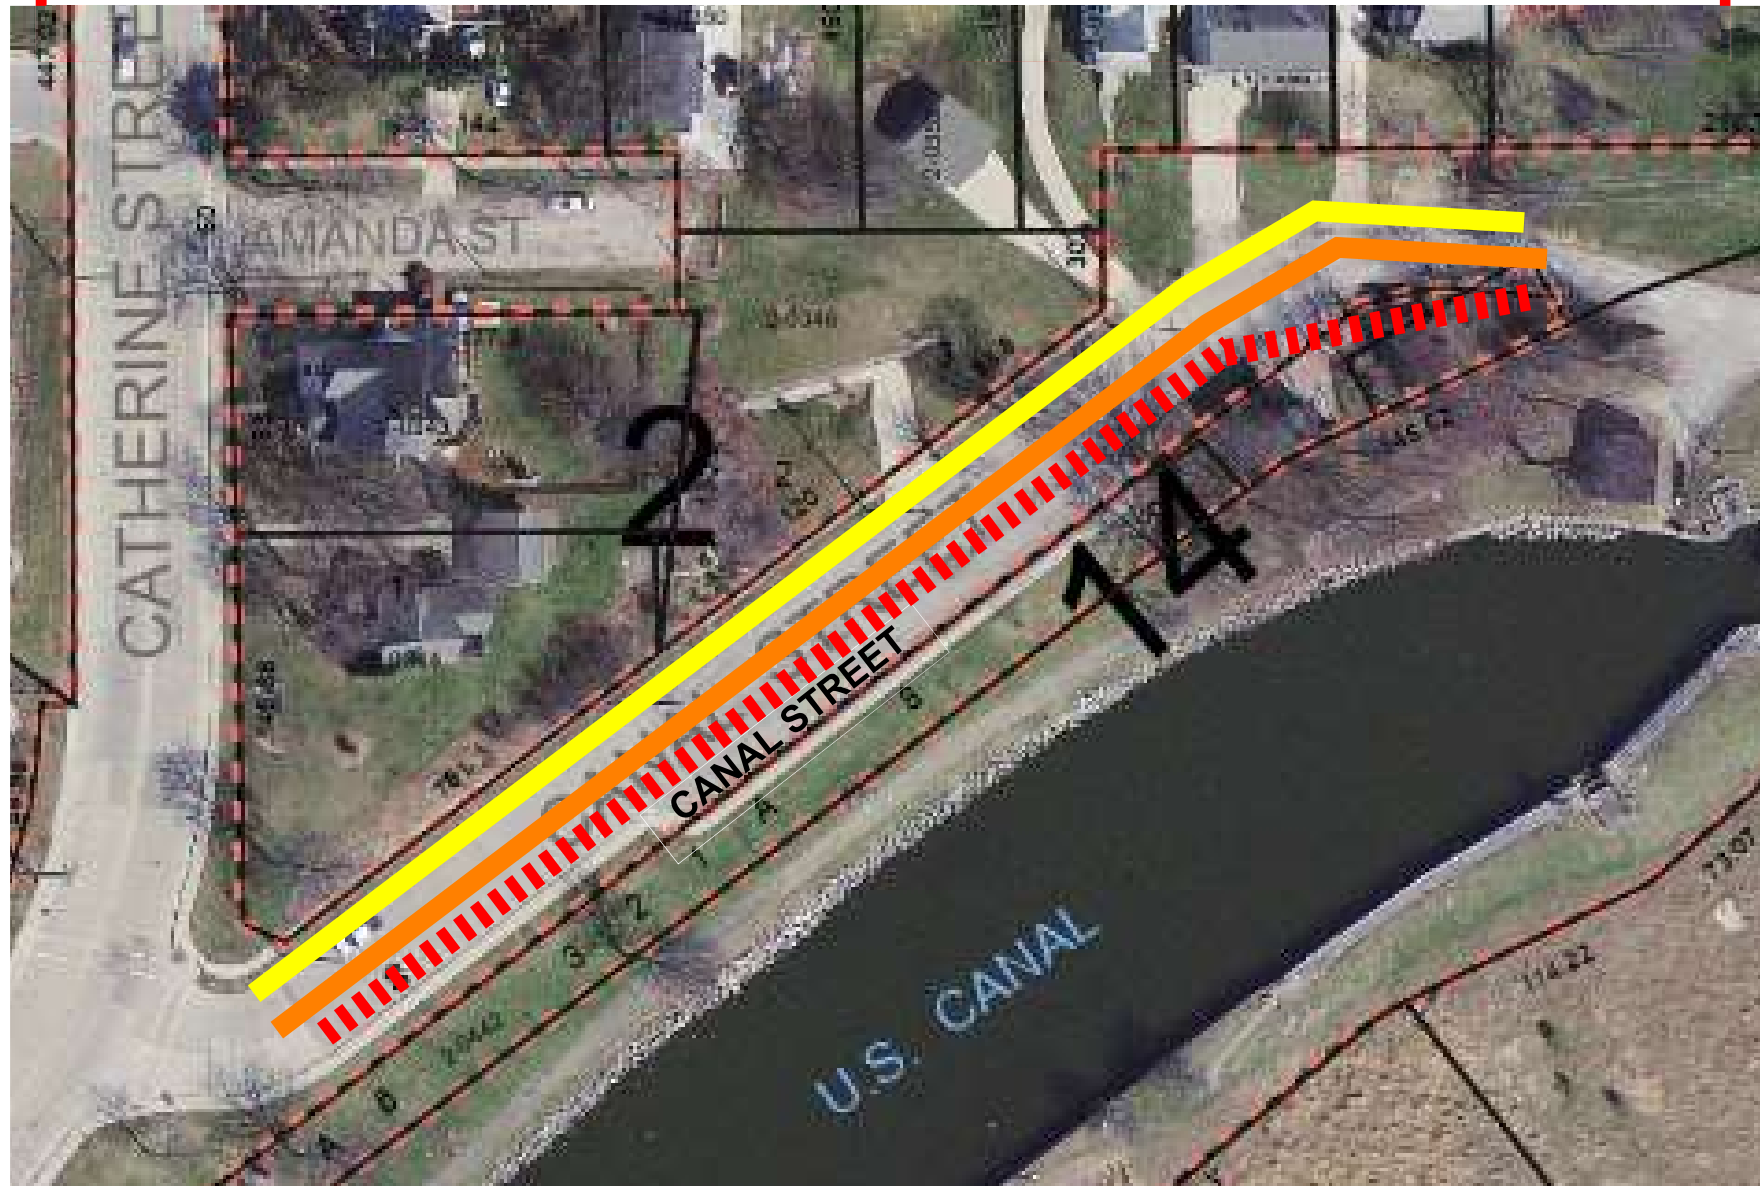WEEKLY SCHEDULE UPDATE FOR THE WEEK OF 10/9 - 10/13 -UPDATE



*PLEASE NOTE THAT THIS WORK AND SCHEDULE CAN CHANGE DUE TO WEATHER OR UNFORESEEN CONSTRUCTION DELAYS. THESE UPDATES ARE TO AID THE COMMUNICATION PROCESS AS WE ALL WORK TOGETHER TO COMPLETE THIS PROJECT.

- OPEN TO TRAFFIC
- STORM SEWER WORK
- PAVMENT REMOVALS
- GRADING
- CONCRETE PAVING
- SIDEWALK/DRIVEWAY WORK
- RECOMMENDED PARKING
- NO PARKING = 
- TEMPORARY PARKING = 

NOTES:

- The contractor will be paving Canal Street the week of October 9th. They will pave the south lane on Monday and the north lane would be paved later in the week. Please stay off the new concrete for about 7 days while the concrete cures and strengthens. You may have to find alternative parking while this work takes place.

Thank you for joining the weekly email list. Encourage your neighbors to email Jeff Bodoh at jbodoh@kaukauna-wi.org to be added to the weekly email update list.
